


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
May-23	564,000	550,907	281,748	269,159
Jun-23	422,000	414,035	207,507	206,528
Jul-23	351,000	239,451	127,232	112,219
Aug-23	303,000	352,751	170,780	181,971
Sep-23	431,000	226,645	110,485	116,160
Oct-23	674,000	582,309	277,729	304,580
Nov-23	796,000	809,264	396,263	413,001
Dec-23	820,000	637,044	312,365	324,679
Jan-24	931,000	604,549	291,738	312,811
Feb-24	737,000	0	0	0
Mar-24	777,000	0	0	0
Apr-24	722,000	0	0	0
May-24	564,000	0	0	0
Production 2024 (ytd) (kWh)	3,731,000	604,549	291,738	312,811
Total Production (LTM) (kWh)	7,528,000	3,866,048	1,894,099	1,971,949
Capacity Factor (LTM)	14.67%			

B. Site Energy Production Graph

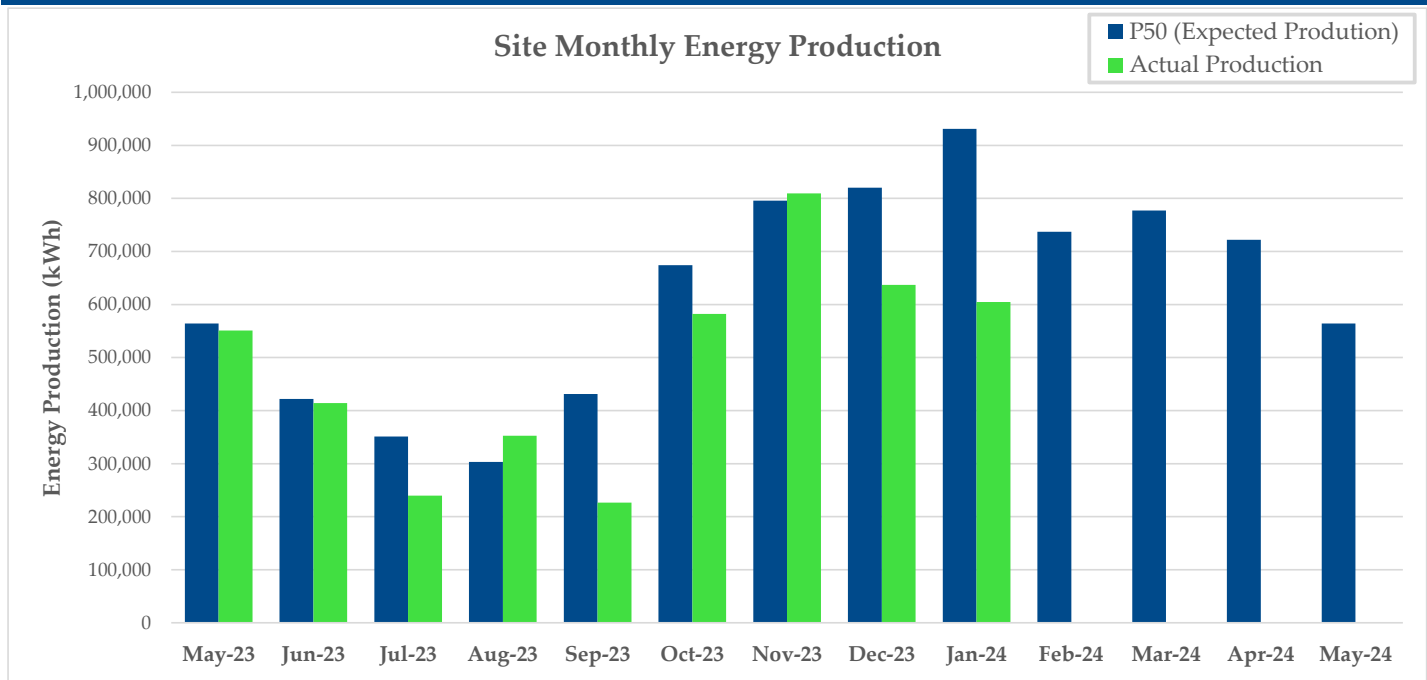

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
June-2024	5.5 Year Maintenance	~8	V1
June-2024	5.5 Year Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/1/2024-5/31/2024	Fleet Retrofit Pending	Unplanned	744.00	V1, V2 ³

F. Downtime¹

Downtime (hr)	This Month	Year To Date
V1	744.00	3169.71
V2	744.00	3132.45
Total	1488.00	6302.16

G. Billed Data

Meter Reading (Date/Time)	6/1/2024 12:00 AM
Meter To Date Produced	38,665,412 kWh
Meter To Date Consumed	109,471 kWh
Last Reading Produced	38,665,223 kWh
Last Reading Consumed	108,423 kWh
Billed kWh	PENDING kWh
Next Meter Reading	7/1/2024 12:00 AM

H. Report Notes and Comments

¹Turbine Availability/Downtime Pending.

²As a result of previously disclosed circumstances, the project has had no energy production since 01/22/2024.

³Investigation has transitioned to a Retrofit operation
