




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual YTD	WTG A	WTG B	WTG C
Apr-16	1,447,248	1,455,700	502,520	466,720	486,460
May-16	1,010,966	1,082,840	378,340	343,790	360,710
Jun-16	668,411	845,300	282,600	284,650	278,050
Jul-16	638,097	527,650	167,110	181,730	178,810
Aug-16	577,992	623,970	212,730	207,380	203,860
Sep-16	631,697	779,920	270,220	251,650	258,050
Oct-16	1,003,602	1,090,010	414,286	397,098	278,626
Nov-16	1,395,914	1,417,200	491,080	464,290	461,830
Dec-16	1,278,858	1,765,070	595,620	592,130	577,320
Jan-17	1,332,437	1,587,840	547,800	521,640	518,400
Feb-17	1,157,019	1,601,650	550,370	513,360	537,920
Mar-17	1,242,761	1,682,140	564,140	545,320	572,680
Apr-17	1,447,248	1,676,860	570,960	544,340	561,560
2017 Annual	12,384,999	6,548,490	2,233,270	2,124,660	2,190,560
Rolling 12 month Capacity Factor:					37.24%

B. Site Energy Production Graph

April-2017

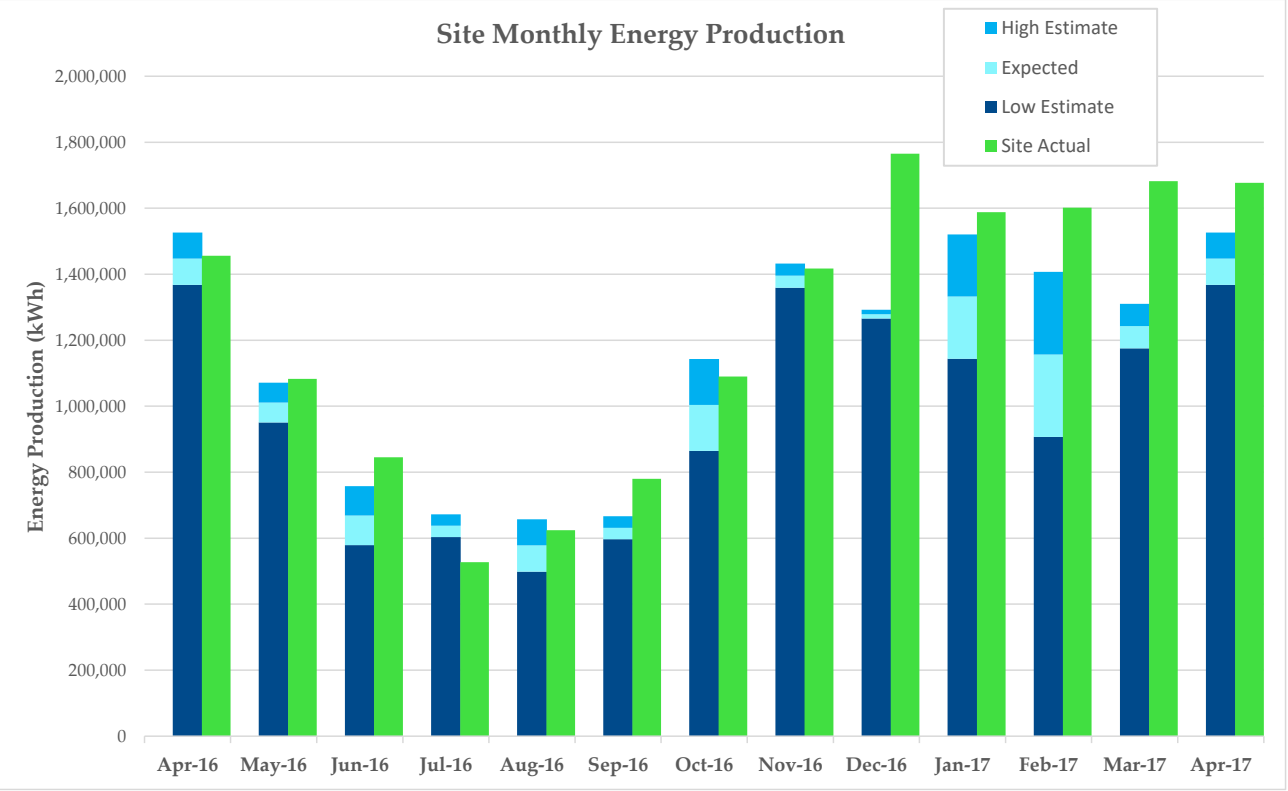

Monthly Report
April-2017



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s):	0	0
Near Miss(es):	0	0

D. Planned Maintenance Events

Date	Event	Duration (hrs)	Turbine
May-2017	Goldwind 5 year maintenance	~8	WTG A
May-2017	Goldwind 5 year maintenance	~8	WTG B
May-2017	Goldwind 5 year maintenance	~8	WTG C

E. Actual Maintenance Events - April 2017

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability (%)	This Month	2017 Annual
WTG A	99.96%	99.61%
WTG B	100.00%	99.59%
WTG C	99.89%	99.72%
Avg		99.64%

Downtime (hrs)	This Month	2017 Annual
WTG A	2.76	56.99
WTG B	1.67	29.03
WTG C	3.01	19.31
Total	7.44	105.33

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2017 Annual
WTG A	15.41	15.09
WTG B	15.19	14.78
WTG C	16.08	15.54
Estimated	16.62	13.39

Capacity Factor (%)	This Month	2017 Annual
WTG A	52.87%	51.70%
WTG B	50.40%	49.18%
WTG C	52.00%	50.71%
Low Estimate	42.22%	50.53%

H. Report Notes and Comments
