




A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Sep-16	348,000	315,178	158,922	156,256
Oct-16	653,000	602,755	311,561	291,194
Nov-16	851,000	803,588	410,578	393,010
Dec-16	1,029,000	1,040,001	516,469	523,532
Jan-17	872,000	875,991	434,082	441,909
Feb-17	914,000	919,768	449,933	469,835
Mar-17	808,000	874,319	455,715	418,604
Apr-17	955,000	865,246	435,360	429,886
May-17	607,000	792,979	401,772	391,207
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Production 2017 (ytd) (kWh)	5,718,000	5,991,235	3,012,929	2,978,306
Total Production (kWh)*	8,251,000	8,437,579	4,251,537	4,186,042
Capacity Factor*	32.11%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

September-2017

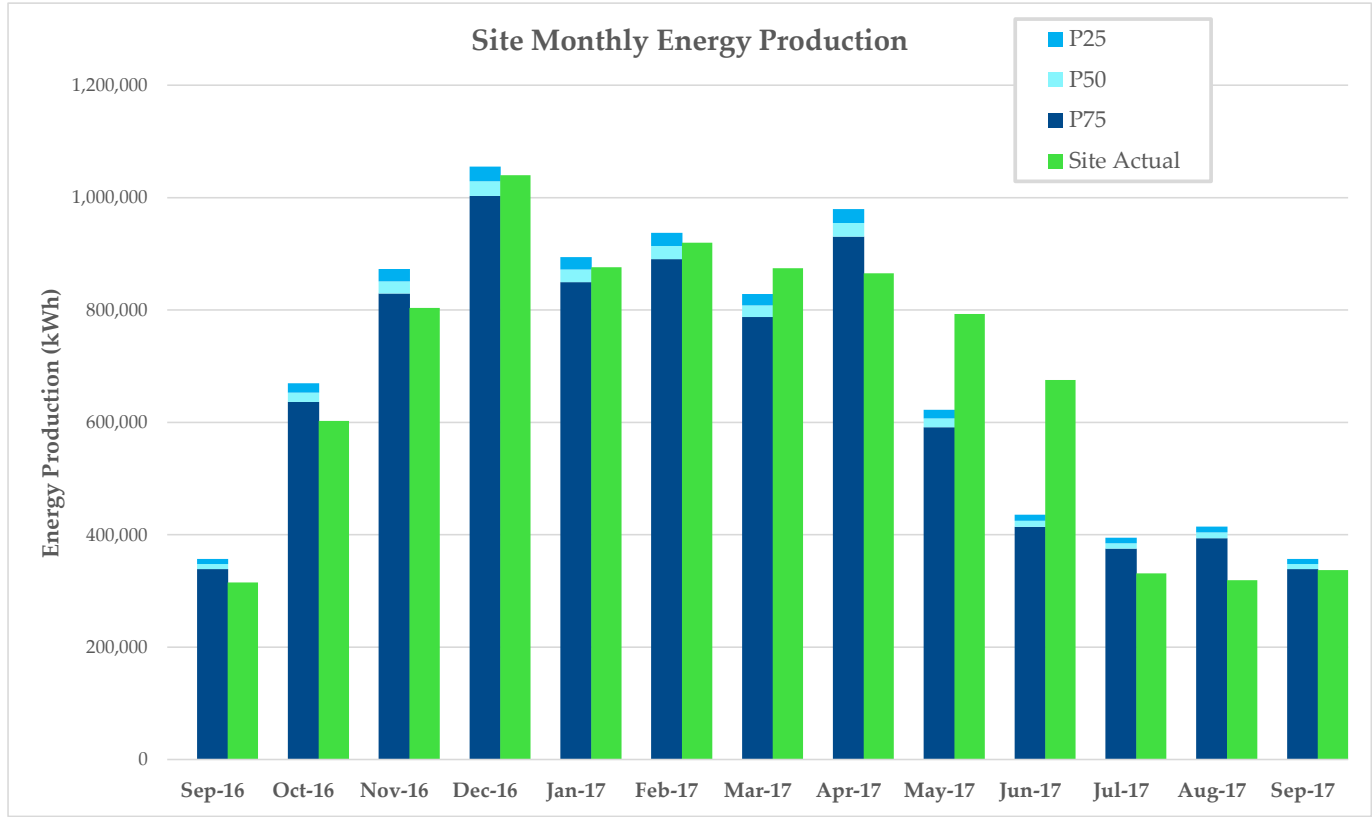

Monthly Report

September-2017



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
October-2017	Goldwind 1.5 Year Maintenance	~15	W1
October-2017	Goldwind 1.5 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
------	-------	-------------------	---------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	99.85%	99.11%
W2	100.00%	99.81%
Avg	99.93%	99.46%
Downtime (hr)	This Month	Annual To Date
W1	4.84	132.17
W2	3.93	71.97
Total	8.77	204.14

G. Billed Data

Meter Reading (Date/Time)	9/28/2017 12:00 AM
Meter To Date Produced	13,078,753 kWh
Meter To Date Consumed	26,961 kWh
Last Reading Produced	12,766,625 kWh
Last Reading Consumed	24,425 kWh
Billed kWh	309,592 kWh
Next Meter Reading	10/28/2017 12:00 AM

H. Report Notes and Comments

**Goldwind 1.5 year maintenance moved to October-2017
