




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG A	WTG B	WTG C
Oct-16	1,003,602	1,090,010	414,286	397,098	278,626
Nov-16	1,395,914	1,417,200	491,080	464,290	461,830
Dec-16	1,278,858	1,765,070	595,620	592,130	577,320
Jan-17	1,332,437	1,587,840	547,800	521,640	518,400
Feb-17	1,157,019	1,601,650	550,370	513,360	537,920
Mar-17	1,242,761	1,682,140	564,140	545,320	572,680
Apr-17	1,447,248	1,676,860	570,960	544,340	561,560
May-17	1,010,966	1,309,614	447,560	424,304	437,750
Jun-17	668,411	1,199,560	427,710	365,940	405,910
Jul-17	638,097	608,374	208,860	199,814	199,700
Aug-17	577,992	550,820	193,760	179,770	177,290
Sep-17	631,697	605,096	208,710	201,632	194,754
Oct-17	1,003,602	1,223,590	422,370	411,740	389,480
Production 2017 (ytd) (kWh)	9,710,228	12,045,544	4,142,240	3,907,860	3,995,444
Total Production (kWh)*	12,384,999	15,227,814	5,228,940	4,964,280	5,034,594
Capacity Factor*	38.63%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

October-2017

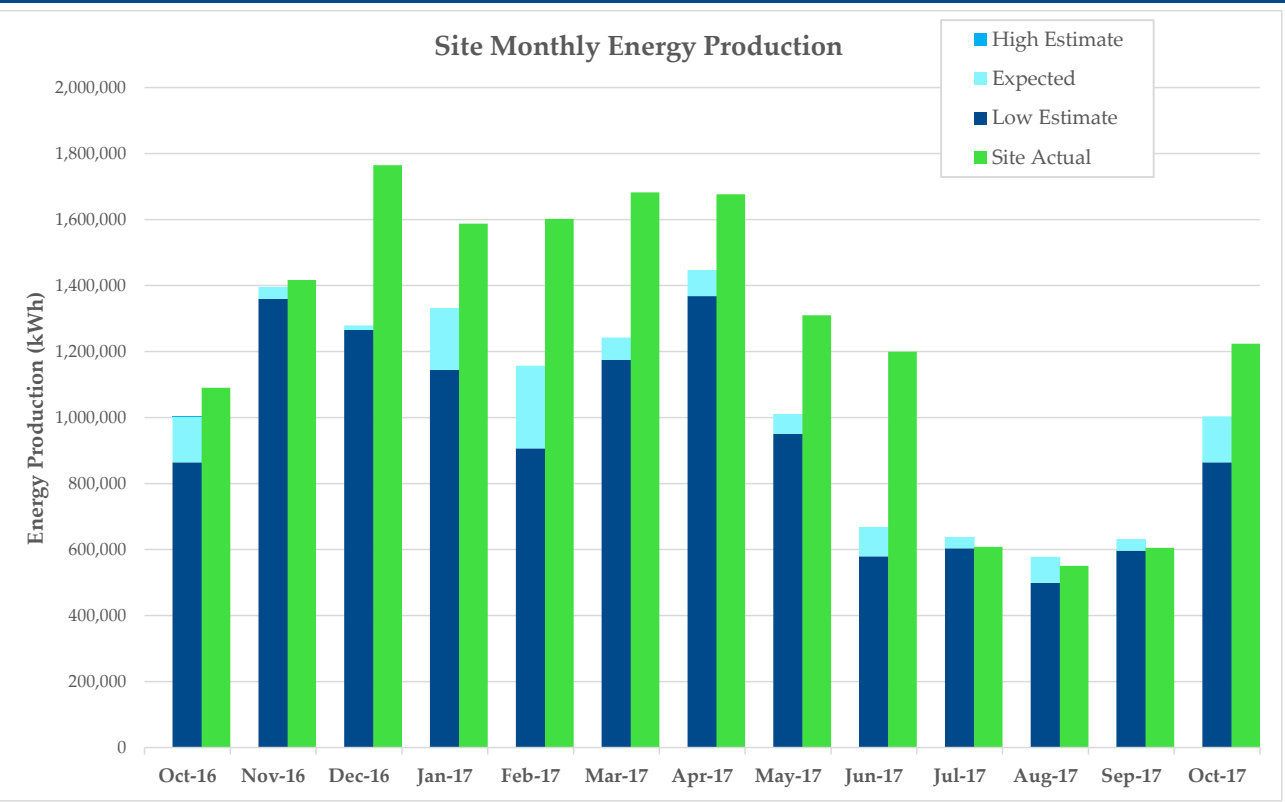

Monthly Report
October-2017



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2017	Goldwind 5.5 Year Maintenance	~8	WTG A
November-2017	Goldwind 5.5 Year Maintenance	~8	WTG B
November-2017	Goldwind 5.5 Year Maintenance	~8	WTG C

E. Actual Maintenance Events - October 2017

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
10/9-10/10/2017	Leading Edge/Blade Repair	Unplanned	22.70	WTG A
10/11-10/13/2017	Gen Side Capacitor Fuse Replaced	Unplanned	50.56	WTG B
10/12-10/13/2017	Leading Edge/Blade Repair, WTG B Repair	Unplanned	23.64	WTG A
10/14/2017	Leading Edge/Blade Repair	Unplanned	10.68	WTG C
10/16-10/17/2017	Hydraulic Motor Feedback Loss Error	Unplanned	12.86	WTG A
10/16-10/18/2017	Leading Edge/Blade Repair	Unplanned	24.67	WTG C
10/19/2017	Leading Edge/Blade Repair	Unplanned	12.12	WTG B
10/21/2017	Leading Edge/Blade Repair	Unplanned	11.25	WTG B
10/21/2017	Stiffener Retrofit	Unplanned	5.52, 4.19	WTG A, C
10/22-10/23/2017	Pitch Inverter Error (No work Sunday)	Unplanned	24.07	WTG A
10/23/2017	Leading Edge/Blade Repair	Unplanned	6.66	WTG A

F. Turbine Availability & Downtime

Availability (%)	This Month	Year to Date
WTG A	96.06%	99.15%
WTG B	93.20%	98.97%
WTG C	97.33%	99.16%
Avg	95.53%	99.09%

Downtime (hr)	This Month	Year to Date
WTG A	73.48	244.69
WTG B	76.23	251.31
WTG C	65.70	217.39
Total	215.41	713.39

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2017 Annual
WTG A	12.78	12.88
WTG B	12.94	12.77
WTG C	13.50	13.34
Estimated	13.89	13.39

Capacity Factor (%)	This Month	2017 Annual
WTG A	37.85%	38.23%
WTG B	36.89%	36.06%
WTG C	34.90%	36.87%
Low Estimate	25.82%	37.05%

H. Report Notes and Comments
