




A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Oct-16	653,000	602,755	311,561	291,194
Nov-16	851,000	803,588	410,578	393,010
Dec-16	1,029,000	1,040,001	516,469	523,532
Jan-17	872,000	875,991	434,082	441,909
Feb-17	914,000	919,768	449,933	469,835
Mar-17	808,000	874,319	455,715	418,604
Apr-17	955,000	865,246	435,360	429,886
May-17	607,000	792,979	401,772	391,207
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Oct-17	653,000	711,340	360,752	350,588
Production 2017 (ytd) (kWh)	6,371,000	6,702,575	3,373,681	3,328,894
Total Production (kWh)*	8,251,000	8,546,164	4,300,728	4,245,436
Capacity Factor*	32.52%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

October-2017

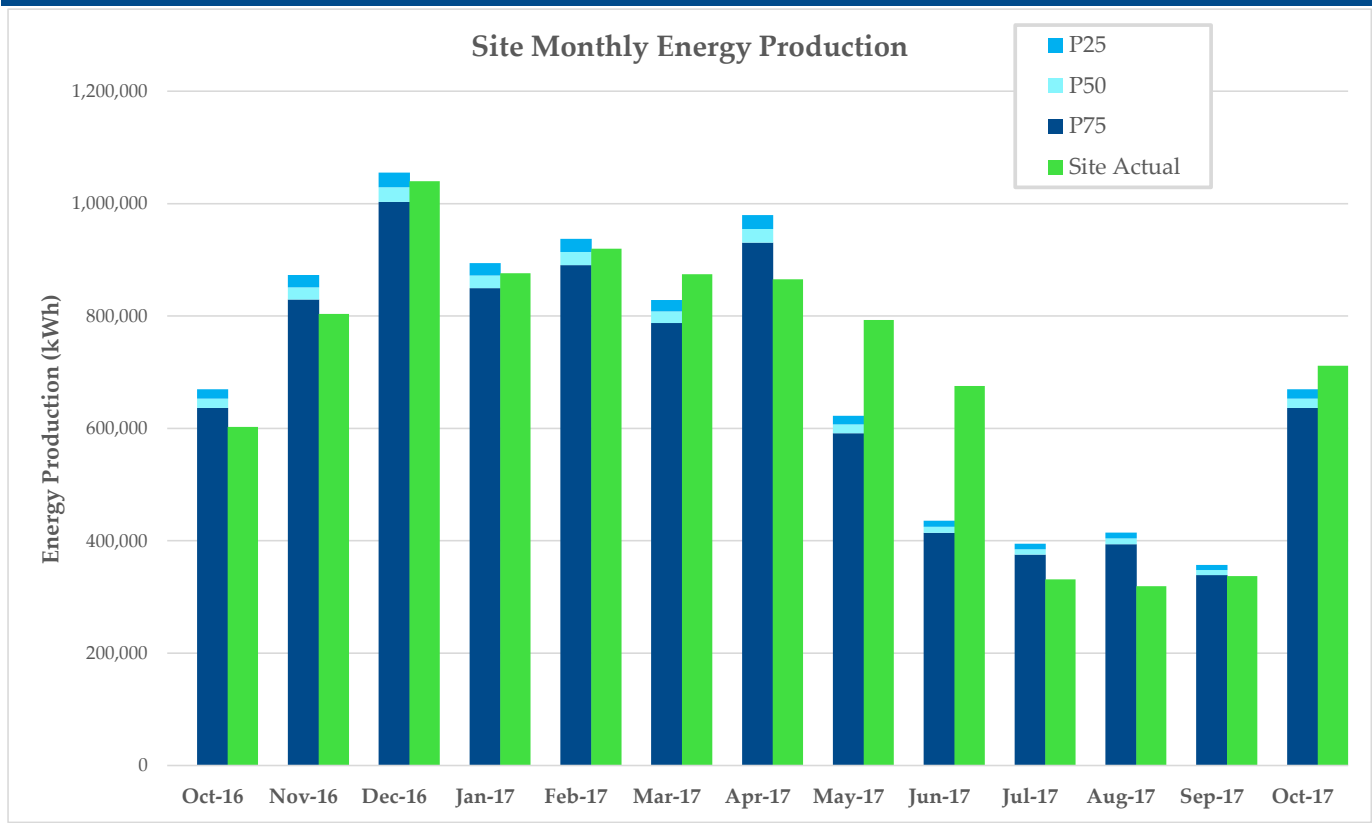

Monthly Report

October-2017



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
November-2017	Goldwind 1.5 Year Maintenance	~15	W1
November-2017	Goldwind 1.5 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
------	-------	-------------------	---------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	99.98%	99.20%
W2	99.96%	99.82%
Avg	99.97%	99.51%
Downtime (hr)	This Month	Annual To Date
W1	2.20	134.37
W2	2.33	74.3
Total	4.53	208.67

G. Billed Data

Meter Reading (Date/Time)	10/28/2017 12:00 AM
Meter To Date Produced	13,714,071 kWh
Meter To Date Consumed	27,880 kWh
Last Reading Produced	13,078,753 kWh
Last Reading Consumed	26,961 kWh
Billed kWh	634,400 kWh
Next Meter Reading	11/28/2017 12:00 AM

H. Report Notes and Comments

**Goldwind 1.5 year maintenance moved to November-2017
