




A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jan-17	872,000	875,991	434,082	441,909
Feb-17	914,000	919,768	449,933	469,835
Mar-17	808,000	874,319	455,715	418,604
Apr-17	955,000	865,246	435,360	429,886
May-17	607,000	792,979	401,772	391,207
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Oct-17	653,000	711,340	360,752	350,588
Nov-17	851,000	787,741	386,194	401,547
Dec-17	1,029,000	866,109	435,332	430,777
Jan-18	872,000	1,041,086	531,433	509,653
Production 2018 (ytd) (kWh)	872,000	1,041,086	531,433	509,653
Total Production (kWh)*	8,251,000	8,521,520	4,292,558	4,228,962
Capacity Factor*	32.43%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

January-2018

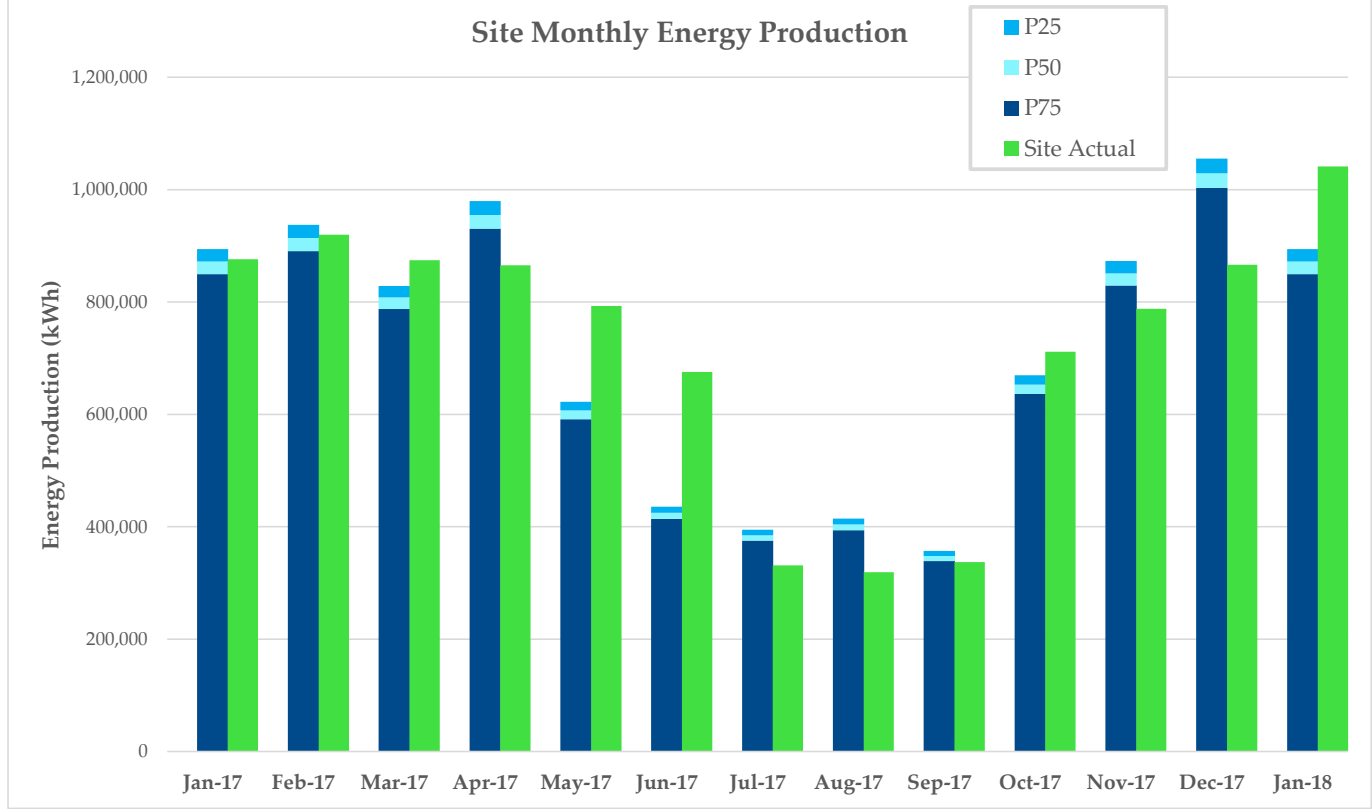

Monthly Report

January-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2018	Goldwind 2 Year Maintenance	~15	W1
May-2018	Goldwind 2 Year Maintenance	~15	W2
May-2018	Goldwind 2 Year Maintenance	~15	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
1/8/2018	Icing Event	Unplanned	11.54	W1
1/8/2018	Icing Event	Unplanned	11.51	W2
1/24-1/25/2018	Icing Event	Unplanned	18.46	W1
1/24-1/25/2018	Icing Event	Unplanned	18.17	W2

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	100.00%	100.00%
W2	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Annual To Date
W1	30.00	30.00
W2	29.68	29.68
Total	59.68	59.68

G. Billed Data

Meter Reading (Date/Time)	1/28/2018 12:00 AM
Meter To Date Produced	16,411,184 kWh
Meter To Date Consumed	31,090 kWh
Last Reading Produced	15,404,558 kWh
Last Reading Consumed	29,910 kWh
Billed kWh	1,005,446 kWh
Next Meter Reading	2/28/2018 12:00 AM

H. Report Notes and Comments
