


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Feb-17	914,000	919,768	449,933	469,835
Mar-17	808,000	874,319	455,715	418,604
Apr-17	955,000	865,246	435,360	429,886
May-17	607,000	792,979	401,772	391,207
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Oct-17	653,000	711,340	360,752	350,588
Nov-17	851,000	787,741	386,194	401,547
Dec-17	1,029,000	866,109	435,332	430,777
Jan-18	872,000	1,041,086	531,433	509,653
Feb-18	914,000	718,724	362,629	356,095
Production 2018 (ytd) (kWh)	1,786,000	1,759,810	894,062	865,748
Total Production (kWh)*	8,251,000	8,320,476	4,205,254	4,115,222
Capacity Factor*	31.66%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

February-2018

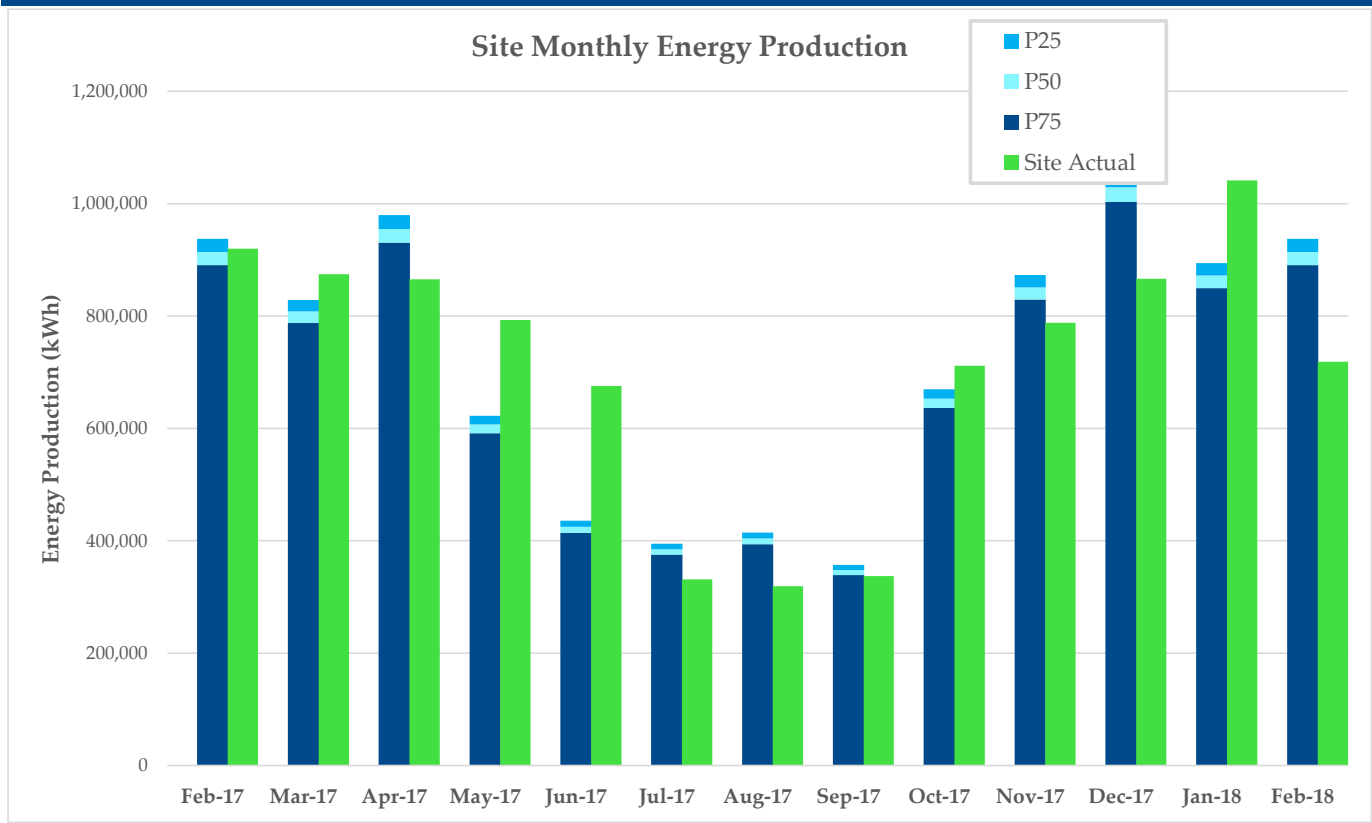

Monthly Report

February-2018

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2018	Goldwind 2 Year Maintenance	~15	W1
May-2018	Goldwind 2 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
2/4-2/5/2018	Icing Event	Unplanned	23.55	W1, W2
2/22/2018	Icing Event	Unplanned	5.76	W1, W2
2/25/2018	Icing Event	Unplanned	4.97	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	99.62%	99.82%
W2	100.00%	100.00%
Avg	99.81%	99.91%
Downtime (hr)	This Month	Annual To Date
W1	40.71	70.71
W2	38.33	68.01
Total	79.04	138.72

G. Billed Data

Meter Reading (Date/Time)	2/28/2018 12:00 AM
Meter To Date Produced	17,174,446 kWh
Meter To Date Consumed	32,691 kWh
Last Reading Produced	16,411,184 kWh
Last Reading Consumed	31,090 kWh
Billed kWh	761,662 kWh
Next Meter Reading	3/28/2018 12:00 AM

H. Report Notes and Comments
