


A. Site Energy Production Summary**

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Jan-18	450,000	146,791
Feb-18	473,000	335,605
Mar-18	417,000	-
Apr-18	494,000	-
May-18	315,000	-
Jun-18	220,000	-
Jul-18	199,000	-
Aug-18	209,000	-
Sep-18	180,000	-
Oct-18	337,000	-
Nov-18	440,000	-
Dec-18	532,000	-
Jan-19	450,000	-
Production 2018 (ytd) (kWh)	923,000	482,396
Total Production (kWh)*	-	-
Capacity Factor*	-	

*Value calculated over the last 12 months

B. Site Energy Production Graph

February-2018

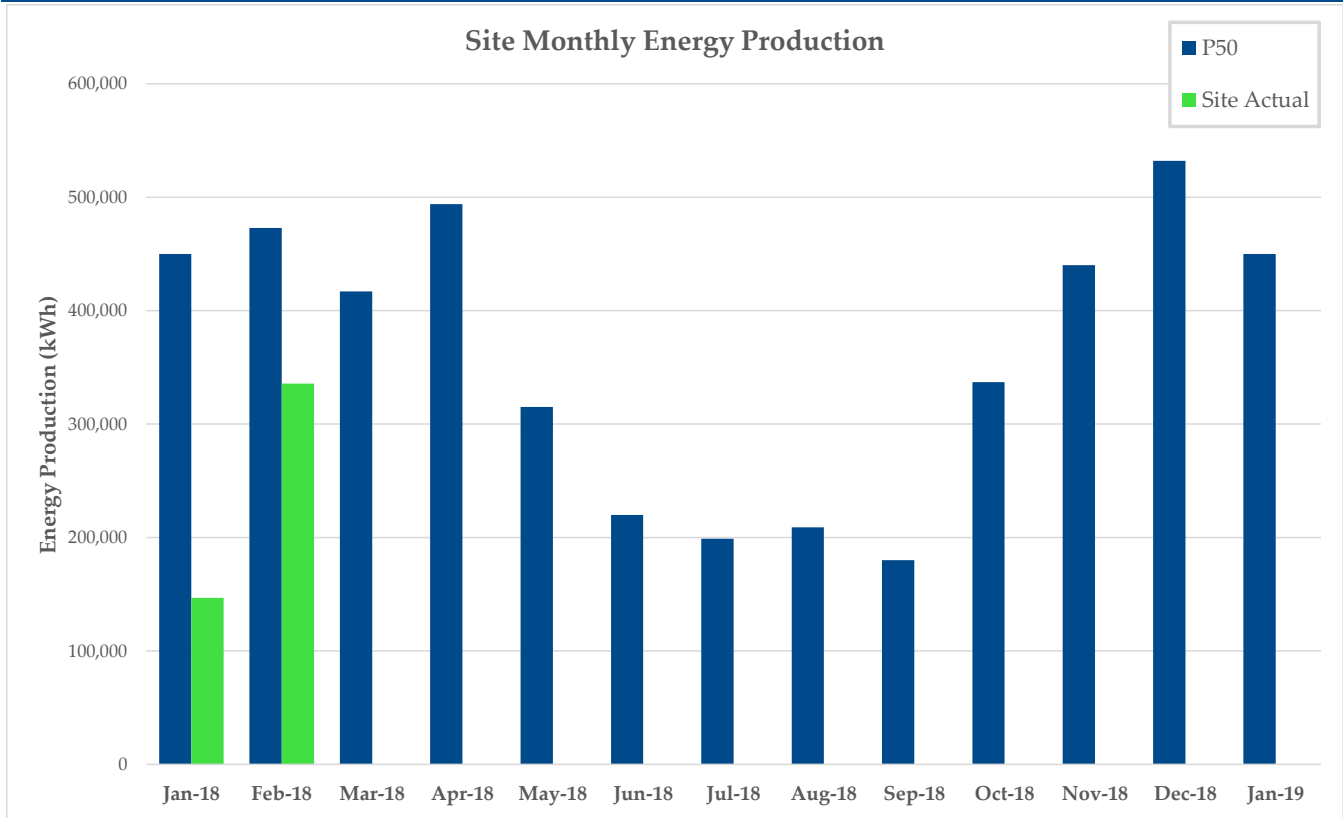

Monthly Report
February-2018

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
August-2018	Goldwind 6-Month Maintenance	~8	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/5-2/7/2018	Grid Fault	Unplanned	53.49	W1
2/14/2018	500 Hour Maintenance	Planned	4.60	W1
2/15/2018	500 Hour Maintenance	Planned	7.34	W1
2/21/2018	500 Hour Maintenance	Planned	7.95	W1
2/22/2018	Icing Event	Unplanned	9.06	W1
2/26/2018	500 Hour Maintenance	Planned	4.95	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.48%	99.48%
	99.48%	
Downtime (hr)	This Month	Year To Date
W1	100.15	100.15

G. Billed Data

Meter Reading (Date/Time)	2/26/2018 12:00 AM
Meter To Date Produced	431,824 kWh
Meter To Date Consumed	6,325 kWh
Last Reading Produced	44,432 kWh
Last Reading Consumed	4,796 kWh
Billed kWh	385,863 kWh
Next Meter Reading	3/26/2018 12:00 AM

H. Report Notes and Comments

**Jan-18 production data read from meter (produced)
**Capacity factor will be included once a year of data has been collected
