




A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Mar-17	808,000	874,319	455,715	418,604
Apr-17	955,000	865,246	435,360	429,886
May-17	607,000	792,979	401,772	391,207
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Oct-17	653,000	711,340	360,752	350,588
Nov-17	851,000	787,741	386,194	401,547
Dec-17	1,029,000	866,109	435,332	430,777
Jan-18	872,000	1,041,086	531,433	509,653
Feb-18	914,000	718,724	362,629	356,095
Mar-18	808,000	853,902	432,831	421,071
Production 2018 (ytd) (kWh)	2,594,000	2,613,712	1,326,893	1,286,819
Total Production (kWh)*	8,251,000	8,300,059	4,182,370	4,117,689
Capacity Factor*	31.58%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

March-2018

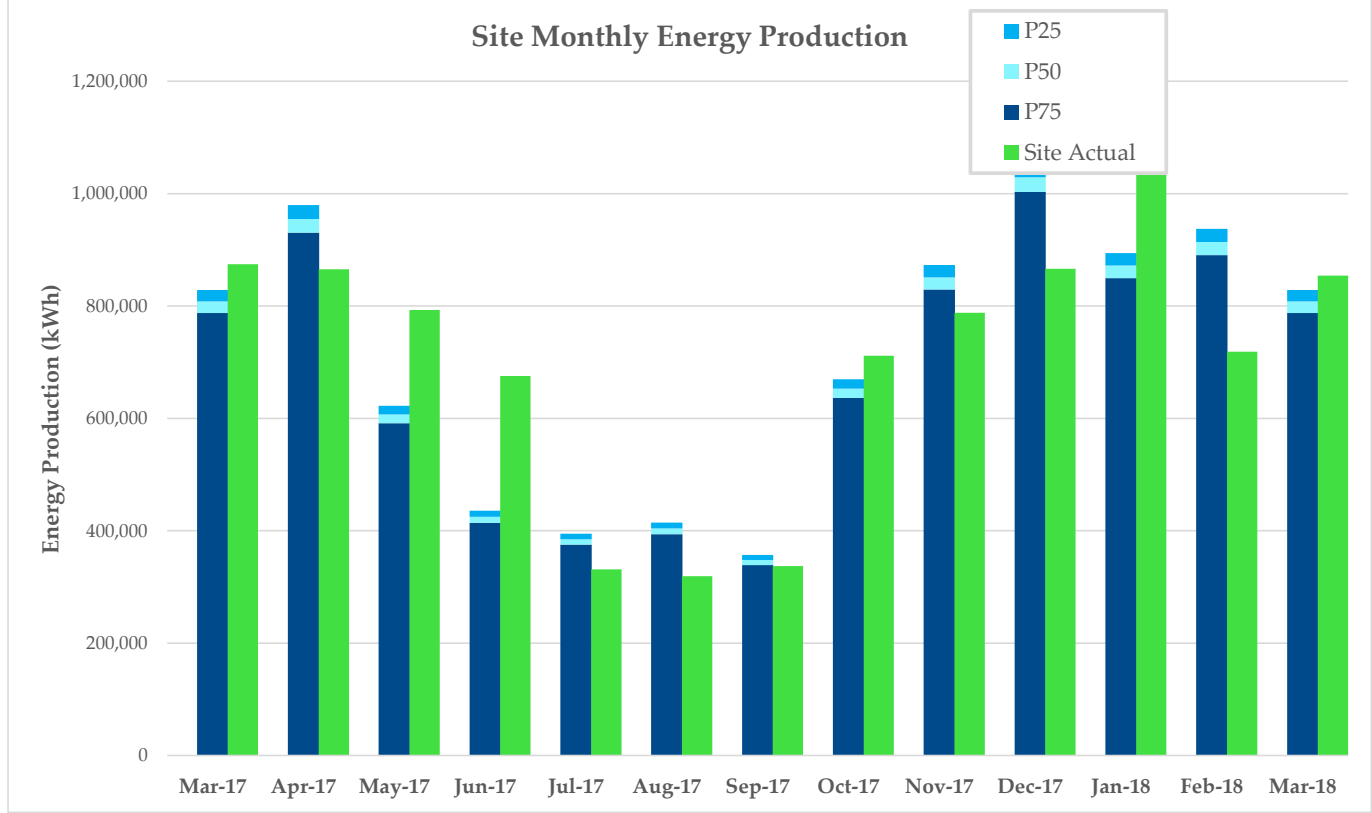

Monthly Report

March-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2018	Goldwind 2 Year Maintenance	~15	W1
May-2018	Goldwind 2 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
------	-------	-------------------	---------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	99.82%	99.82%
W2	99.71%	99.90%
Avg	99.77%	99.86%
Downtime (hr)	This Month	Annual To Date
W1	4.12	74.83
W2	4.40	72.41
Total	8.52	147.24

G. Billed Data

Meter Reading (Date/Time)	3/28/2018 12:00 AM
Meter To Date Produced	17,972,296 kWh
Meter To Date Consumed	33,229 kWh
Last Reading Produced	17,174,446 kWh
Last Reading Consumed	32,691 kWh
Billed kWh	797,312 kWh
Next Meter Reading	4/28/2018 12:00 AM

H. Report Notes and Comments
