

A. Site Energy Production Summary**

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
Nov-17	1,123,000	466,686	-	-	-
Dec-17	1,153,000	852,755	-	-	-
Jan-18	1,306,000	1,214,611	405,820	399,594	409,197
Feb-18	1,137,000	881,991	301,494	285,462	295,035
Mar-18	1,134,000	1,184,135	407,384	386,300	390,451
Apr-18	1,176,000	996,362	345,950	318,571	331,841
May-18	927,000	759,639	251,931	248,291	259,417
Jun-18	634,000	-	-	-	-
Jul-18	527,000	-	-	-	-
Aug-18	449,000	-	-	-	-
Sep-18	610,000	-	-	-	-
Oct-18	990,000	-	-	-	-
Nov-18	1,123,000	-	-	-	-
Production 2018 (ytd) (kWh)	5,680,000	5,036,738	1,712,579	1,638,218	1,685,941
Total Production (kWh)*	-	-	-	-	-
Capacity Factor*	-		*Value calculated over the last 12 months		

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events


Date	Event	Duration (hr)	Turbine
June-2018	Goldwind 6 Month Maintenance	~8	W1
June-2018	Goldwind 6 Month Maintenance	~8	W2
June-2018	Goldwind 6 Month Maintenance	~8	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/27/2018	Customer Maintenance	Unplanned	20.14	W1, W2, W3
5/28/2018	Customer Maintenance	Unplanned	9.31	W1, W2, W3

B. Site Energy Production Graph

May-2018

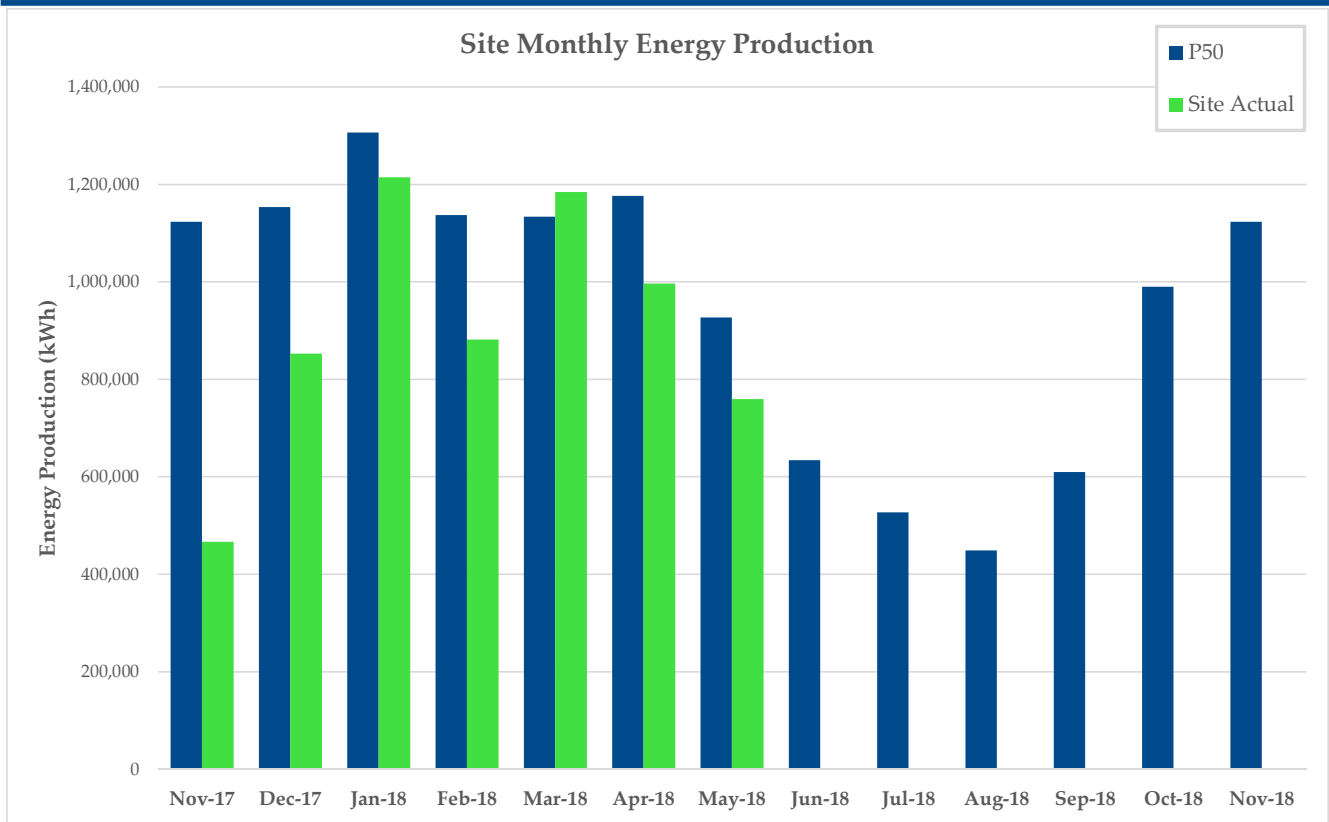

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.74%
W2	99.96%	99.63%
W3	99.66%	99.85%
Avg	99.87%	99.74%

Downtime (hr)	This Month	Year To Date
W1	35.96	238.75
W2	36.47	207.51
W3	38.46	162.45
Total	110.89	608.71

G. Billed Data

Meter Reading (Date/Time)	5/20/2018 12:00 AM
Meter To Date Produced	6,050,221 kWh
Meter To Date Consumed	12,690 kWh
Last Reading Produced	5,261,876 kWh
Last Reading Consumed	11,099 kWh
Billed kWh	786,754 kWh
Next Meter Reading	6/20/2018 12:00 AM

H. Report Notes and Comments

**Nov-17 and Dec-17 production data read from meter. Capacity factor will be included once a year of data has been collected.
