



HARPSTER WIND PROJECT

Harpster, OH


A. Site Energy Production Summary

	Energy Production (kWh)	
	Project	
	P50 (Expected Production)	Actual Production
Jun-17	228,000	236,682
Jul-17	179,000	127,663
Aug-17	157,000	127,837
Sep-17	224,000	129,889
Oct-17	338,000	290,901
Nov-17	402,000	389,716
Dec-17	403,000	369,540
Jan-18	460,000	459,673
Feb-18	372,000	301,893
Mar-18	417,000	387,657
Apr-18	399,000	345,831
May-18	311,000	239,306
Jun-18	228,000	163,129
Production 2018 (ytd) (kWh)	2,187,000	1,897,489
Total Production (kWh)*	3,890,000	3,333,035
Capacity Factor*	25.37%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

June-2018

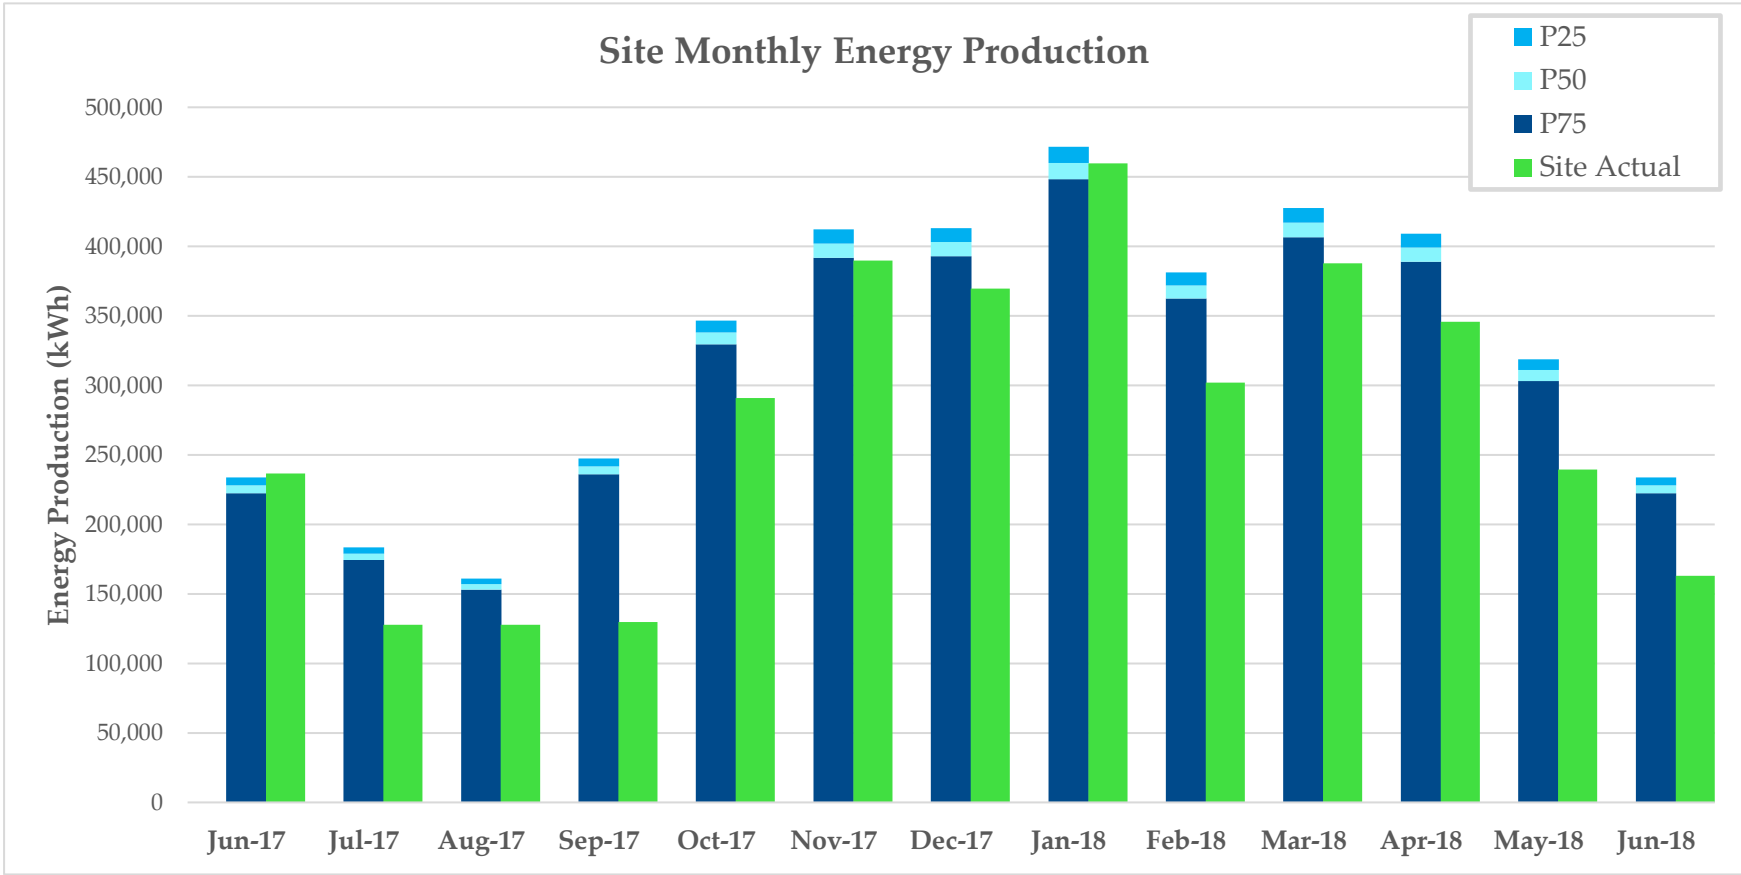

Monthly Report

June-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Wind Turbine
November-2018	Goldwind 2.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Wind Turbine
6/11/2018	Goldwind 2 Year Maintenance	Planned	9.54	H1
6/13/2018	Goldwind 2 Year Maintenance	Planned	4.91	H1
6/14/2018	Goldwind 2 Year Basement Maintenance	Planned	1.49	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
WTG	100.00%	99.89%
Downtime (hr)	This Month	Year To Date
WTG	27.49	143.07

G. Billed Data

Meter Reading (Date/Time)	6/25/2018 12:00 AM
Meter To Date Produced	8,026,339 kWh
Meter To Date Consumed	27,504 kWh
Last Reading Produced	7,854,394 kWh
Last Reading Consumed	26,151 kWh
Billed kWh	170,591 kWh
Next Meter Reading	7/25/2018 12:00 AM

H. Report Notes and Comments
