




A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jun-17	425,000	675,393	338,704	336,689
Jul-17	385,000	331,091	167,175	163,916
Aug-17	404,000	319,203	161,508	157,695
Sep-17	348,000	337,245	168,680	168,565
Oct-17	653,000	711,340	360,752	350,588
Nov-17	851,000	787,741	386,194	401,547
Dec-17	1,029,000	866,109	435,332	430,777
Jan-18	872,000	1,041,086	531,433	509,653
Feb-18	914,000	718,724	362,629	356,095
Mar-18	808,000	853,902	432,831	421,071
Apr-18	955,000	748,389	381,330	367,059
May-18	607,000	594,897	296,616	298,281
Jun-18	425,000	410,074	205,521	204,553
Production 2018 (ytd) (kWh)	4,581,000	4,367,072	2,210,360	2,156,712
Total Production (kWh)*	8,251,000	7,719,801	3,890,001	3,829,800
Capacity Factor*	29.38% *Value calculated over the last 12 months			

B. Site Energy Production Graph

June-2018

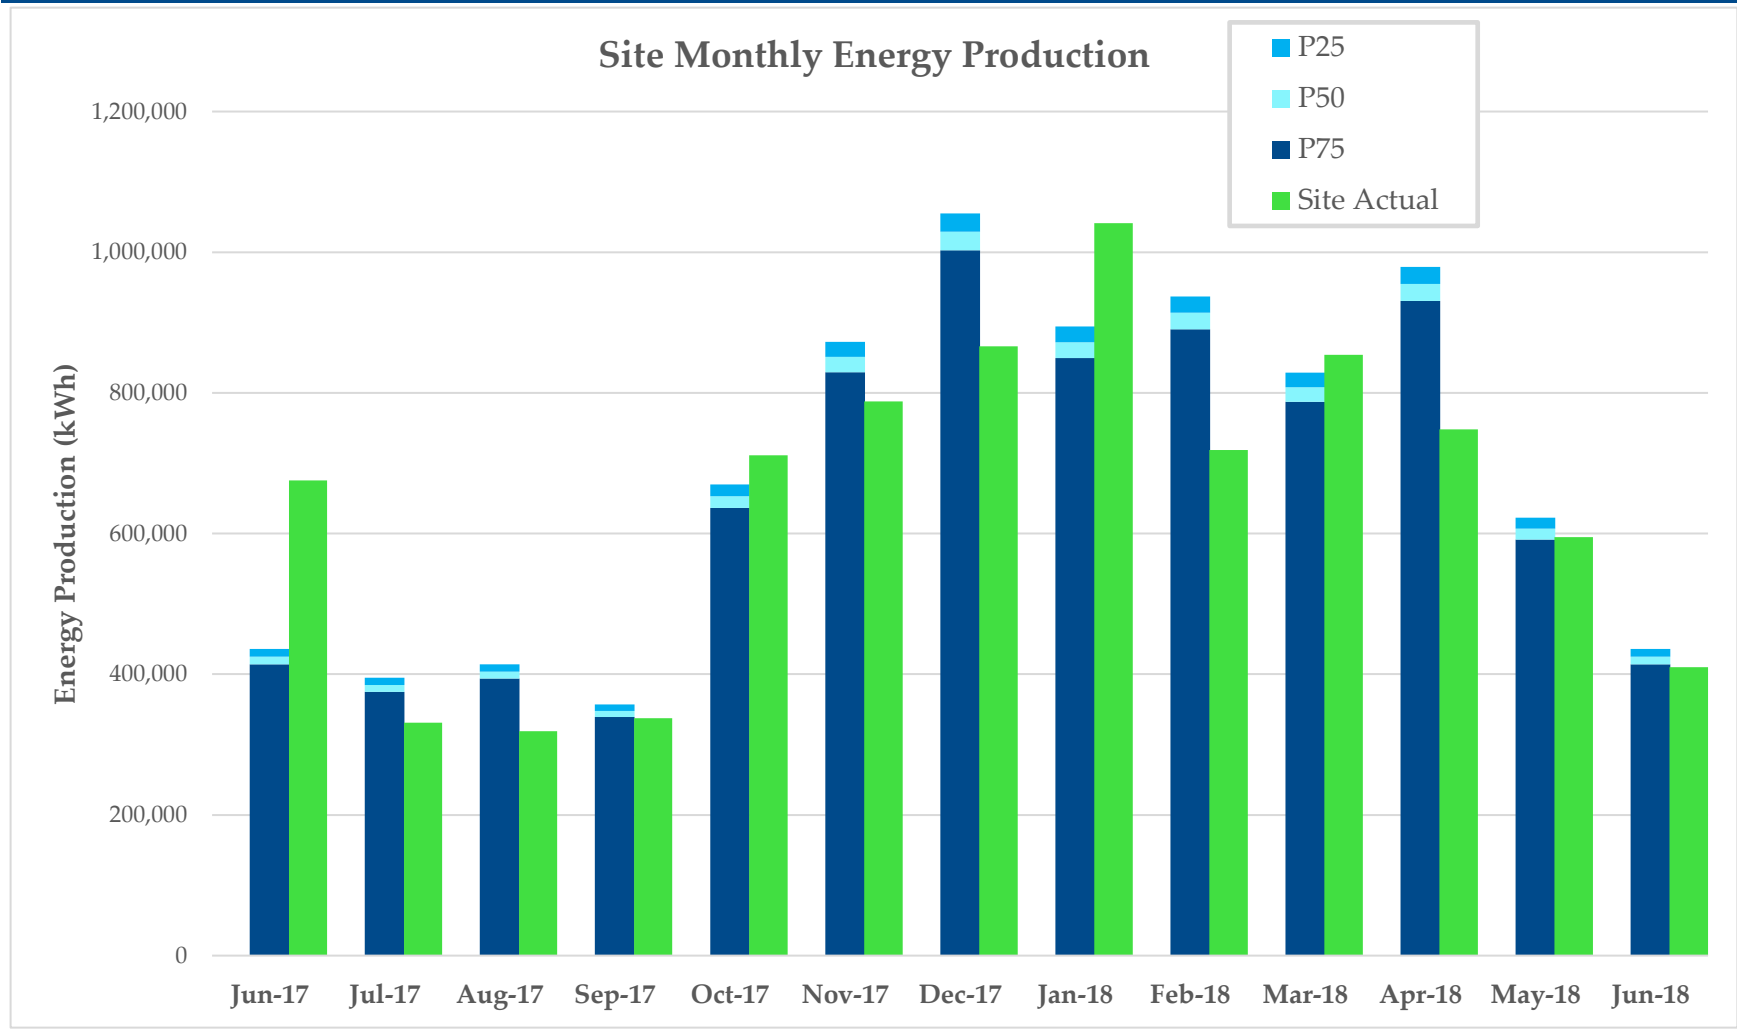

Monthly Report

June-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
July-2018	Goldwind 2 Year Maintenance	~15	W1
July-2018	Goldwind 2 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
6/29/2018	Goldwind 2 Year Maintenance	Planned	5.14	W1

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	100.00%	99.88%
W2	100.00%	99.94%
Avg	100.00%	99.91%

Downtime (hr)	This Month	Annual To Date
W1	14.12	109.90
W2	3.00	83.23
Total	17.12	193.13

G. Billed Data

Meter Reading (Date/Time)	6/28/2018 12:00 AM
Meter To Date Produced	19,750,080 kWh
Meter To Date Consumed	37,140 kWh
Last Reading Produced	19,309,063 kWh
Last Reading Consumed	35,793 kWh
Billed kWh	439,670 kWh
Next Meter Reading	7/28/2018 12:00 AM

H. Report Notes and Comments

*Goldwind 2 Year Maintenance to be completed July-2018
