




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG A	WTG B	WTG C
Aug-17	577,992	550,820	193,760	179,770	177,290
Sep-17	631,697	605,096	208,710	201,632	194,754
Oct-17	1,003,602	1,223,590	422,370	411,740	389,480
Nov-17	1,395,914	1,441,140	493,690	470,470	476,980
Dec-17	1,278,858	1,521,630	522,010	495,750	503,870
Jan-18	1,332,437	1,726,420	585,680	568,390	572,350
Feb-18	1,157,019	1,303,000	447,860	426,380	428,760
Mar-18	1,242,761	1,576,970	530,020	505,480	541,470
Apr-18	1,447,248	1,316,810	462,450	405,270	449,090
May-18	1,010,966	1,077,570	344,730	377,970	354,870
Jun-18	668,411	686,130	223,300	224,540	238,290
Jul-18	638,097	499,960	165,840	165,390	168,730
Aug-18	577,992	610,690	217,500	193,470	199,720
Production 2018 (ytd) (kWh)	8,074,929	8,797,550	2,977,380	2,866,890	2,953,280
Total Production (kWh)*	12,384,999	13,589,006	4,624,160	4,446,482	4,518,364
Capacity Factor*	34.47%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

August-2018

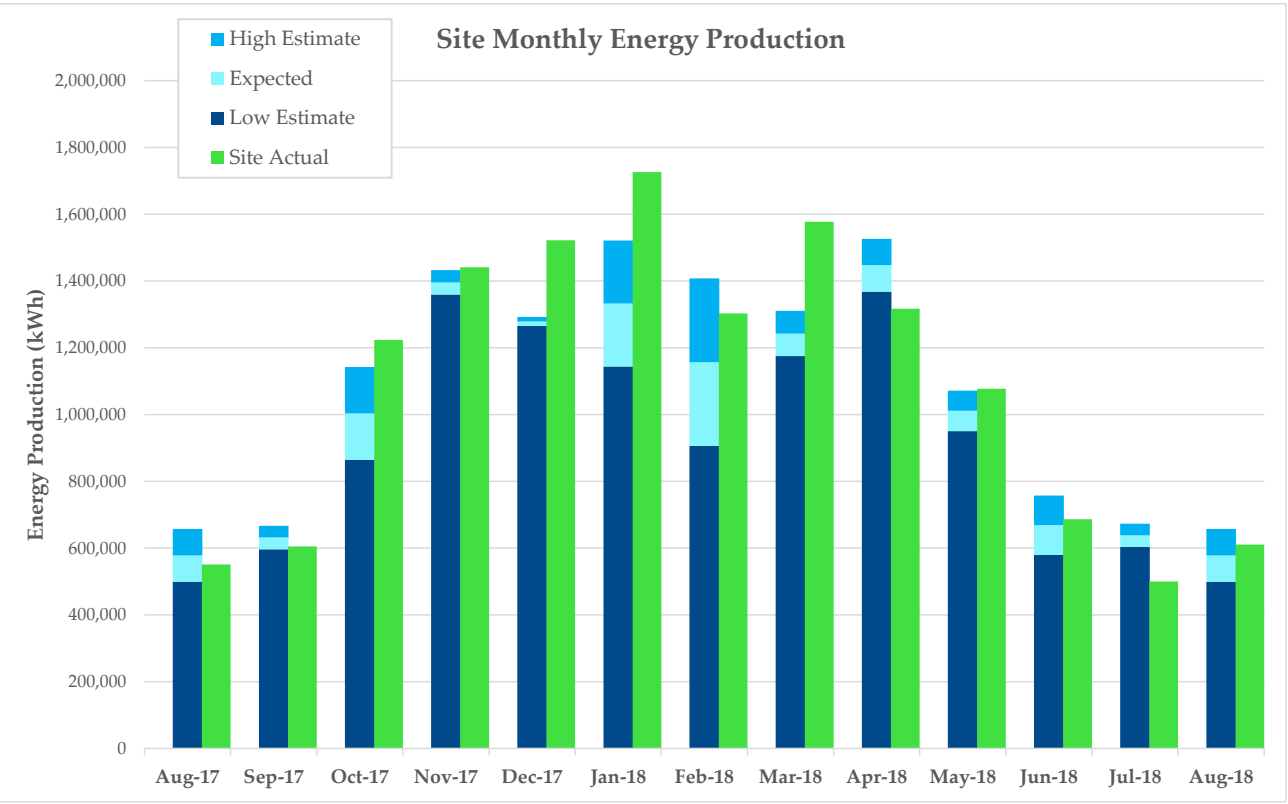

Monthly Report
August-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2018	Goldwind 6.5 Year Maintenance	~8	WTG A
November-2018	Goldwind 6.5 Year Maintenance	~8	WTG B
November-2018	Goldwind 6.5 Year Maintenance	~8	WTG C

E. Actual Maintenance Events - August 2018

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
8/1/2018	Bearing Inspection	Unplanned	6.47	WTG C
8/2/2018	Bearing Inspection	Unplanned	5.86	WTG B
8/5-6/2018	CPU Resource Error	Unplanned	26.88	WTG C
8/6/2018	Bearing Inspection	Unplanned	5.46	WTG B
8/8/2018	Blade Alignment	Unplanned	7.66	WTG A
8/9/2018	Bolt Hole Cleaning	Unplanned	5.23	WTG A
8/10/2018	Basement Maintenance	Planned	4.62	WTG A, B, C
8/15/2018	Goldwind 6 Year Maintenance	Planned	7.31	WTG B
8/17,8/20/2018	Goldwind 6 Year Maintenance	Planned	7.60	WTG C
8/25/2018	Convertor Inductor Temperature Error	Planned	4.28	WTG C

F. Turbine Availability & Downtime

Availability (%)	This Month	Year to Date
WTG A	96.91%	98.14%
WTG B	97.38%	98.55%
WTG C	98.32%	99.51%
Avg	97.54%	98.73%

Downtime (hr)	This Month	Year to Date
WTG A	34.13	210.25
WTG B	37.92	185.29
WTG C	58.05	160.83
Total	130.10	556.37

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2018 Annual
WTG A	9.87	12.07
WTG B	9.69	12.05
WTG C	10.40	12.73
Estimated	11.09	13.39

Capacity Factor (%)	This Month	2018 Annual
WTG A	19.49%	34.03%
WTG B	17.34%	32.77%
WTG C	17.90%	33.76%
Low Estimate	14.90%	33.52%

H. Report Notes and Comments
