


A. Site Energy Production Summary

	Energy Production (kWh)		
	Site		
	P50 (Expected Production)	Actual Production	
Jan-18	450,000	146,791	**
Feb-18	473,000	335,605	
Mar-18	417,000	442,275	
Apr-18	494,000	391,503	
May-18	315,000	324,011	
Jun-18	220,000	202,020	
Jul-18	199,000	149,361	
Aug-18	209,000	149,747	
Sep-18	180,000	-	
Oct-18	337,000	-	
Nov-18	440,000	-	
Dec-18	532,000	-	
Jan-19	450,000	-	
Production 2018 (ytd) (kWh)	2,777,000	2,141,313	
Total Production (kWh)*	-	-	
Capacity Factor*	-		*Value calculated over the last 12 months

*Value calculated over the last 12 months

B. Site Energy Production Graph

August-2018

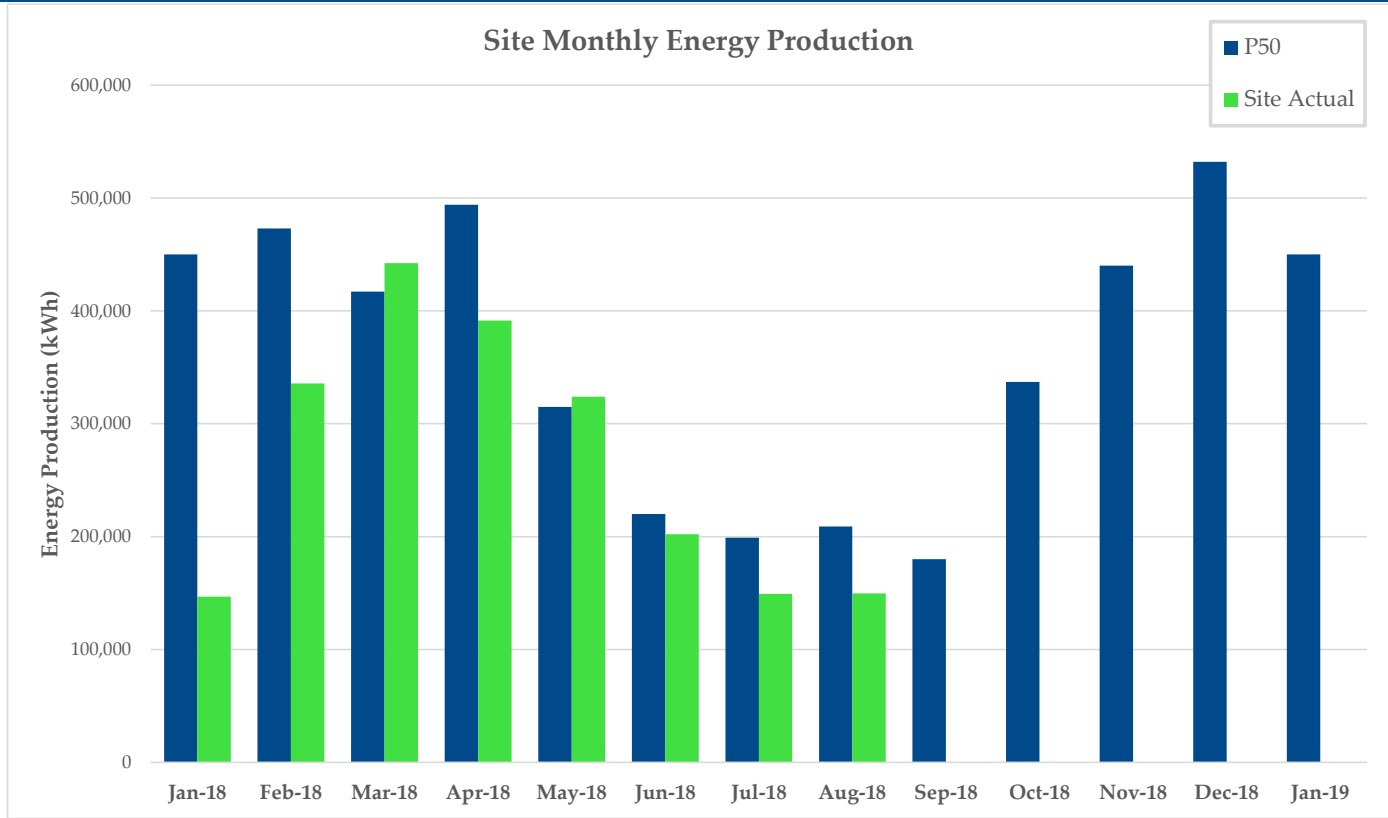

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
August-2018	Goldwind 6-Month Maintenance	~8	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
8/19/2018	Grid Fault	Unplanned	19.06	W1
8/20/2018	Grid Fault	Unplanned	13.53	W1
8/21/2018	Goldwind 6-Month Maintenance	Planned	3.25	W1
8/23/2018	Goldwind 6-Month Maintenance	Planned	6.00	W1
8/28-31/2018	Blade Repairs	Unplanned	88.75	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.77%
Downtime (hr)	This Month	Year To Date
W1	132.78	255.38

G. Billed Data

Meter Reading (Date/Time)	8/31/2018 12:00 AM
Meter To Date Produced	2,108,033 kWh
Meter To Date Consumed	15,403 kWh
Last Reading Produced	1,954,518 kWh
Last Reading Consumed	13,593 kWh
Billed kWh	151,704 kWh
Next Meter Reading	9/30/2018 12:00 AM

H. Report Notes and Comments

*Capacity factor will be included once a year of data has been collected

**Jan-18 production data read from meter (produced)
