




A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Nov-17	851,000	787,741	386,194	401,547
Dec-17	1,029,000	866,109	435,332	430,777
Jan-18	872,000	1,041,086	531,433	509,653
Feb-18	914,000	718,724	362,629	356,095
Mar-18	808,000	853,902	432,831	421,071
Apr-18	955,000	748,389	381,330	367,059
May-18	607,000	594,897	296,616	298,281
Jun-18	425,000	410,074	205,521	204,553
Jul-18	385,000	278,804	145,255	133,549
Aug-18	404,000	365,718	185,127	180,591
Sep-18	346,000	399,326	202,515	196,811
Oct-18	649,000	709,011	359,965	349,046
Nov-18	846,000	616,294	307,095	309,199
Production 2018 (ytd) (kWh)	7,211,000	6,736,225	3,410,317	3,325,908
Total Production (kWh)*	8,240,000	7,602,334	3,845,649	3,756,685
Capacity Factor*	28.93% *Value calculated over the last 12 months			

B. Site Energy Production Graph

November-2018

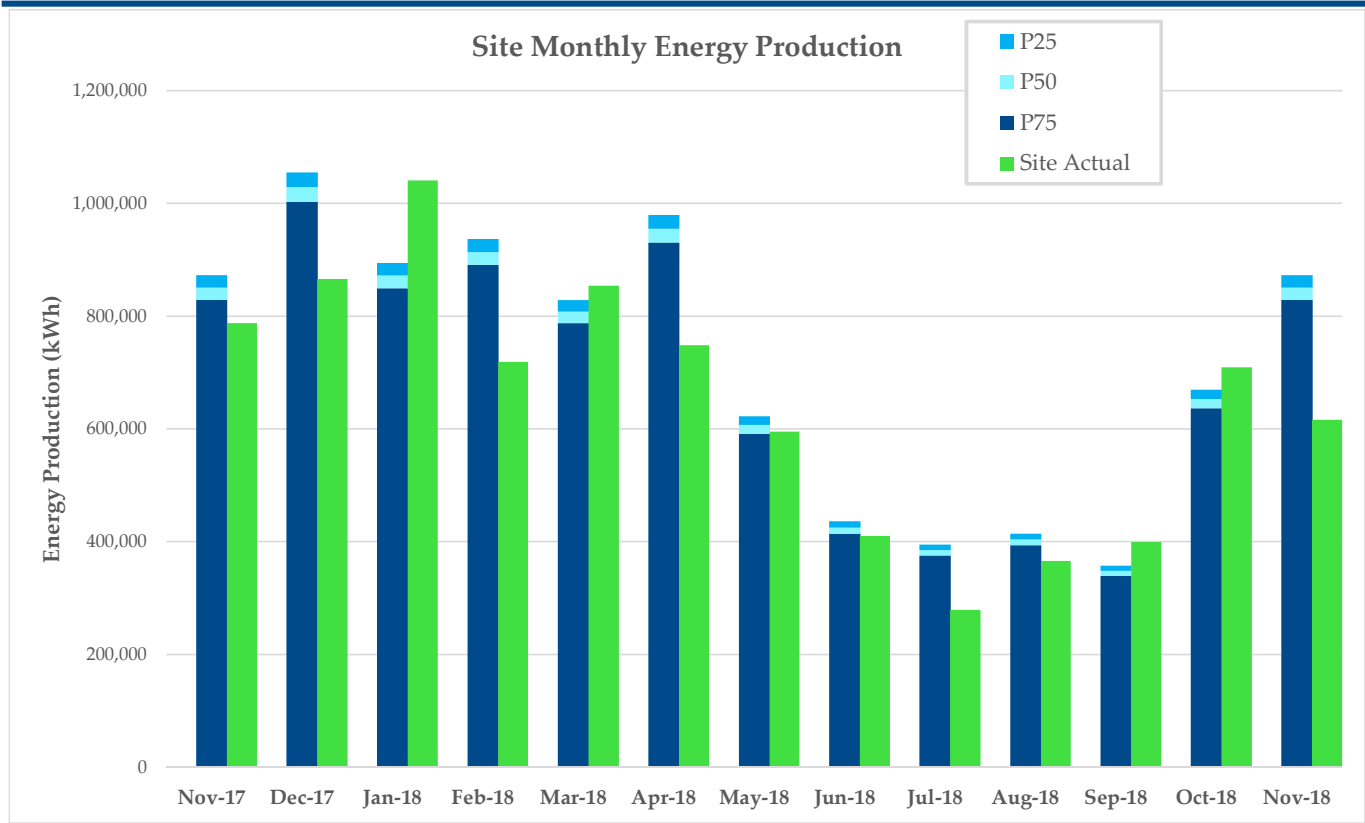

Monthly Report
November-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
December-2018	Goldwind 2.5 Year Maintenance	~8	W1
December-2018	Goldwind 2.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
11/15-16/2018	Icing Event	Unplanned	38.68	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	100.00%	99.93%
W2	100.00%	99.96%
Avg	100.00%	99.95%
Downtime (hr)	This Month	Annual To Date
W1	45.43	185.04
W2	42.35	155.42
Total	87.78	340.46

G. Billed Data

Meter Reading (Date/Time)	11/28/2018 12:00 AM
Meter To Date Produced	22,083,474 kWh
Meter To Date Consumed	44,819 kWh
Last Reading Produced	21,414,893 kWh
Last Reading Consumed	42,992 kWh
Billed kWh	666,754 kWh
Next Meter Reading	12/28/2018 12:00 AM

H. Report Notes and Comments

*Change to P50 Expected Production due to Material Change in Circumstance.
