




A. Site Energy Production Summary*

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WG1	WG2	WG3
Oct-18	990,000	679,703	238,340	226,535	214,828
Nov-18	1,123,000	816,424	287,961	268,275	260,188
Dec-18	1,153,000	1,053,069	363,815	347,442	341,812
Jan-19	1,306,000	-	-	-	-
Feb-19	1,137,000	-	-	-	-
Mar-19	1,134,000	-	-	-	-
Apr-19	1,176,000	-	-	-	-
May-19	927,000	-	-	-	-
Jun-19	634,000	-	-	-	-
Jul-19	527,000	-	-	-	-
Aug-19	449,000	-	-	-	-
Sep-19	610,000	-	-	-	-
Oct-19	990,000	-	-	-	-
Production 2018 (ytd) (kWh)	3,266,000	2,549,196	890,116	842,252	816,828
Total Production (kWh)*	-	-	-	-	-
Capacity Factor*	- *Value calculated over the last 12 months				

B. Site Energy Production Graph

December-2018

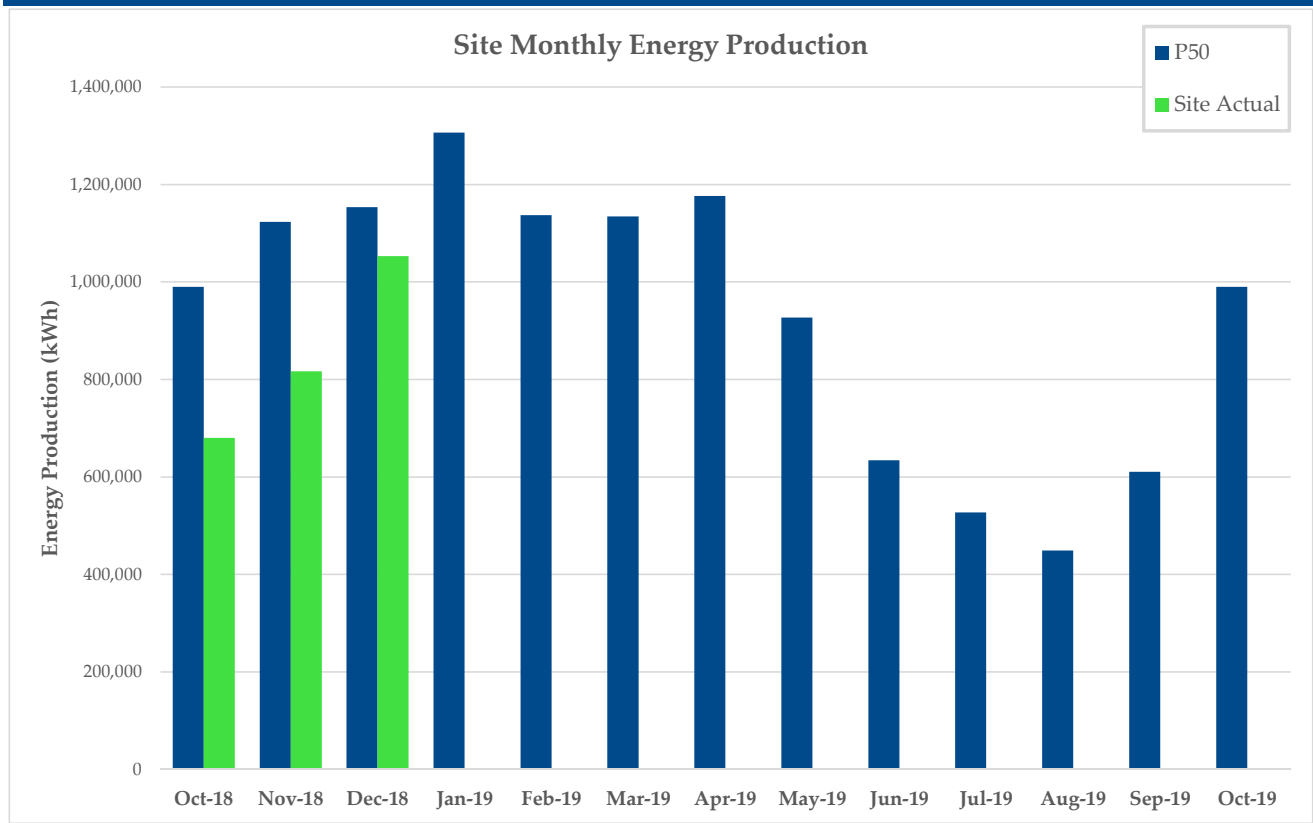

Monthly Report
December-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
April-2019	Goldwind 6 Month Maintenance	~8	WG 1
April-2019	Goldwind 6 Month Maintenance	~8	WG 2
April-2019	Goldwind 6 Month Maintenance	~8	WG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
12/6/2018	Icing Event	Unplanned	5.51	WG 1
12/7/2018	Icing Event	Unplanned	12.84	WG 1
12/11/2018	Icing Event	Unplanned	10.50	WG 1, 2, 3

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
WG1	100.00%	100.00%
WG2	100.00%	100.00%
WG3	100.00%	99.24%
Avg	100.00%	99.75%

Downtime (hr)	This Month	Year To Date
WG1	28.85	247.07
WG2	10.50	186.13
WG3	10.50	274.01
Total	49.85	707.21

G. Billed Data

Meter Reading (Date/Time)	12/28/2018 12:00 AM
Meter To Date Produced	2,269,540 kWh
Meter To Date Consumed	9,085 kWh
Last Reading Produced	1,332,616 kWh
Last Reading Consumed	5,480 kWh
Billed kWh	933,319 kWh
Next Meter Reading	1/28/2019 12:00 AM

H. Report Notes and Comments

*Capacity factor to be included once full year of data is available.
**Goldwind 500 Hour Maintenance completed in November-2018.
