




Monthly Report
January-2019



A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jan-18	872,000	1,041,086	531,433	509,653
Feb-18	914,000	718,724	362,629	356,095
Mar-18	808,000	853,902	432,831	421,071
Apr-18	955,000	748,389	381,330	367,059
May-18	607,000	594,897	296,616	298,281
Jun-18	425,000	410,074	205,521	204,553
Jul-18	385,000	278,804	145,255	133,549
Aug-18	404,000	365,718	185,127	180,591
Sep-18	346,000	399,326	202,515	196,811
Oct-18	649,000	709,011	359,965	349,046
Nov-18	846,000	616,294	307,095	309,199
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Production 2019 (ytd) (kWh)	867,000	942,829	486,578	456,251
Total Production (kWh)*	8,228,000	7,375,010	3,741,861	3,633,149
Capacity Factor*	28.06%		*Value calculated over the last 12 months	

B. Site Energy Production Graph January-2019

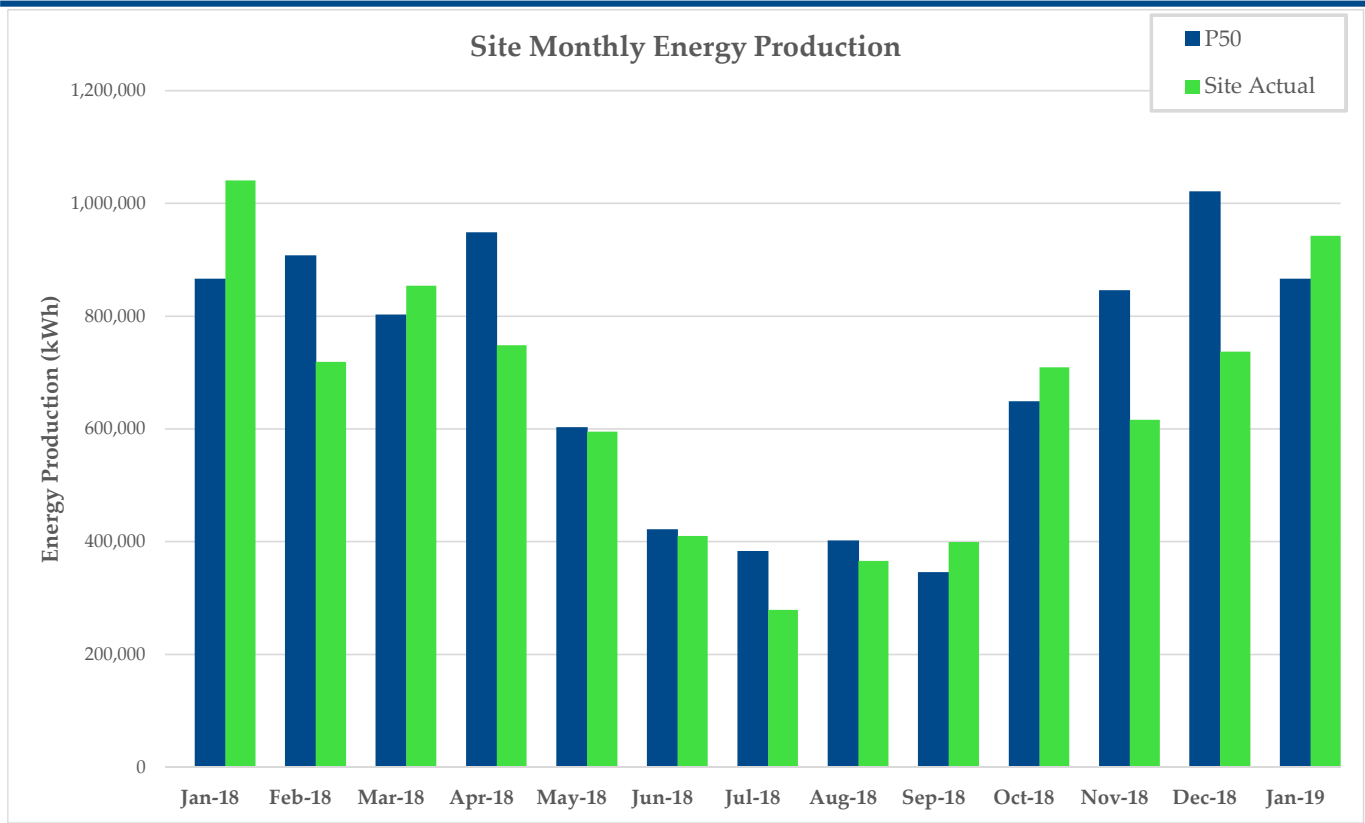

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
May-2019	Goldwind 3.5 Year Maintenance	~8	W1
May-2019	Goldwind 3.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
1/15-16/2019	Icing Event	Unplanned	18.22	W1
1/15-16/2019	Icing Event	Unplanned	18.61	W2
1/17/2019	Goldwind 3 Year Maintenance	Planned	1.31	W1, W2
1/21/2019	Pitch Code Error	Unplanned	10.07	W1
1/21-22/2019	Convertor Voltage Error	Unplanned	28.18	W2
1/24/2019	Goldwind 3 Year Maintenance	Planned	8.94	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	98.17%	98.17%
W2	96.17%	96.17%
Avg	97.17%	97.17%
Downtime (hr)	This Month	Annual To Date
W1	48.37	48.37
W2	60.47	60.47
Total	108.84	108.84

G. Billed Data

Meter Reading (Date/Time)	1/28/2019 12:00 AM
Meter To Date Produced	23,571,131 kWh
Meter To Date Consumed	47,850 kWh
Last Reading Produced	22,723,844 kWh
Last Reading Consumed	46,305 kWh
Billed kWh	845,742 kWh
Next Meter Reading	2/28/2019 12:00 AM

H. Report Notes and Comments

*Change to P50 Expected Production due to Material Change in Circumstance.
