


A. Site Energy Production Summary

	Energy Production (kWh)		
	Site		
	P50 (Expected Production)	Actual Production	
Jan-18	450,000	146,791	**
Feb-18	473,000	335,605	
Mar-18	417,000	442,275	
Apr-18	494,000	391,503	
May-18	315,000	324,011	
Jun-18	220,000	202,020	
Jul-18	199,000	149,361	
Aug-18	209,000	149,747	
Sep-18	180,000	120,485	
Oct-18	337,000	377,866	
Nov-18	440,000	347,233	
Dec-18	532,000	384,067	
Jan-19	450,000	424,745	
Production 2019 (ytd) (kWh)	450,000	424,745	
Total Production (kWh)*	4,266,000	3,648,918	
Capacity Factor*	27.77%		*Value calculated over the last 12 months

B. Site Energy Production Graph

January-2019

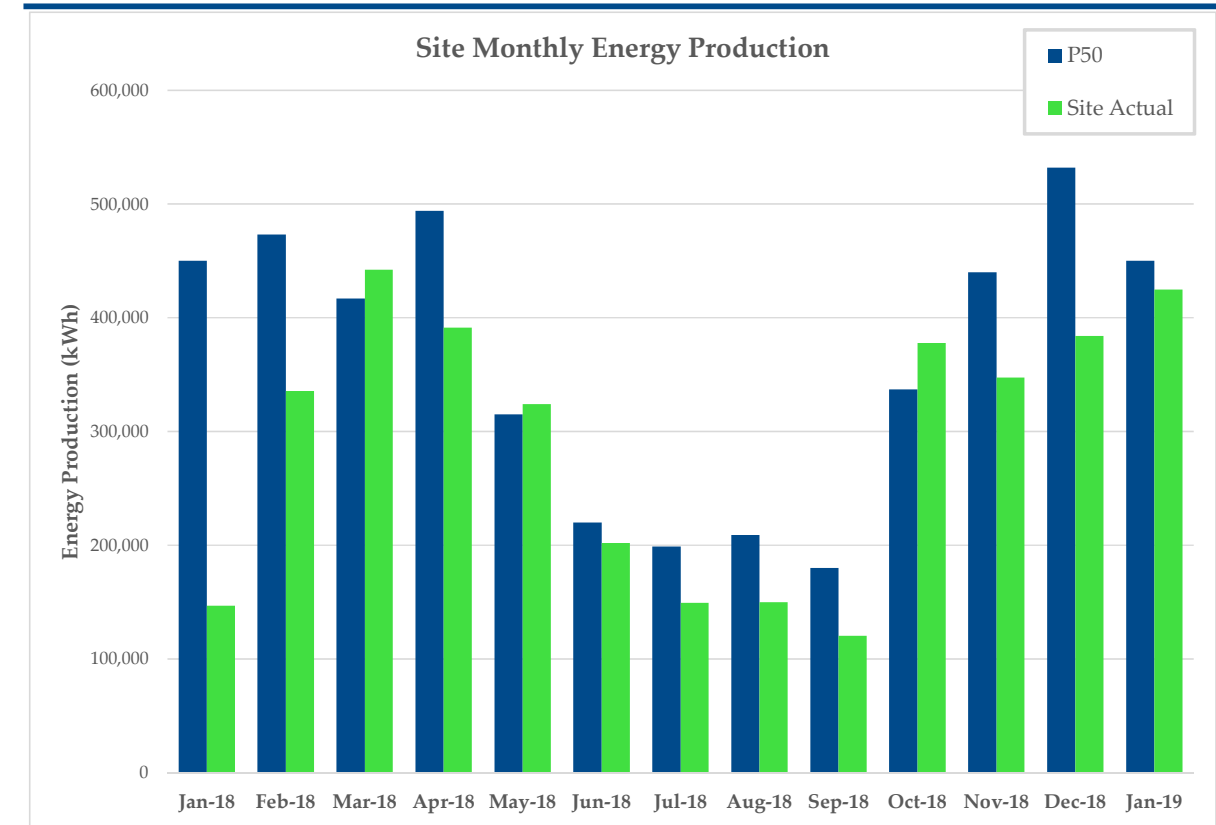

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
February-2019	Goldwind 1 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/ Unplanned	Duration (hrs)	Turbine
1/15-16/2019	Icing Event	Unplanned	34.33	W1
1/26/2019	Pitch Angle Error	Unplanned	14.68	W1
1/26/2019	Cable Bracket Investigation	Unplanned	9.25	W1
1/27/2019	Cable Bracket Investigation	Unplanned	7.74	W1
1/29-31/2019	Pitch Angle Error, unable to correct due to high wind	Unplanned	47.91	W1
1/31/2019	Pitch Angle Error correction	Unplanned	7.43	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	96.97%	96.97%
Downtime (hr)	This Month	Year To Date
W1	124.59	124.59

G. Billed Data

Meter Reading (Date/Time)	1/31/2019 12:00 AM
Meter To Date Produced	3,739,783 kWh
Meter To Date Consumed	23,230 kWh
Last Reading Produced	3,308,684 kWh
Last Reading Consumed	21,445 kWh
Billed kWh	429,315 kWh
Next Meter Reading	2/28/2019 12:00 AM

H. Report Notes and Comments

*Goldwind 1 Year Maintenance moved to February.
**Jan-18 production data read from meter (produced)
