




A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Feb-18	473,000	335,605
Mar-18	417,000	442,275
Apr-18	494,000	391,503
May-18	315,000	324,011
Jun-18	220,000	202,020
Jul-18	199,000	149,361
Aug-18	209,000	149,747
Sep-18	180,000	120,485
Oct-18	337,000	377,866
Nov-18	440,000	347,233
Dec-18	532,000	384,067
Jan-19	450,000	424,745
Feb-19	473,000	354,625
Production 2019 (ytd) (kWh)	923,000	779,370
Total Production (kWh)*	4,266,000	3,667,938
Capacity Factor*	27.91%	

*Value calculated over last 12 months

B. Site Energy Production Graph

February-2019

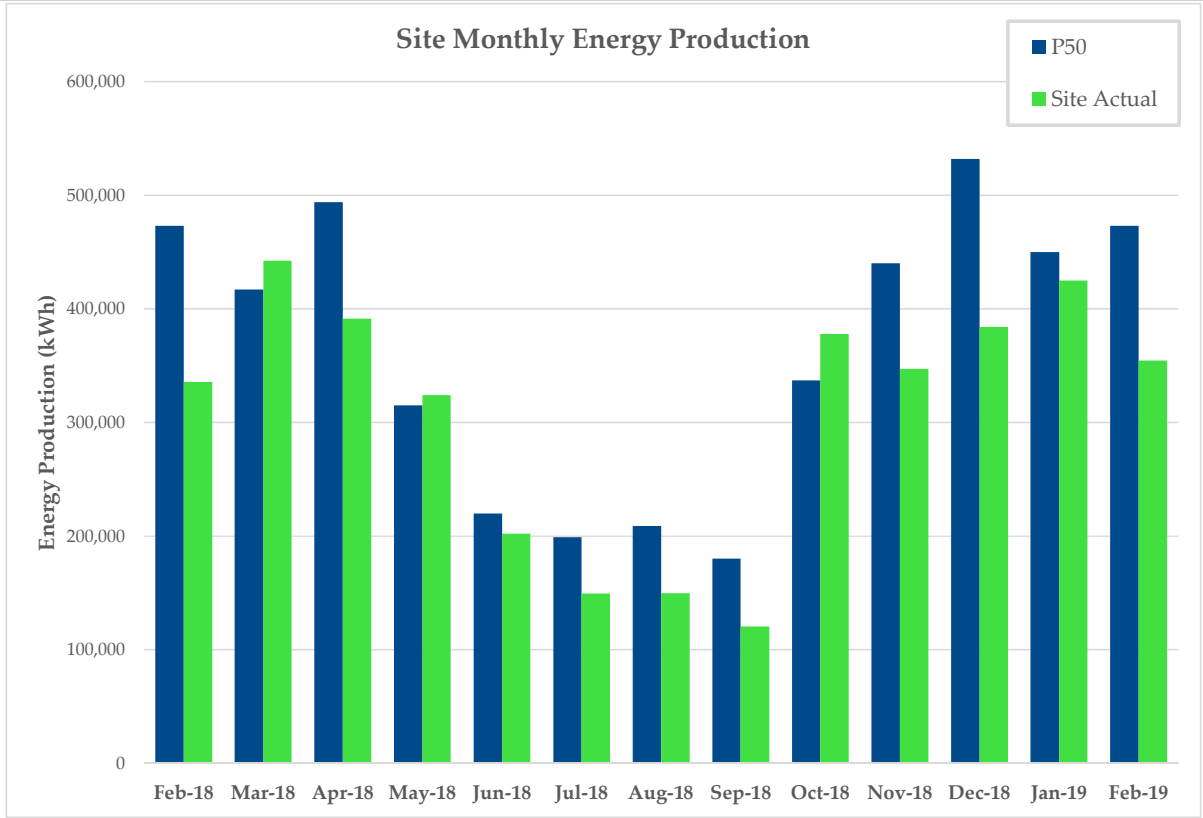

Monthly Report
February-2019



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
March-2019	Goldwind 1 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/2/2019	Blade Pitch Angle Error	Unplanned	6.24	W1
2/11/2019	Icing Event	Unplanned	16.33	W1
2/12/2019	Icing Event	Unplanned	12.66	W1
2/17/2019	Icing Event	Unplanned	2.39	W1
2/18/2019	Icing Event	Unplanned	14.94	W1
2/19/2019	Icing Event	Unplanned	5.41	W1
2/24/2019	High Wind Event	Unplanned	21.13	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.07%	97.97%
Downtime (hr)	This Month	Year To Date
W1	79.10	203.69

G. Billed Data

Meter Reading (Date/Time)	3/1/2019 12:00 AM
Meter To Date Produced	4,089,434 kWh
Meter To Date Consumed	25,227 kWh
Last Reading Produced	3,739,783 kWh
Last Reading Consumed	23,230 kWh
Billed kWh	347,654 kWh
Next Meter Reading	4/1/2019 12:00 AM

H. Report Notes and Comments

*Goldwind 1 Year Maintenance moved to March.
