




A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Mar-18	808,000	853,902	432,831	421,071
Apr-18	955,000	748,389	381,330	367,059
May-18	607,000	594,897	296,616	298,281
Jun-18	425,000	410,074	205,521	204,553
Jul-18	385,000	278,804	145,255	133,549
Aug-18	404,000	365,718	185,127	180,591
Sep-18	346,000	399,326	202,515	196,811
Oct-18	649,000	709,011	359,965	349,046
Nov-18	846,000	616,294	307,095	309,199
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Production 2019 (ytd) (kWh)	2,578,000	2,499,063	1,278,479	1,220,584
Total Production (kWh)*	8,217,000	7,358,618	3,738,302	3,620,316
Capacity Factor*	28.00%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

March-2019

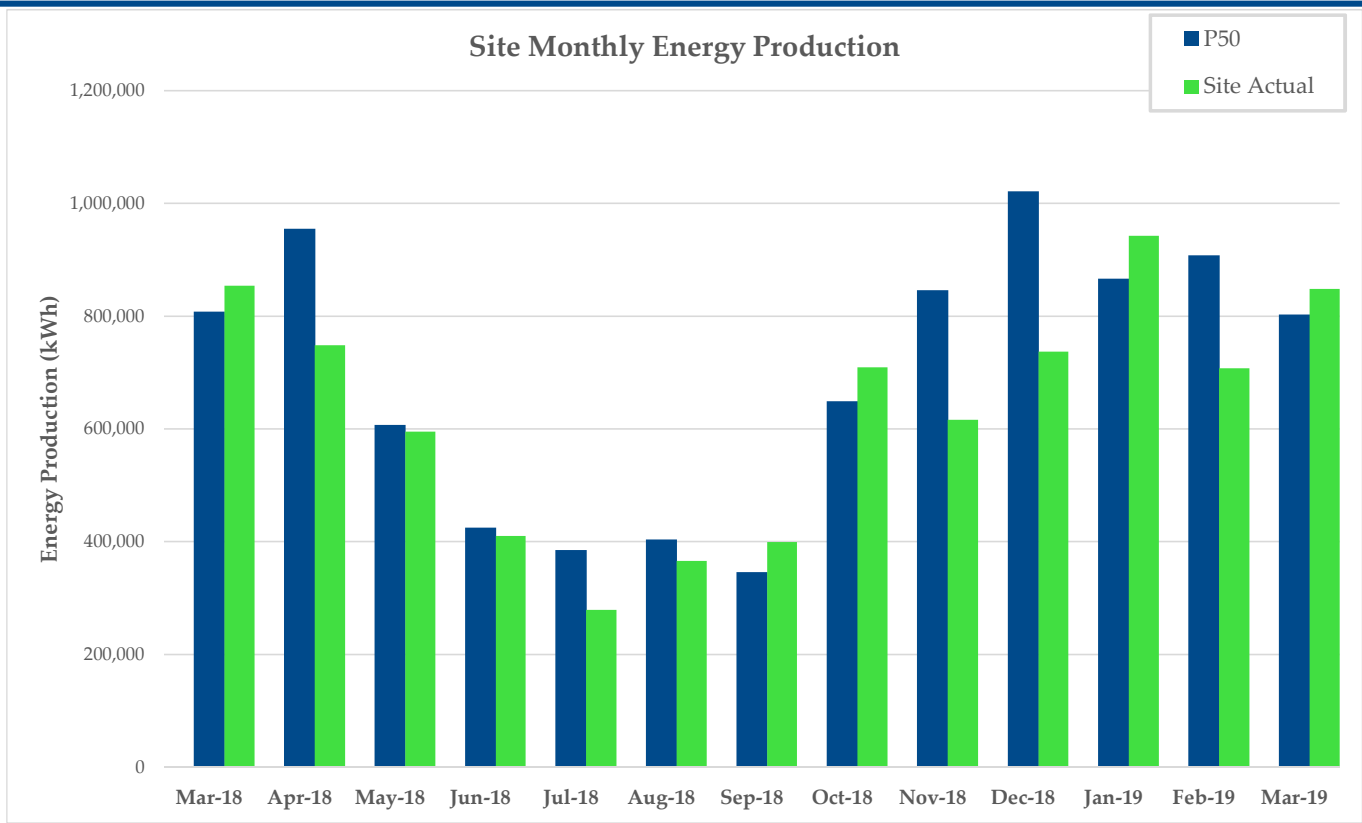

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
May-2019	Goldwind 3.5 Year Maintenance	~8	W1
May-2019	Goldwind 3.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
------	-------	-------------------	---------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	100.00%	99.37%
W2	100.00%	98.68%
Avg	100.00%	99.03%
Downtime (hr)	This Month	Annual To Date
W1	0.16	125.01
W2		135.59
Total	0.16	260.6

G. Billed Data

Meter Reading (Date/Time)	3/29/2019 12:00 AM
Meter To Date Produced	25,217,186 kWh
Meter To Date Consumed	51,095 kWh
Last Reading Produced	24,477,966 kWh
Last Reading Consumed	49,996 kWh
Billed kWh	738,121 kWh
Next Meter Reading	4/29/2019 12:00 AM

H. Report Notes and Comments

*Change to P50 Expected Production due to Material Change in Circumstance.
