


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Mar-18	417,000	442,275
Apr-18	494,000	391,503
May-18	315,000	324,011
Jun-18	220,000	202,020
Jul-18	199,000	149,361
Aug-18	209,000	149,747
Sep-18	180,000	120,485
Oct-18	337,000	377,866
Nov-18	440,000	347,233
Dec-18	532,000	384,067
Jan-19	450,000	424,745
Feb-19	473,000	354,625
Mar-19	417,000	450,944
Production 2019 (ytd) (kWh)	1,340,000	1,230,314
Total Production (kWh)*	4,266,000	3,676,607
Capacity Factor*	27.98%	

*Value calculated over last 12 months

B. Site Energy Production Graph

March-2019

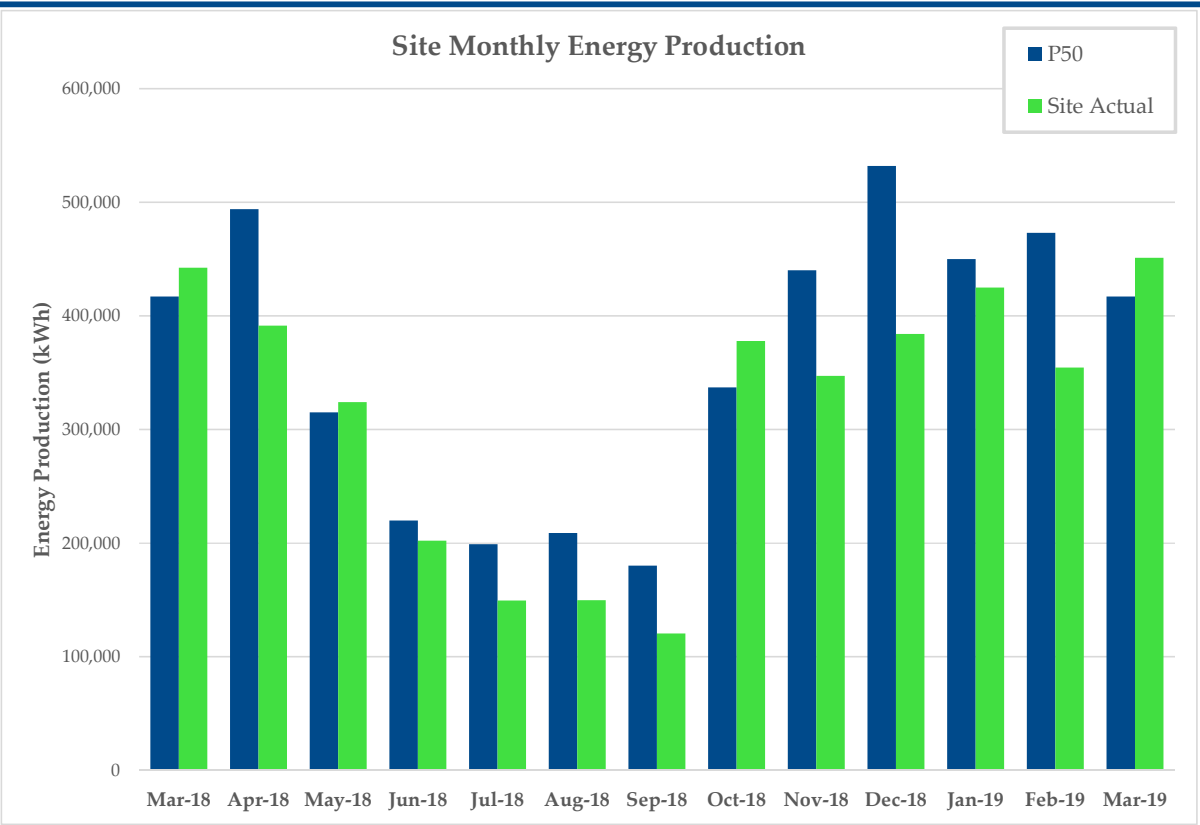

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
September-2019	Goldwind 1.5 Year Maintenance	~8	W1

E. Actual Maintenance Events

Date	Event	Planned/ Unplanned	Duration (hrs)	Turbine
3/13/2019	Goldwind 1 Year Maintenance	Planned	6.62	W1
3/19/2019	Goldwind 1 Year Maintenance	Planned	3.09	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.97%	98.66%

Downtime (hr)	This Month	Year To Date
W1	9.92	213.61

G. Billed Data

Meter Reading (Date/Time)	4/1/2019 12:00 AM
Meter To Date Produced	4,534,108 kWh
Meter To Date Consumed	26,485 kWh
Last Reading Produced	4,089,434 kWh
Last Reading Consumed	25,227 kWh
Billed kWh	443,416 kWh
Next Meter Reading	5/1/2019 12:00 AM

H. Report Notes and Comments
