




A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Apr-18	955,000	748,389	381,330	367,059
May-18	607,000	594,897	296,616	298,281
Jun-18	425,000	410,074	205,521	204,553
Jul-18	385,000	278,804	145,255	133,549
Aug-18	404,000	365,718	185,127	180,591
Sep-18	346,000	399,326	202,515	196,811
Oct-18	649,000	709,011	359,965	349,046
Nov-18	846,000	616,294	307,095	309,199
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Apr-19	949,000	852,957	427,080	425,877
Production 2019 (ytd) (kWh)	3,527,000	3,352,020	1,705,559	1,646,461
Total Production (kWh)*	8,211,000	7,463,186	3,784,052	3,679,134
Capacity Factor*	28.40%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

April-2019

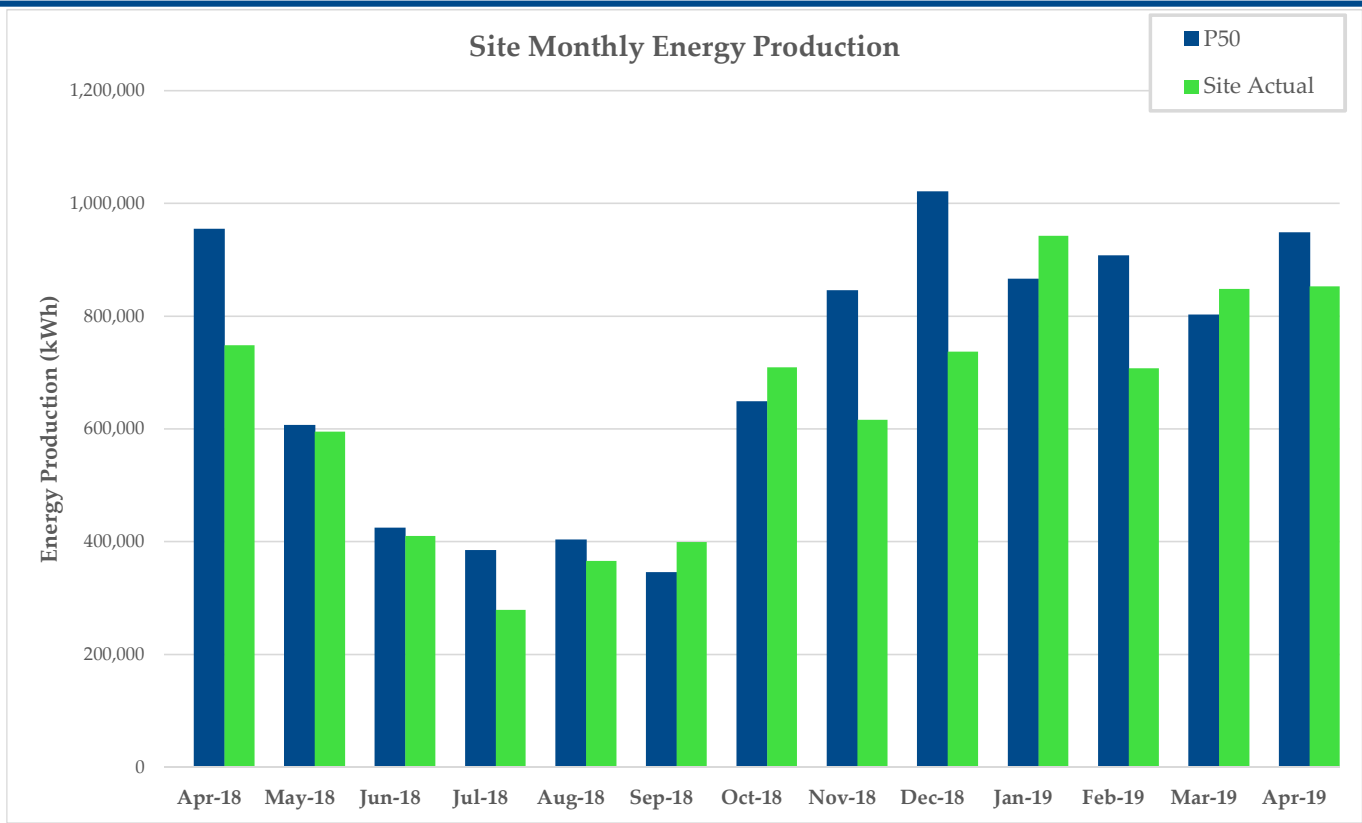

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
May-2019	Goldwind 3.5 Year Maintenance	~8	W1
May-2019	Goldwind 3.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
4/26/2019	High Water Event	Unplanned	9.68	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Annual To Date
W1	100.00%	99.53%
W2	100.00%	99.01%
Avg	100.00%	99.27%
Downtime (hr)	This Month	Annual To Date
W1	12.81	137.82
W2	9.93	145.52
Total	22.74	283.34

G. Billed Data

Meter Reading (Date/Time)	4/29/2019 12:00 AM
Meter To Date Produced	26,123,794 kWh
Meter To Date Consumed	52,041 kWh
Last Reading Produced	25,217,186 kWh
Last Reading Consumed	51,095 kWh
Billed kWh	905,663 kWh
Next Meter Reading	5/29/2019 12:00 AM

H. Report Notes and Comments

*Change to P50 Expected Production due to Material Change in Circumstance.
