


A. Site Energy Production Summary

		Energy Production (kWh)				
		Site		By Turbine		
		P50 (Expected Production)	Actual Production	V1	V2	
	Sep-18	449,000	151,192	-	-	**
	Oct-18	688,000	665,292	327,890	337,402	
	Nov-18	804,000	481,743	247,418	234,325	
	Dec-18	822,000	694,925	363,901	331,024	
	Jan-19	924,000	965,472	479,398	486,074	
	Feb-19	736,000	656,163	327,762	328,401	
	Mar-19	794,000	838,578	420,238	418,340	
	Apr-19	734,000	855,698	425,093	430,605	
	May-19	574,000	605,674	299,620	306,054	
	Jun-19	429,000	-	-	-	
	Jul-19	357,000	-	-	-	
	Aug-19	314,000	-	-	-	
	Sep-19	449,000	-	-	-	
Production 2019 (ytd) (kWh)		3,762,000	3,921,585	1,952,111	1,969,474	
Total Production (kWh)*		-	-	-	-	
Capacity Factor*		-		*Value calculated over the last 12 months		

B. Site Energy Production Graph

May-2019

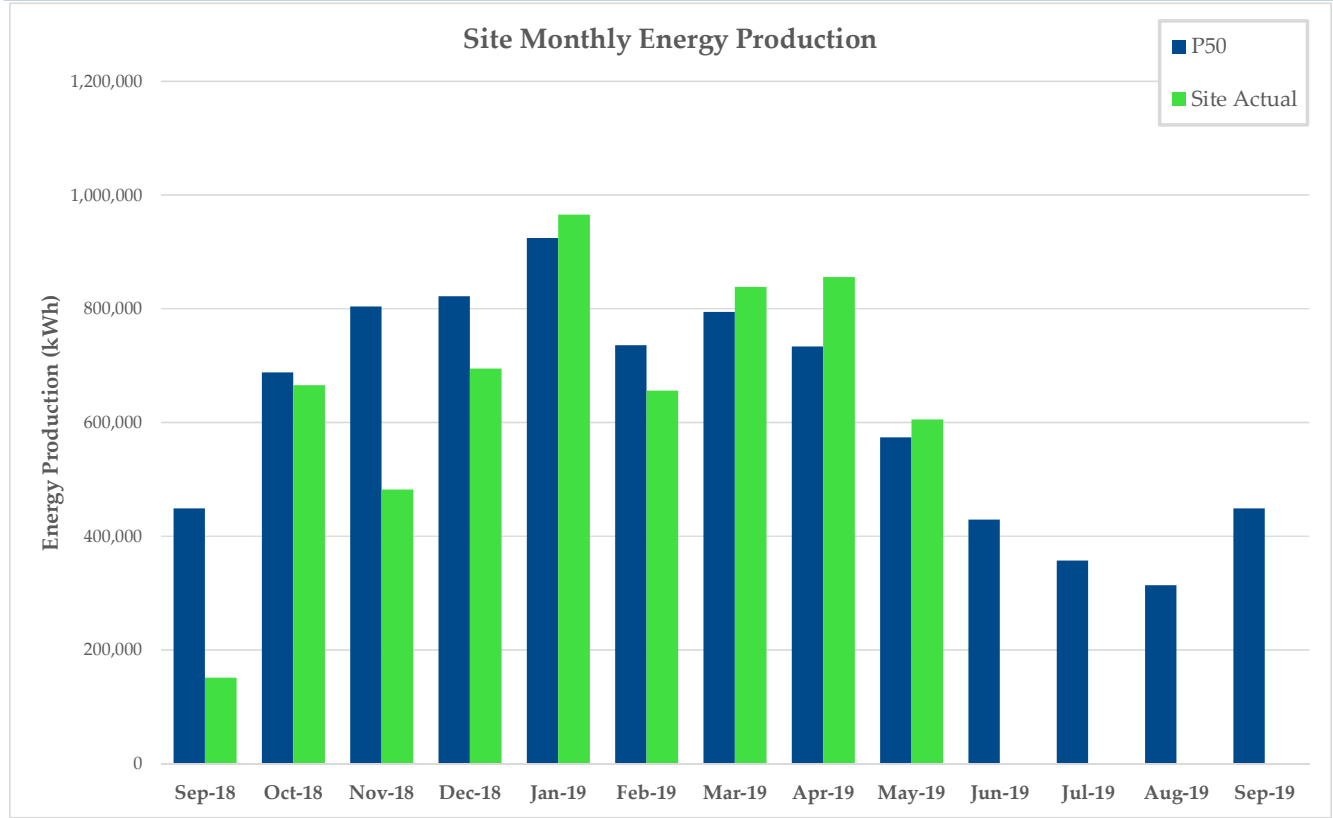

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
June-19	Goldwind 6 Month Maintenance	~8	V1
June-19	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/13/2019	Grid Fault	Unplanned	5.50	V1, V2
5/14/2019	Grid Fault	Unplanned	9.54	V1
5/14/2019	Grid Fault	Unplanned	9.93	V2
5/28/2019	High Wind Event	Unplanned	6.35	V1, V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.77%
V2	100.00%	100.00%
Avg	100.00%	99.88%
Downtime (hr)	This Month	Year To Date
V1	34.65	184.26
V2	35.04	152.04
Total	69.69	336.30

G. Billed Data

Meter Reading (Date/Time)	6/1/2019 12:00 AM
Meter To Date Produced	5,779,110 kWh
Meter To Date Consumed	11,573 kWh
Last Reading Produced	5,187,581 kWh
Last Reading Consumed	10,294 kWh
Billed kWh	590,250 kWh
Next Meter Reading	7/1/2019 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to June.
**Sep-18 production data read from meter. Capacity factor to be included once full year of data is available.
