


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	V1	V2	
Sep-18	449,000	151,192	-	-	**
Oct-18	688,000	665,292	327,890	337,402	
Nov-18	804,000	481,743	247,418	234,325	
Dec-18	822,000	694,925	363,901	331,024	
Jan-19	924,000	965,472	479,398	486,074	
Feb-19	736,000	656,163	327,762	328,401	
Mar-19	794,000	838,578	420,238	418,340	
Apr-19	734,000	855,698	425,093	430,605	
May-19	574,000	605,674	299,620	306,054	
Jun-19	429,000	479,262	235,381	243,881	
Jul-19	357,000	307,376	145,001	162,375	
Aug-19	314,000	369,367	181,572	187,795	
Sep-19	449,000	-	-	-	
Production 2019 (ytd) (kWh)	4,862,000	5,077,590	2,514,065	2,563,525	
Total Production (kWh)*	-	-	-	-	
Capacity Factor*	-		*Value calculated over the last 12 months		

B. Site Energy Production Graph

August-2019

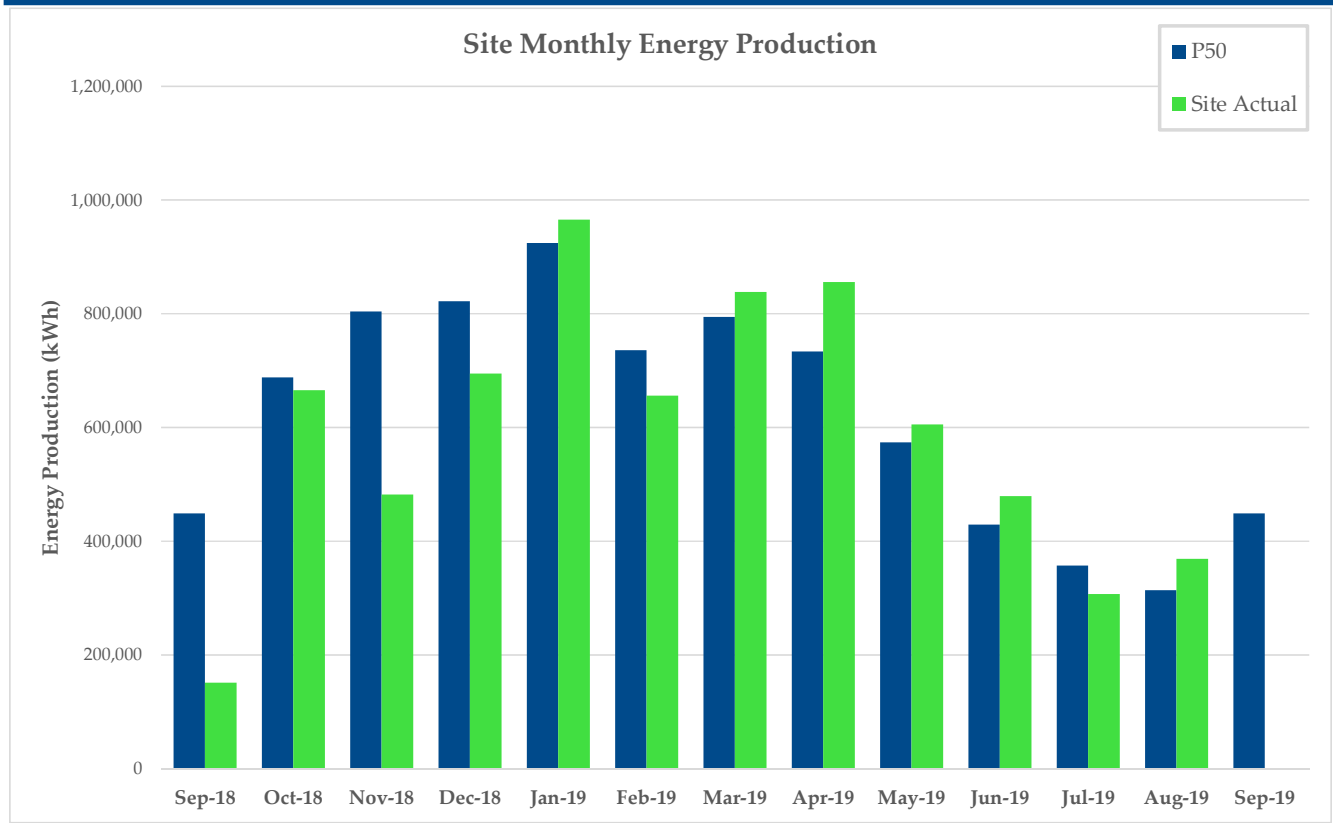

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
September-19	Goldwind 6 Month Maintenance	~8	V1
September-19	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/ Unplanned	Duration (hrs)	Turbine
8/18/2019	Weather Event	Unplanned	4.25	V1, V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.01%
V2	100.00%	100.00%
Avg	100.00%	99.51%
Downtime (hr)	This Month	Year To Date
V1	4.25	246.07
V2	4.25	161.43
Total	8.50	407.50

G. Billed Data

Meter Reading (Date/Time)	9/1/2019 12:00 AM
Meter To Date Produced	6,904,858 kWh
Meter To Date Consumed	18,013 kWh
Last Reading Produced	6,545,741 kWh
Last Reading Consumed	16,175 kWh
Billed kWh	357,279 kWh
Next Meter Reading	10/1/2019 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to September.
**Sep-18 production data read from meter.
