




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG A	WTG B	WTG C
Aug-18	577,992	610,690	217,500	193,470	199,720
Sep-18	631,697	754,220	249,590	254,010	250,620
Oct-18	1,003,602	1,199,060	420,610	355,340	423,110
Nov-18	1,395,914	1,126,610	386,320	352,100	388,190
Dec-18	1,278,858	1,203,370	406,960	390,900	405,510
Jan-19	1,332,437	1,549,490	530,840	514,790	503,860
Feb-19	1,157,019	1,189,460	406,280	396,000	387,180
Mar-19	1,242,761	1,352,210	484,800	453,230	414,180
Apr-19	1,447,248	1,456,800	503,290	479,380	474,130
May-19	1,010,966	1,102,180	380,120	364,910	357,150
Jun-19	668,411	934,460	320,720	307,820	305,920
Jul-19	638,097	575,390	191,700	191,910	191,780
Aug-19	577,992	634,650	218,690	210,230	205,730
Production 2019 (ytd) (kWh)	8,074,929	8,794,640	3,036,440	2,918,270	2,839,930
Total Production (kWh)*	12,384,999	13,077,900	4,499,920	4,270,620	4,307,360
Capacity Factor*	33.18%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

August-2019

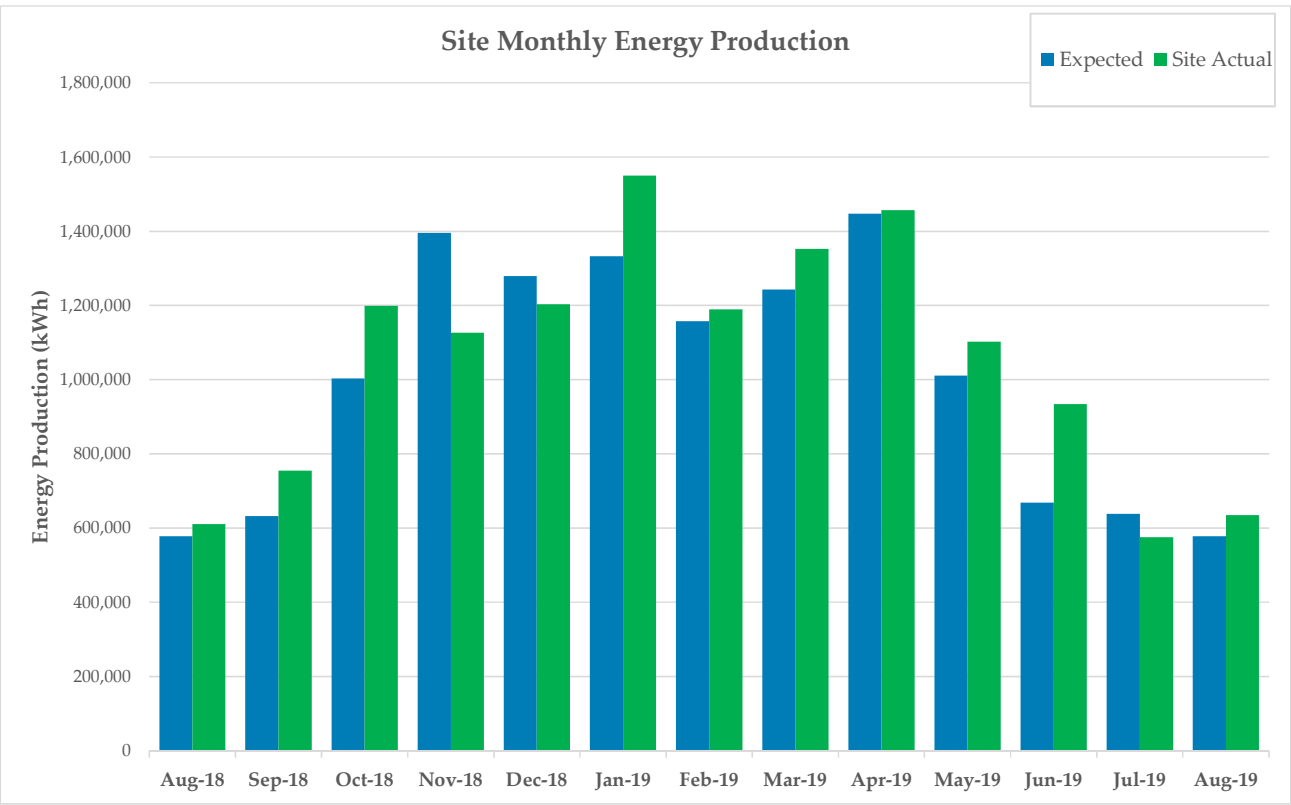

Monthly Report
August-2019



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
September-2019	Goldwind 7 Year Maintenance	~15	WTG A
September-2019	Goldwind 7 Year Maintenance	~15	WTG B
September-2019	Goldwind 7 Year Maintenance	~15	WTG C

E. Actual Maintenance Events - August 2019

Date	Event	Planned/Unplanned	Duration (hr)	Turbine
8/5/2019	Goldwind 7 Year Maintenance	Planned	7.33	WTG B
8/7/2019	Goldwind 7 Year Maintenance	Planned	6.84	WTG C
8/20/2019	Yaw Position Error	Unplanned	5.24	WTG B
8/22/2019	Pitch Capacitor Error	Unplanned	10.96	WTG C
8/27/2019	Goldwind 7 Year Maintenance	Planned	6.96	WTG A
8/28/2019	Goldwind 7 Year Maintenance	Planned	2.45	WTG A
8/30/2019	Goldwind 7 Year Maintenance	Planned	5.31	WTG B

F. Turbine Availability & Downtime

Availability (%)	This Month	Year to Date
WTG A	100.00%	99.83%
WTG B	99.30%	99.78%
WTG C	98.53%	99.31%
Avg	99.27%	99.64%

Downtime (hr)	This Month	Year to Date
WTG A	12.80	175.91
WTG B	21.27	135.41
WTG C	21.19	196.37
Total	55.26	507.69

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2019 Annual
WTG A	9.70	12.19
WTG B	9.78	12.21
WTG C	10.37	12.96
Estimated	11.09	13.39

Capacity Factor (%)	This Month	2019 Annual
WTG A	19.60%	34.71%
WTG B	18.84%	33.36%
WTG C	18.43%	32.46%
Low Estimate	14.90%	33.51%

H. Report Notes and Comments

*WTG C total production includes estimated production for April 1-7 due to meter malfunction.
**Goldwind 7 Year Maintenance to continue in September.
