



BALL CORPORATION - ZEPHYR WIND PROJECT


North Findlay Wind Campus, Findlay, OH

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Oct-18	966,000	1,026,498	357,069	338,941	330,488
Nov-18	1,262,000	931,705	303,735	310,115	317,855
Dec-18	1,524,000	1,090,402	371,241	361,728	357,433
Jan-19	1,291,000	1,404,829	478,894	461,547	464,388
Feb-19	1,355,000	990,378	351,191	338,149	301,038
Mar-19	1,197,000	1,205,738	426,173	396,015	383,550
Apr-19	1,415,000	1,258,163	431,314	415,843	411,006
May-19	900,000	674,985	237,304	222,891	214,790
Jun-19	628,000	682,994	232,437	224,872	225,685
Jul-19	571,000	469,744	167,832	151,963	149,949
Aug-19	598,000	513,686	177,673	167,452	168,561
Sep-19	515,000	585,768	205,203	193,838	186,727
Oct-19	966,000	1,039,656	350,721	348,791	340,144
Production 2019 (ytd) (kWh)	9,436,000	8,825,941	3,058,742	2,921,361	2,845,838
Total Production (kWh)*	12,222,000	10,848,048	3,733,718	3,593,204	3,521,126
Capacity Factor*	27.52%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

October-2019

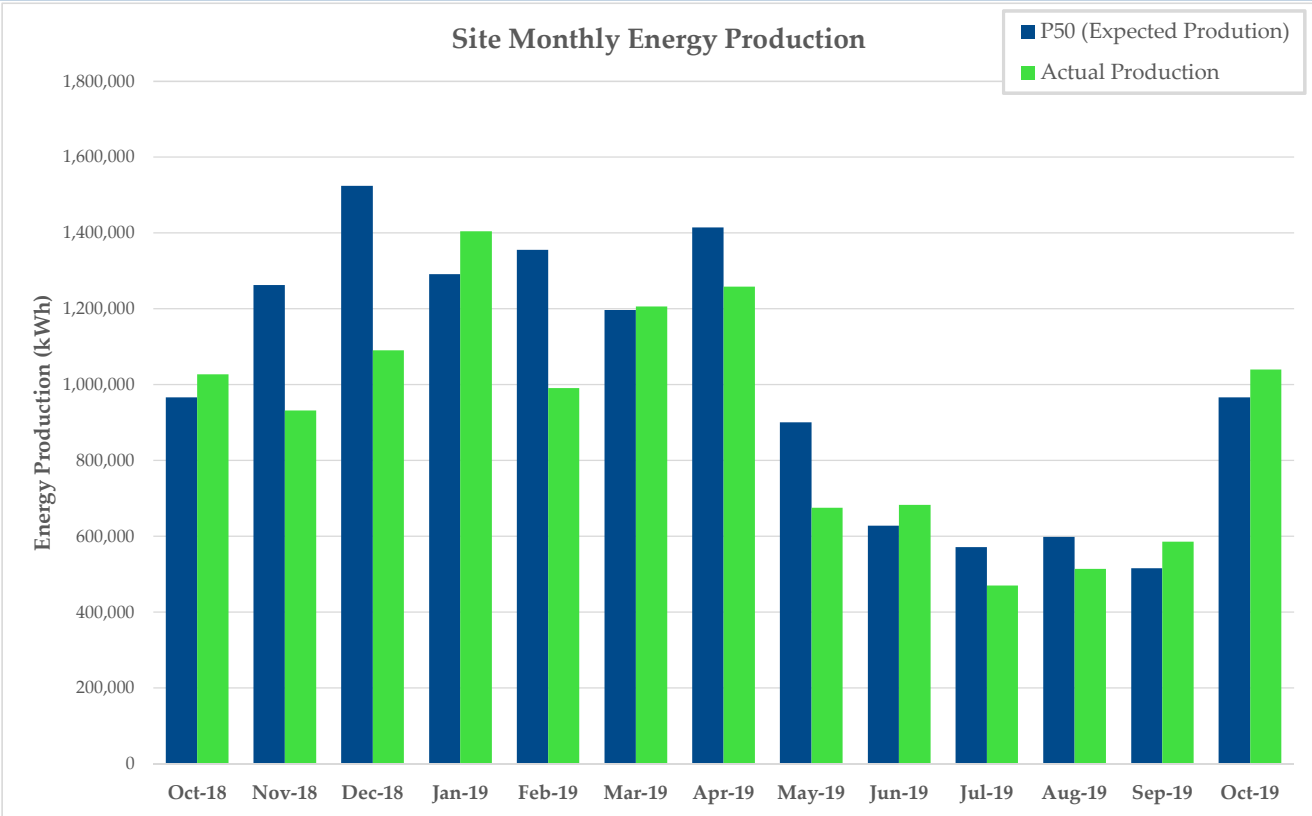

Monthly Report October-2019



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2020	Goldwind 4 Year Maintenance	~15	Z1
April-2020	Goldwind 4 Year Maintenance	~15	Z2
April-2020	Goldwind 4 Year Maintenance	~15	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/2/2019	Relay Test	Unplanned	5.86	Z1, Z2, Z3
10/29/2019	Anchor Bolt Tensioning	Unplanned	7.14	Z1, Z2
10/29/2019	Anchor Bolt Tensioning	Unplanned	7.17	Z3

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z1	100.00%	100.00%
Z2	100.00%	99.98%
Z3	100.00%	98.89%
Avg	100.00%	99.62%

Downtime (hr)	This Month	Year To Date
Z1	15.55	332.86
Z2	15.55	335.30
Z3	15.58	420.39
Total	46.68	1088.55

G. Billed Data

Meter Reading (Date/Time)	10/17/2019 12:00 AM
Meter To Date Produced	40,565,595 kWh
Meter To Date Consumed	51,897 kWh
Last Reading Produced	39,744,328 kWh
Last Reading Consumed	51,173 kWh
Billed kWh	820,543 kWh
Next Meter Reading	11/15/2019 12:00 AM

H. Report Notes and Comments

*Z3 production total for May and June 2019 is an estimate due to loss of communications.
