


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Oct-18	688,000	665,292	327,890	337,402
Nov-18	804,000	481,743	247,418	234,325
Dec-18	822,000	694,925	363,901	331,024
Jan-19	924,000	965,472	479,398	486,074
Feb-19	736,000	656,163	327,762	328,401
Mar-19	794,000	838,578	420,238	418,340
Apr-19	734,000	855,698	425,093	430,605
May-19	574,000	605,674	299,620	306,054
Jun-19	429,000	479,262	235,381	243,881
Jul-19	357,000	307,376	145,001	162,375
Aug-19	314,000	369,367	181,572	187,795
Sep-19	449,000	392,366	197,834	194,532
Oct-19	688,000	676,972	338,413	338,559
Production 2019 (ytd) (kWh)	5,999,000	6,146,928	3,050,312	3,096,616
Total Production (kWh)*	7,625,000	7,323,596	3,661,631	3,661,965
Capacity Factor*	27.87%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

October-2019

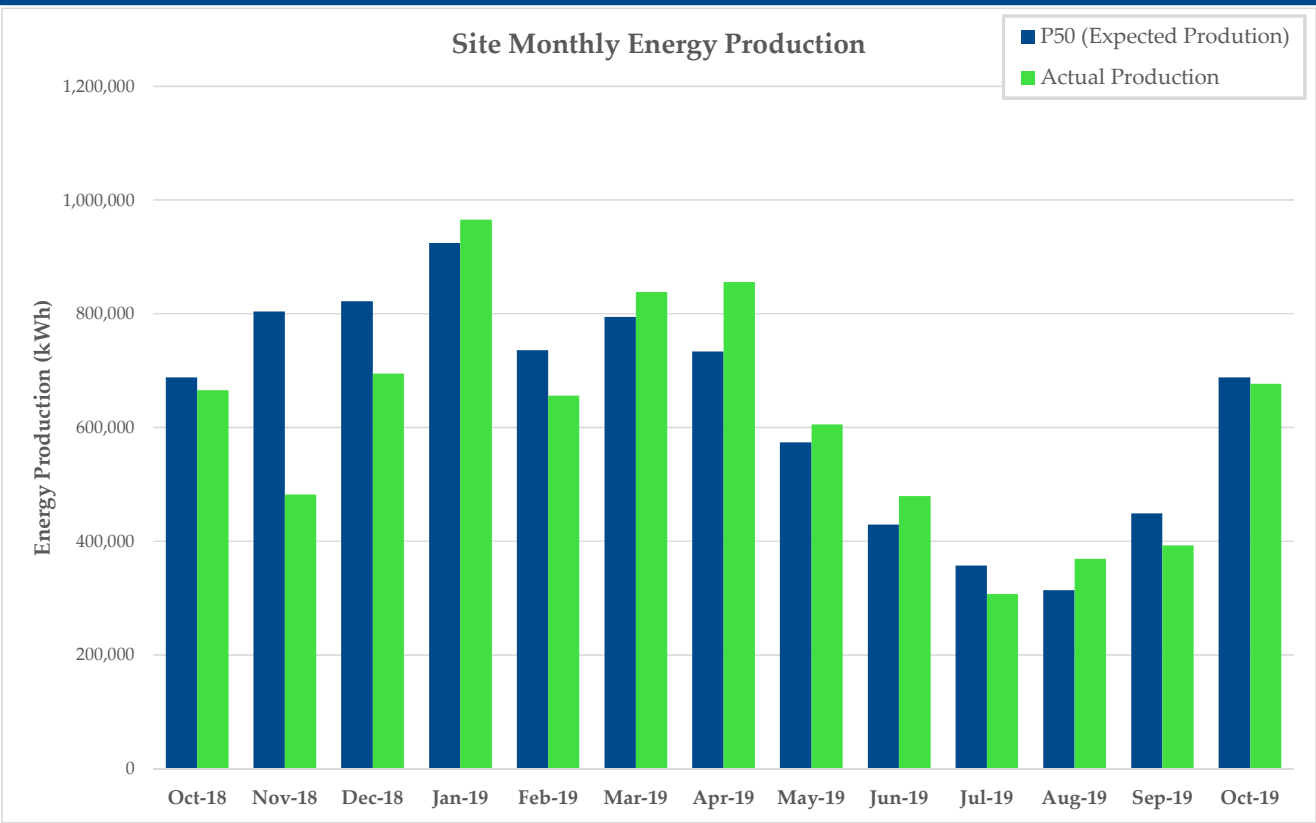

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-19	Goldwind 6 Month Maintenance	~8	V1
November-19	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/10/2019	Plant Transformer Event	Unplanned	8.30	V1, V2
10/11/2019	Pitch Fault	Unplanned	6.74	V1
10/11/2019	Pitch Fault	Unplanned	9.55	V2
10/30/2019	Plant Shutdown	Unplanned	13.18	V1, V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.22%
V2	100.00%	100.00%
Avg	100.00%	99.61%

Downtime (hr)	This Month	Year To Date
V1	33.98	298.92
V2	35.88	217.29
Total	69.86	516.21

G. Billed Data

Meter Reading (Date/Time)	11/1/2019 12:00 AM
Meter To Date Produced	7,945,536 kWh
Meter To Date Consumed	21,016 kWh
Last Reading Produced	7,286,590 kWh
Last Reading Consumed	19,656 kWh
Billed kWh	657,586 kWh
Next Meter Reading	12/1/2019 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to November.
