


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Oct-18	649,000	709,011	359,965	349,046
Nov-18	846,000	616,294	307,095	309,199
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Apr-19	949,000	852,957	427,080	425,877
May-19	603,000	615,463	306,237	309,226
Jun-19	422,000	474,817	240,372	234,445
Jul-19	383,000	338,373	171,861	166,512
Aug-19	402,000	355,979	180,172	175,807
Sep-19	346,000	403,384	203,853	199,531
Oct-19	649,000	709,389	354,865	354,524
Production 2019 (ytd) (kWh)	6,332,000	6,249,425	3,162,919	3,086,506
Total Production (kWh)*	8,200,000	7,602,761	3,846,413	3,756,348
Capacity Factor*	28.93%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

October-2019

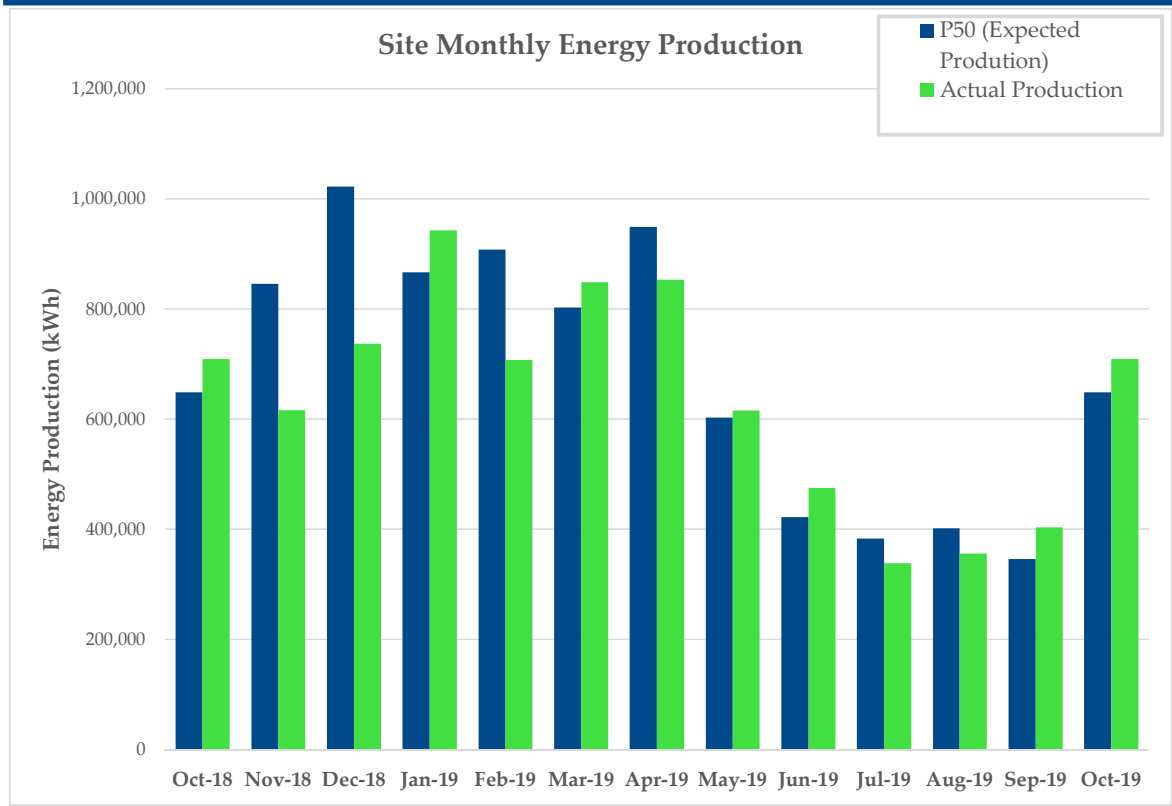

Monthly Report
October-2019

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
November-2019	Goldwind 4 Year Maintenance	~15	W1
November-2019	Goldwind 4 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/8/2019	Basement Maintenance	Unplanned	8.59	W1, W2
10/28/2019	Owner/Operator Maintenance	Unplanned	7.86	W1
10/28/2019	Owner/Operator Maintenance	Unplanned	7.84	W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.80%
W2	100.00%	99.61%
Avg	100.00%	99.70%

Downtime (hr)	This Month	Year To Date
W1	21.39	203.38
W2	20.91	196.34
Total	42.30	399.72

G. Billed Data

Meter Reading (Date/Time)	10/29/2019 12:00 AM
Meter To Date Produced	28,963,235 kWh
Meter To Date Consumed	59,531 kWh
Last Reading Produced	28,305,819 kWh
Last Reading Consumed	58,698 kWh
Billed kWh	656,583 kWh
Next Meter Reading	11/29/2019 12:00 AM

H. Report Notes and Comments

*Goldwind 4 Year Maintenance to continue into November.
