


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Nov-18	804,000	481,743	247,418	234,325
Dec-18	822,000	694,925	363,901	331,024
Jan-19	924,000	965,472	479,398	486,074
Feb-19	736,000	656,163	327,762	328,401
Mar-19	794,000	838,578	420,238	418,340
Apr-19	734,000	855,698	425,093	430,605
May-19	574,000	605,674	299,620	306,054
Jun-19	429,000	479,262	235,381	243,881
Jul-19	357,000	307,376	145,001	162,375
Aug-19	314,000	369,367	181,572	187,795
Sep-19	449,000	392,366	197,834	194,532
Oct-19	688,000	676,972	338,413	338,559
Nov-19	804,000	631,219	315,003	316,216
Production 2019 (ytd) (kWh)	6,803,000	6,778,147	3,365,315	3,412,832
Total Production (kWh)*	7,625,000	7,473,072	3,729,216	3,743,856
Capacity Factor*	28.44%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

November-2019

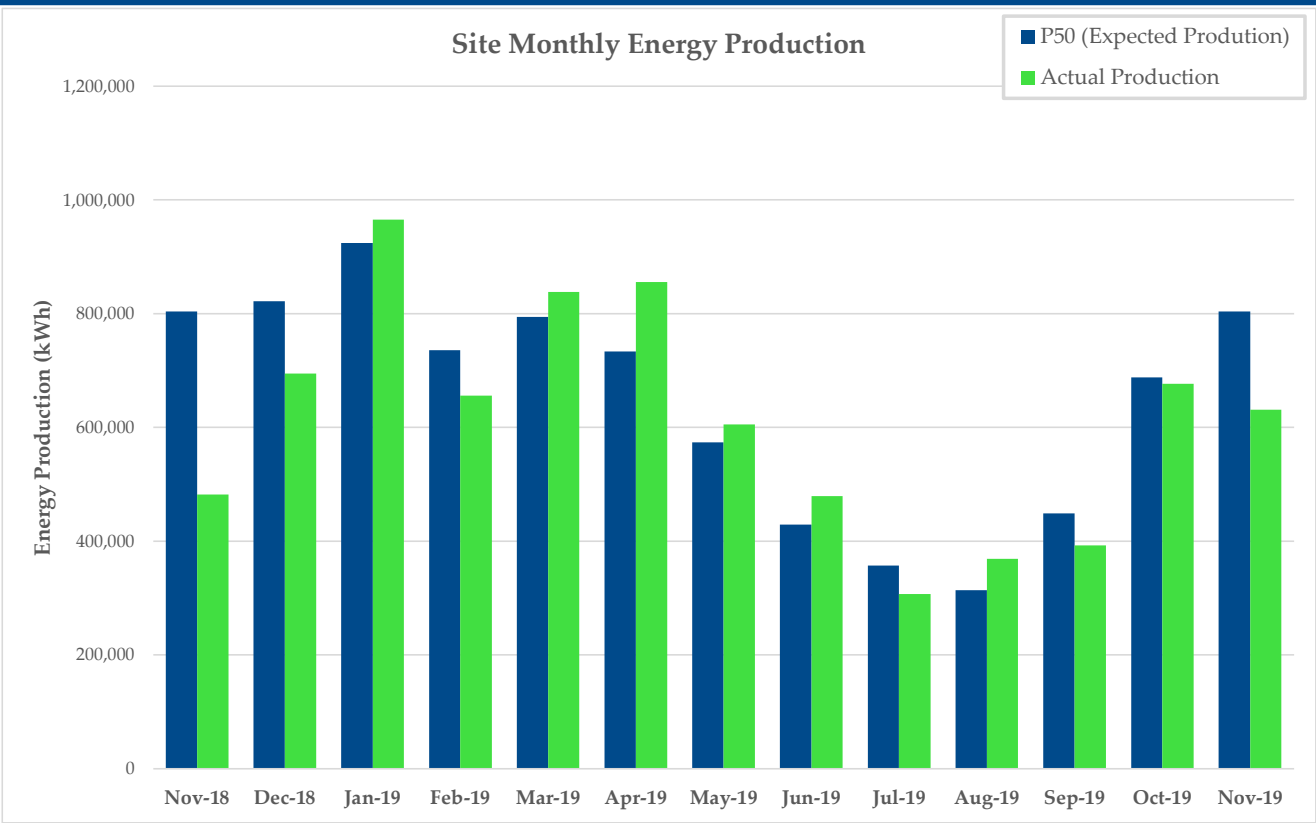

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
December-19	Goldwind 6 Month Maintenance	~8	V1
December-19	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/27/2019	High Wind Event	Unplanned	8.80	V1, V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.29%
V2	100.00%	100.00%
Avg	100.00%	99.65%

Downtime (hr)	This Month	Year To Date
V1	18.05	316.97
V2	18.05	235.34
Total	36.10	552.31

G. Billed Data

Meter Reading (Date/Time)	12/1/2019 12:00 AM
Meter To Date Produced	8,564,261 kWh
Meter To Date Consumed	22,616 kWh
Last Reading Produced	7,945,536 kWh
Last Reading Consumed	21,016 kWh
Billed kWh	617,126 kWh
Next Meter Reading	1/1/2020 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to December
