


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Nov-18	846,000	616,294	307,095	309,199
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Apr-19	949,000	852,957	427,080	425,877
May-19	603,000	615,463	306,237	309,226
Jun-19	422,000	474,817	240,372	234,445
Jul-19	383,000	338,373	171,861	166,512
Aug-19	402,000	355,979	180,172	175,807
Sep-19	346,000	403,384	203,853	199,531
Oct-19	649,000	709,389	354,865	354,524
Nov-19	846,000	669,872	338,584	331,288
Production 2019 (ytd) (kWh)	7,178,000	6,919,297	3,501,503	3,417,794
Total Production (kWh)*	8,200,000	7,656,339	3,877,902	3,778,437
Capacity Factor*	29.13%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

November-2019

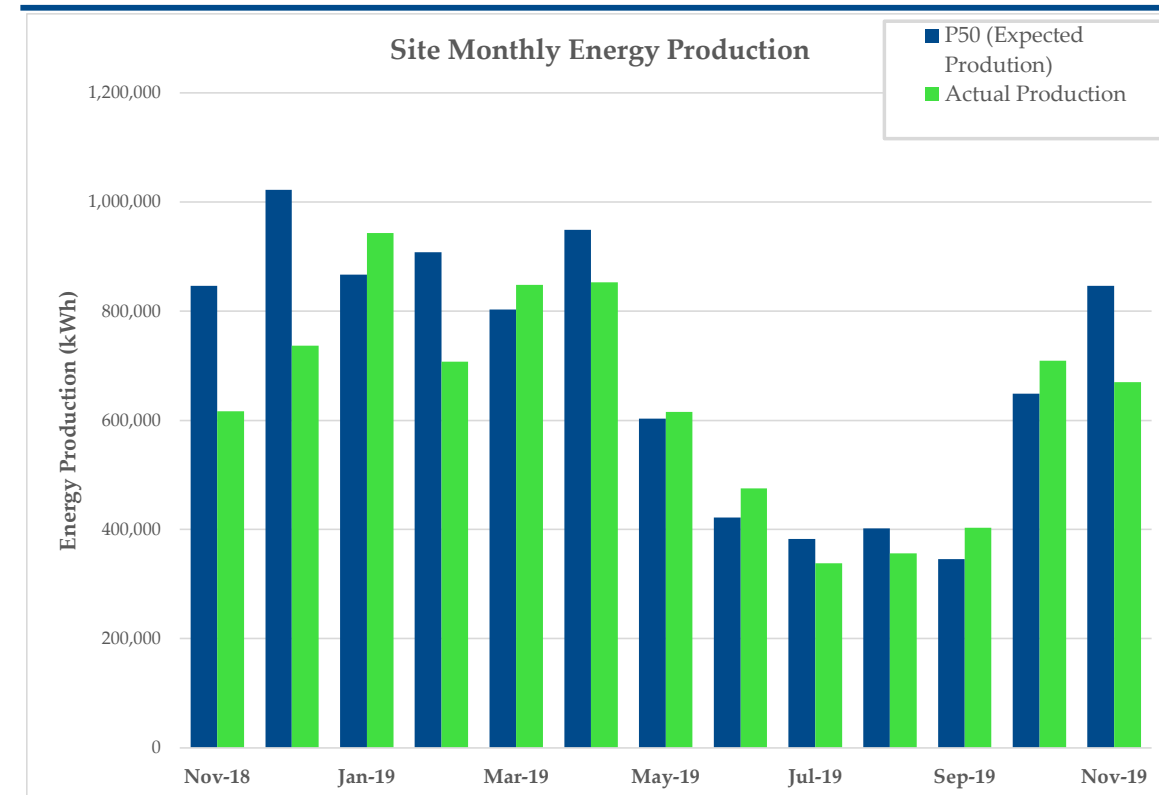

Monthly Report

November-2019

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2020	Goldwind 4.5 Year Maintenance	~8	W1
May-2020	Goldwind 4.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/13/2019	Goldwind 4 Year Maintenance	Planned	6.95	W1
11/14/2019	Goldwind 4 Year Maintenance	Planned	7.04	W2
11/18/2019	Goldwind 4 Year Maintenance	Planned	2.92	W1, W2
11/27/2019	High Wind Event	Unplanned	8.80	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.84%	99.81%
W2	100.00%	99.64%
Avg	99.92%	99.72%

Downtime (hr)	This Month	Year To Date
W1	19.81	223.19
W2	18.76	215.10
Total	38.57	438.29

G. Billed Data

Meter Reading (Date/Time)	11/29/2019 12:00 AM
Meter To Date Produced	29,664,726 kWh
Meter To Date Consumed	60,815 kWh
Last Reading Produced	28,963,235 kWh
Last Reading Consumed	59,531 kWh
Billed kWh	700,207 kWh
Next Meter Reading	12/29/2019 12:00 AM

H. Report Notes and Comments
