


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Nov-18	440,000	347,233
Dec-18	532,000	384,067
Jan-19	450,000	424,745
Feb-19	473,000	354,625
Mar-19	417,000	450,944
Apr-19	494,000	450,366
May-19	315,000	335,596
Jun-19	220,000	276,978
Jul-19	199,000	166,408
Aug-19	209,000	188,300
Sep-19	180,000	205,853
Oct-19	337,000	395,663
Nov-19	440,000	329,892
Production 2019 (ytd) (kWh)	3,734,000	3,579,370
Total Production (kWh)*	4,266,000	3,963,437
Capacity Factor*	30.16%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

November-2019

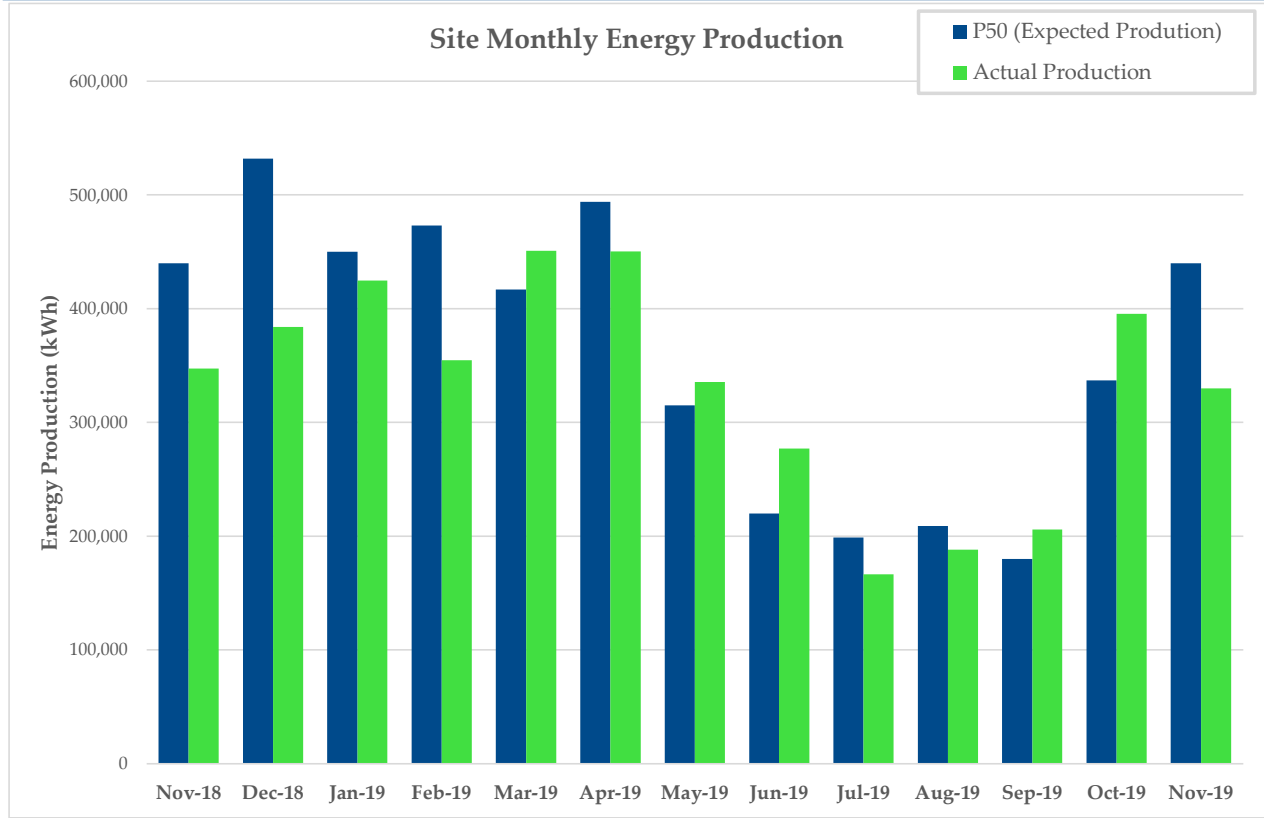

Monthly Report
November-2019

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2020	Goldwind 2 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/11-13/2019	Icing Event	Unplanned	47.67	W1
11/27/2019	High Wind Event	Unplanned	8.78	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.63%

Downtime (hr)	This Month	Year To Date
W1	56.45	316.54

G. Billed Data

Meter Reading (Date/Time)	12/1/2019 12:00 AM
Meter To Date Produced	6,849,568 kWh
Meter To Date Consumed	38,208 kWh
Last Reading Produced	6,523,943 kWh
Last Reading Consumed	36,501 kWh
Billed kWh	323,918 kWh
Next Meter Reading	1/1/2020 12:00 AM

H. Report Notes and Comments
