


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Dec-18	1,022,000	737,042	376,399	360,643
Jan-19	867,000	942,829	486,578	456,251
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Apr-19	949,000	852,957	427,080	425,877
May-19	603,000	615,463	306,237	309,226
Jun-19	422,000	474,817	240,372	234,445
Jul-19	383,000	338,373	171,861	166,512
Aug-19	402,000	355,979	180,172	175,807
Sep-19	346,000	403,384	203,853	199,531
Oct-19	649,000	709,389	354,865	354,524
Nov-19	846,000	669,872	338,584	331,288
Dec-19	1,022,000	943,766	481,616	462,150
Production 2019 (ytd) (kWh)	8,200,000	7,863,063	3,983,119	3,879,944
Total Production (kWh)*	8,200,000	7,863,063	3,983,119	3,879,944
Capacity Factor*	29.92% *Value calculated over the last 12 months			

B. Site Energy Production Graph

December-2019

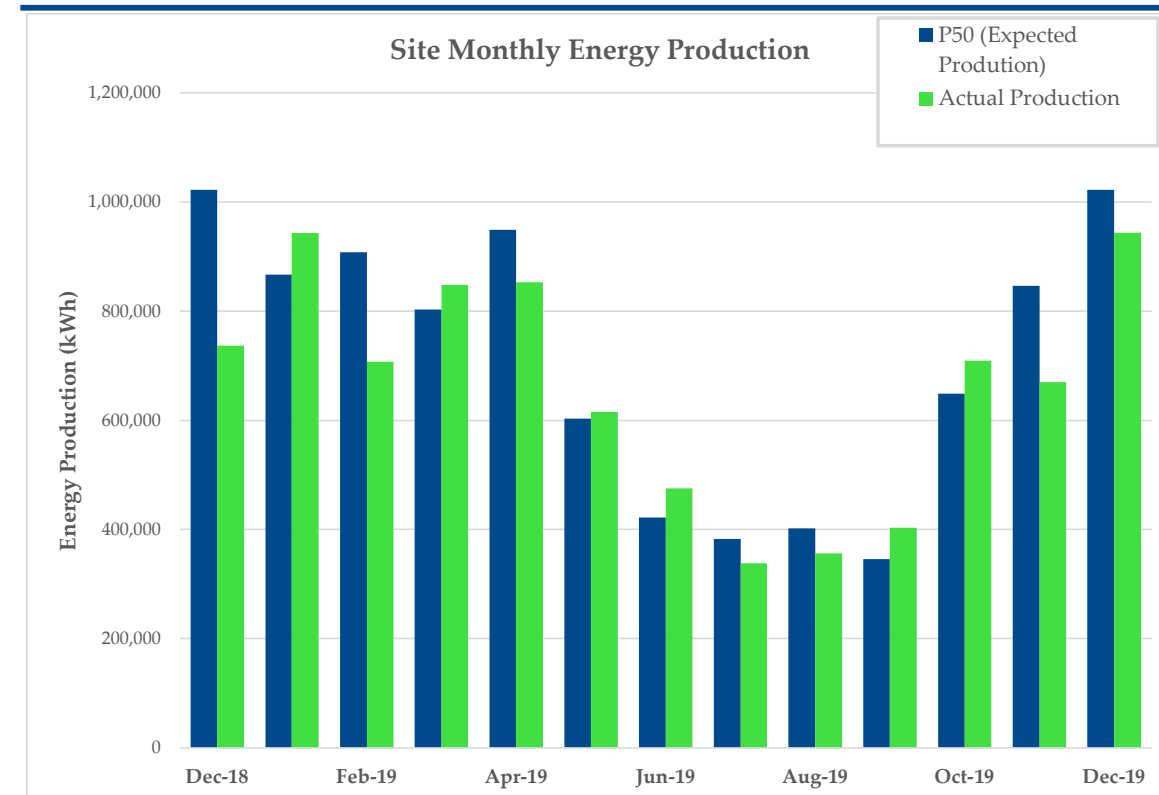

Monthly Report December-2019

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2020	Goldwind 4.5 Year Maintenance	~8	W1
May-2020	Goldwind 4.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
12/31/2019	Grid Fault	Unplanned	4.88	W1, W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.82%
W2	100.00%	99.67%
Avg	100.00%	99.75%

Downtime (hr)	This Month	Year To Date
W1	5.62	228.81
W2	5.66	220.76
Total	11.28	449.57

G. Billed Data

Meter Reading (Date/Time)	12/29/2019 12:00 AM
Meter To Date Produced	30,488,484 kWh
Meter To Date Consumed	61,750 kWh
Last Reading Produced	29,664,726 kWh
Last Reading Consumed	60,815 kWh
Billed kWh	822,823 kWh
Next Meter Reading	1/29/2020 12:00 AM

H. Report Notes and Comments
