



BALL CORPORATION - ZEPHYR WIND PROJECT


North Findlay Wind Campus, Findlay, OH

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Jan-19	1,291,000	1,404,829	478,894	461,547	464,388
Feb-19	1,355,000	990,378	351,191	338,149	301,038
Mar-19	1,197,000	1,205,738	426,173	396,015	383,550
Apr-19	1,415,000	1,258,163	431,314	415,843	411,006
May-19	900,000	674,985	237,304	222,891	214,790
Jun-19	628,000	682,994	232,437	224,872	225,685
Jul-19	571,000	469,744	167,832	151,963	149,949
Aug-19	598,000	513,686	177,673	167,452	168,561
Sep-19	515,000	585,768	205,203	193,838	186,727
Oct-19	966,000	1,039,656	350,721	348,791	340,144
Nov-19	1,262,000	889,667	312,289	296,145	281,233
Dec-19	1,524,000	1,392,651	483,293	460,120	449,238
Jan-20	1,291,000	1,187,158	410,228	396,206	380,724
Production 2020 (ytd) (kWh)	1,291,000	1,187,158	410,228	396,206	380,724
Total Production (kWh)*	12,222,000	10,890,588	3,785,658	3,612,285	3,492,645
Capacity Factor*	27.63%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

January-2020

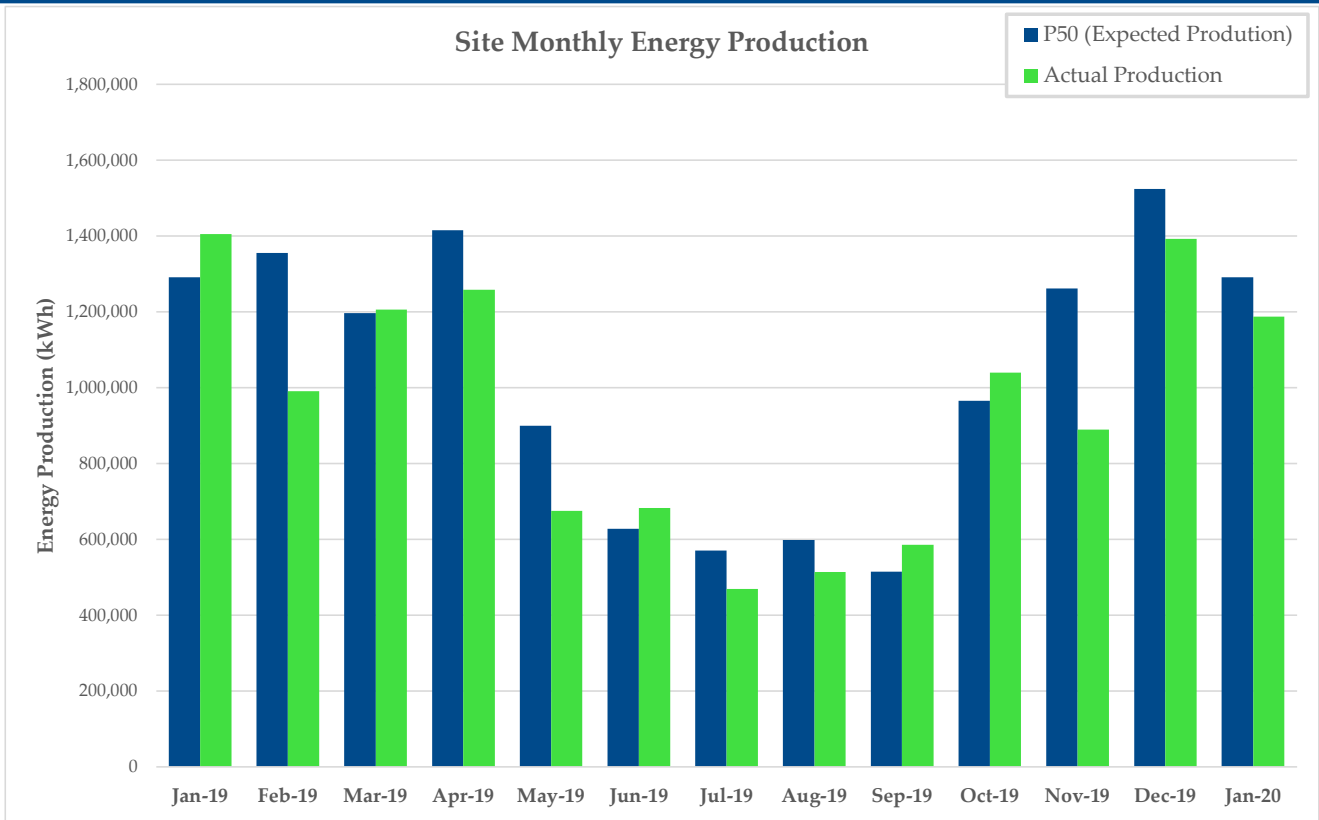

Monthly Report

January-2020



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2020	Goldwind 4 Year Maintenance	~15	Z1
April-2020	Goldwind 4 Year Maintenance	~15	Z2
April-2020	Goldwind 4 Year Maintenance	~15	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/11-12/2020	High Wind Event	Unplanned	4.45	Z 1, 2, 3
1/18/2020	Icing Event	Unplanned	7.12	Z3
1/26-27/2020	Device Break	Unplanned	6.90	Z1
1/28/2020	Anchor Bolt Retensioning	Unplanned	7.59	Z1
1/28/2020	Anchor Bolt Retensioning	Unplanned	7.53	Z 2, 3
1/31/2020	Anchor Bolt Retensioning	Unplanned	5.17	Z3

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z1	99.06%	99.06%
Z2	99.96%	99.96%
Z3	100.00%	100.00%
Avg	99.67%	99.67%

Downtime (hr)	This Month	Year To Date
Z1	20.67	20.67
Z2	16.55	16.55
Z3	25.55	25.55
Total	62.77	62.77

G. Billed Data

Meter Reading (Date/Time)	1/21/2020 12:00 AM
Meter To Date Produced	44,244,808 kWh
Meter To Date Consumed	55,061 kWh
Last Reading Produced	42,690,058 kWh
Last Reading Consumed	54,279 kWh
Billed kWh	1,553,968 kWh
Next Meter Reading	2/19/2020 12:00 AM

H. Report Notes and Comments

*Z3 production total for May and June 2019 is an estimate due to loss of communications.
