


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Jan-19	924,000	965,472	479,398	486,074
Feb-19	736,000	656,163	327,762	328,401
Mar-19	794,000	838,578	420,238	418,340
Apr-19	734,000	855,698	425,093	430,605
May-19	574,000	605,674	299,620	306,054
Jun-19	429,000	479,262	235,381	243,881
Jul-19	357,000	307,376	145,001	162,375
Aug-19	314,000	369,367	181,572	187,795
Sep-19	449,000	392,366	197,834	194,532
Oct-19	688,000	676,972	338,413	338,559
Nov-19	804,000	631,219	315,003	316,216
Dec-19	822,000	904,108	456,015	448,093
Jan-20	924,000	772,641	385,505	387,136
Production 2020 (ytd) (kWh)	924,000	772,641	385,505	387,136
Total Production (kWh)*	7,625,000	7,489,424	3,727,437	3,761,987
Capacity Factor*	28.50%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

January-2020

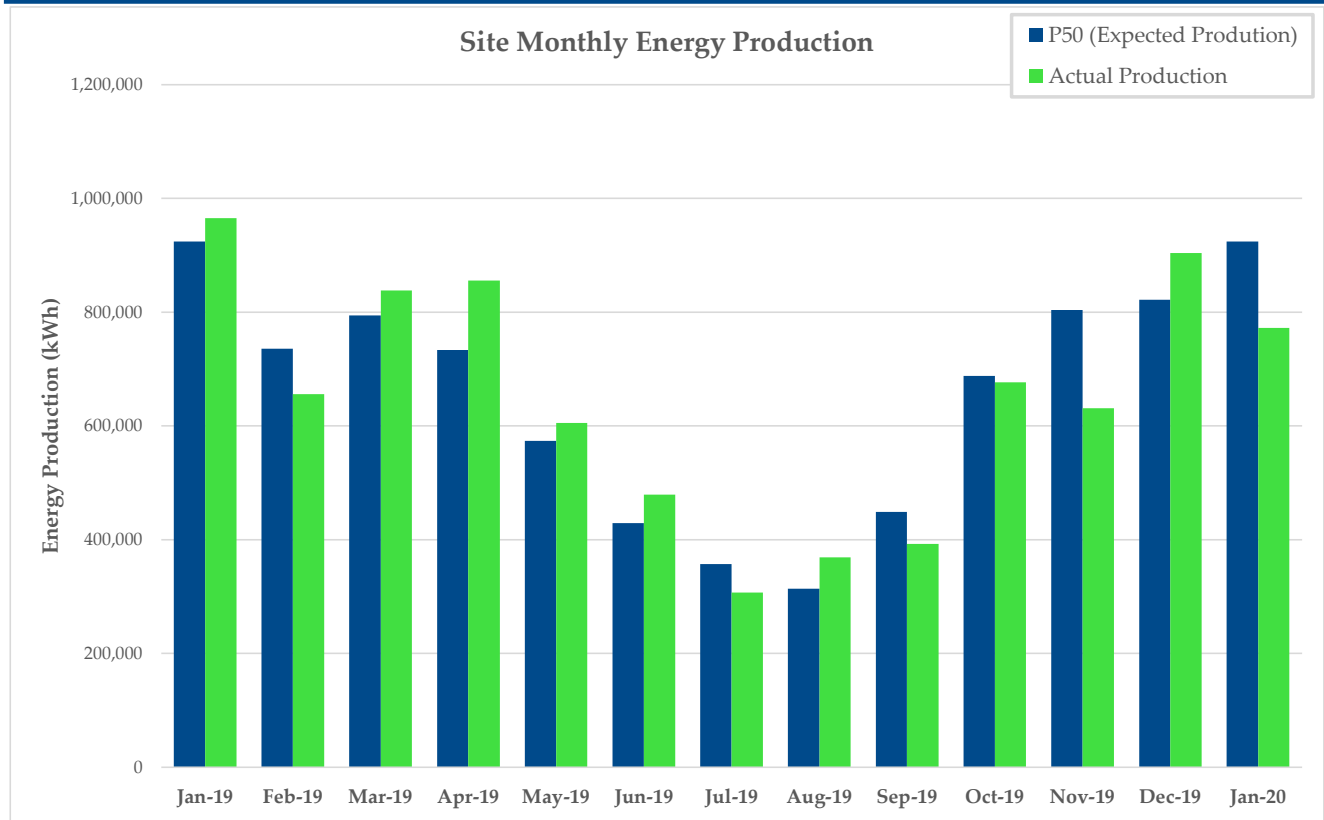

Monthly Report

January-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
February-20	Goldwind 6 Month Maintenance	~8	V1
February-20	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/11-12/2020	High Wind Event	Unplanned	4.50	V1, V2
1/18/2020	Icing Event	Unplanned	6.21	V1
1/18/2020	Icing Event	Unplanned	4.53	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
V1	11.21	11.21
V2	9.71	9.71
Total	20.92	20.92

G. Billed Data

Meter Reading (Date/Time)	2/1/2020 12:00 AM
Meter To Date Produced	10,204,855 kWh
Meter To Date Consumed	24,920 kWh
Last Reading Produced	9,447,412 kWh
Last Reading Consumed	23,552 kWh
Billed kWh	756,075 kWh
Next Meter Reading	3/1/2020 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to February.
