


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WG1	WG2	WG3
Jan-19	1,343,000	952,287	325,224	314,810	312,253
Feb-19	1,133,000	935,828	324,947	304,407	306,474
Mar-19	1,312,000	1,099,016	403,803	310,433	384,780
Apr-19	1,272,000	1,210,371	406,808	400,071	403,492
May-19	974,000	805,247	272,374	265,063	267,810
Jun-19	714,000	750,094	254,695	247,674	247,725
Jul-19	566,000	437,042	130,830	155,812	150,400
Aug-19	514,000	482,340	171,490	156,018	154,832
Sep-19	716,000	597,745	203,475	201,926	192,344
Oct-19	1,051,000	1,033,402	351,806	342,691	338,905
Nov-19	1,224,000	869,845	297,447	287,622	284,776
Dec-19	1,217,000	1,216,234	461,480	437,079	317,675
Jan-20	1,343,000	966,360	362,196	344,267	259,897
Production 2020 (ytd) (kWh)	1,343,000	966,360	362,196	344,267	259,897
Total Production (kWh)*	12,036,000	10,403,524	3,641,351	3,453,063	3,309,110
Capacity Factor*	26.39%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

January-2020

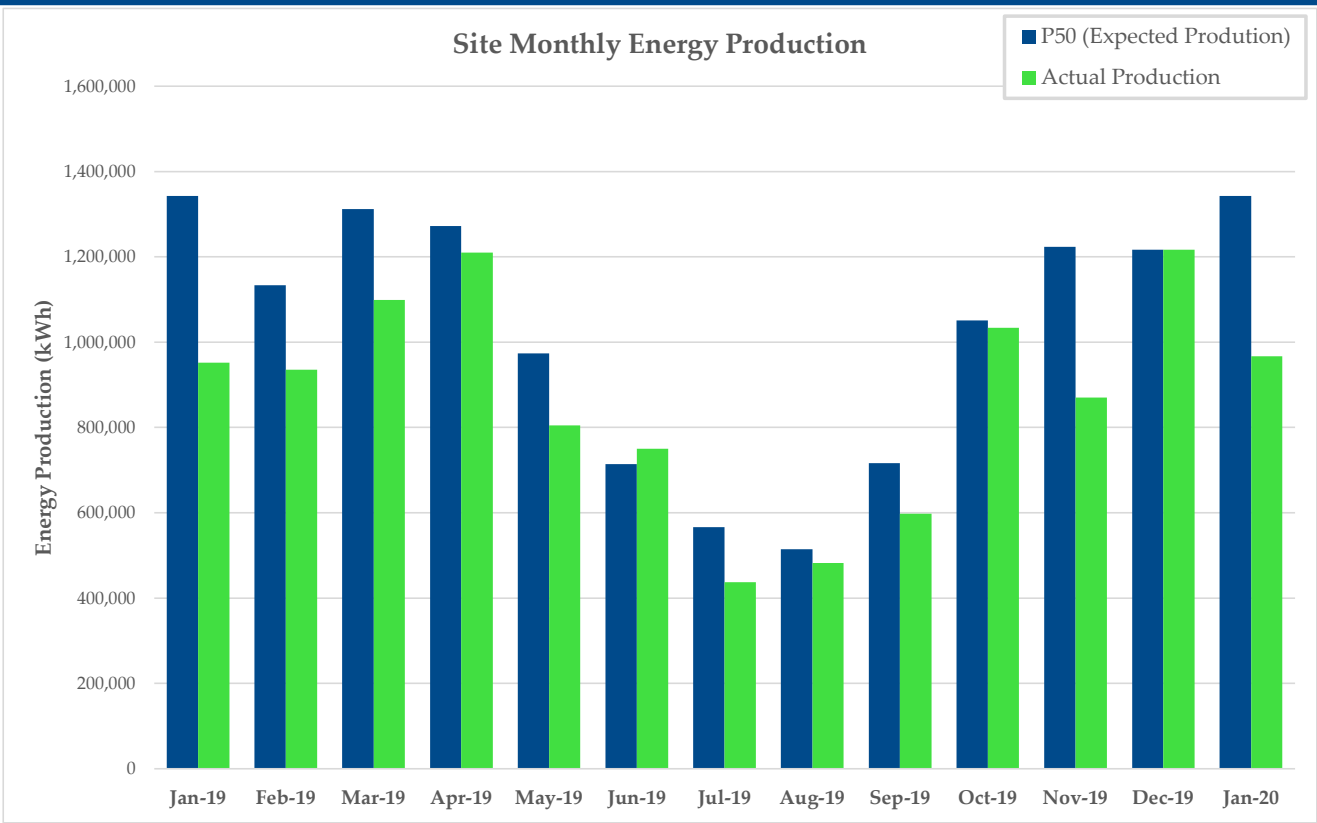

Monthly Report
January-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
February-2020	Goldwind 6 Month Maintenance	~8	WG 1
February-2020	Goldwind 6 Month Maintenance	~8	WG 2
February-2020	Goldwind 6 Month Maintenance	~8	WG 3

E. Actual Maintenance Events

Date	Event	Planned/ Unplanned	Duration (hrs)	Turbine
1/1-6/2020	Device Break	Unplanned	131.67	WG 3
1/3/2020	Anchor Bolt Tensioning, Turbine Fault	Unplanned	14.20	WG 1, 2
1/4/2020	Turbine Fault	Unplanned	7.77	WG 1
1/5/2020	Turbine Fault	Unplanned	7.69	WG 2
1/11-12/2020	High Wind Event	Unplanned	4.53	WG 1, 2, 3
1/15/2020	Icing Event	Unplanned	4.12	WG 2
1/18/2020	Icing Event	Unplanned	7.55	WG 1
1/18/2020	Icing Event	Unplanned	7.40	WG 2
1/18/2020	Icing Event	Unplanned	7.17	WG 3
1/23/2020	Nachelle Fuse Error	Unplanned	6.70	WG 3
1/26/2020	Icing Event	Unplanned	13.79	WG 1
1/26/2020	Icing Event	Unplanned	14.34	WG 2
1/26/2020	Icing Event	Unplanned	13.68	WG 3

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
WG1	100.00%	100.00%
WG2	99.97%	99.97%
WG3	81.17%	81.17%
Avg	93.71%	93.71%

Downtime (hr)	This Month	Year To Date
WG1	50.72	50.72
WG2	56.31	56.31
WG3	168.24	168.24
Total	275.27	275.27

G. Billed Data

Meter Reading (Date/Time)	1/29/2020 12:00 AM
Meter To Date Produced	13,624,490 kWh
Meter To Date Consumed	52,073 kWh
Last Reading Produced	12,524,941 kWh
Last Reading Consumed	49,213 kWh
Billed kWh	1,096,689 kWh
Next Meter Reading	2/29/2020 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to February.
**Goldwind Availability and Downtime under dispute.
***WG3 production for December 2019 and January 2020 is an estimate due to communication issue.
