


A. Site Energy Production Summary*

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Jan-19	455,000	424,745
Feb-19	478,000	354,625
Mar-19	422,000	450,944
Apr-19	499,000	450,366
May-19	318,000	335,596
Jun-19	222,000	276,978
Jul-19	201,000	166,408
Aug-19	211,000	188,300
Sep-19	182,000	205,853
Oct-19	341,000	395,663
Nov-19	445,000	329,892
Dec-19	537,000	480,035
Jan-20	455,000	427,899
Production 2020 (ytd) (kWh)	455,000	427,899
Total Production (kWh)*	4,311,000	4,062,559
Capacity Factor*	30.92%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

January-2020

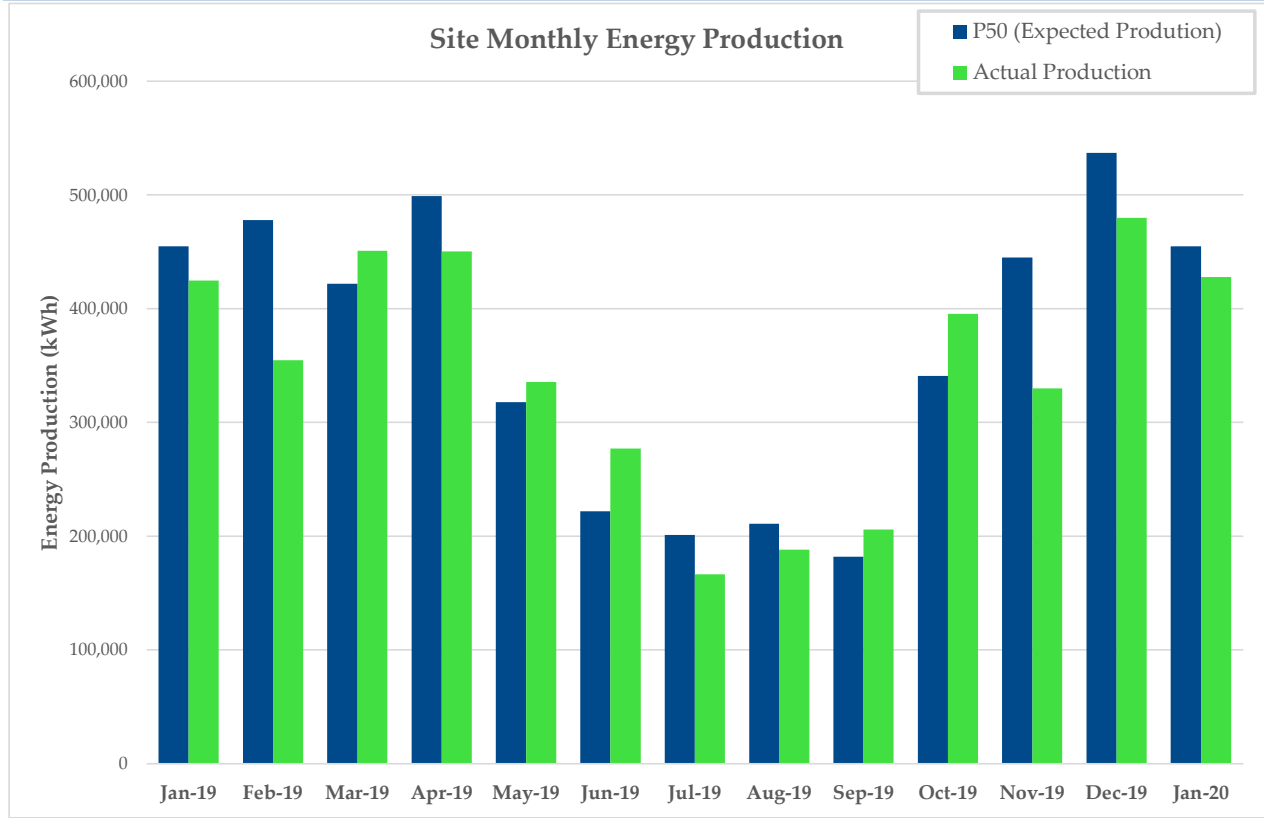

Monthly Report

January-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2020	Goldwind 2 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/11-12/2020	High Wind Event	Unplanned	4.46	W1
1/18/2020	Icing Event	Unplanned	6.80	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
W1	13.57	13.57

G. Billed Data

Meter Reading (Date/Time)	2/1/2020 12:00 AM
Meter To Date Produced	7,745,695 kWh
Meter To Date Consumed	40,212 kWh
Last Reading Produced	7,323,655 kWh
Last Reading Consumed	39,016 kWh
Billed kWh	420,844 kWh
Next Meter Reading	3/1/2020 12:00 AM

H. Report Notes and Comments

*An error in the source file for the project P50 was found and corrected, leading to the change in reported P50 production.
