


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Feb-19	908,000	707,729	356,127	351,602
Mar-19	803,000	848,505	435,774	412,731
Apr-19	949,000	852,957	427,080	425,877
May-19	603,000	615,463	306,237	309,226
Jun-19	422,000	474,817	240,372	234,445
Jul-19	383,000	338,373	171,861	166,512
Aug-19	402,000	355,979	180,172	175,807
Sep-19	346,000	403,384	203,853	199,531
Oct-19	649,000	709,389	354,865	354,524
Nov-19	846,000	669,872	338,584	331,288
Dec-19	1,022,000	943,766	481,616	462,150
Jan-20	867,000	820,679	407,059	413,620
Feb-20	908,000	670,274	317,389	352,885
Production 2020 (ytd) (kWh)	1,775,000	1,490,953	724,448	766,505
Total Production (kWh)*	8,200,000	7,703,458	3,864,862	3,838,596
Capacity Factor*	29.23%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

February-2020

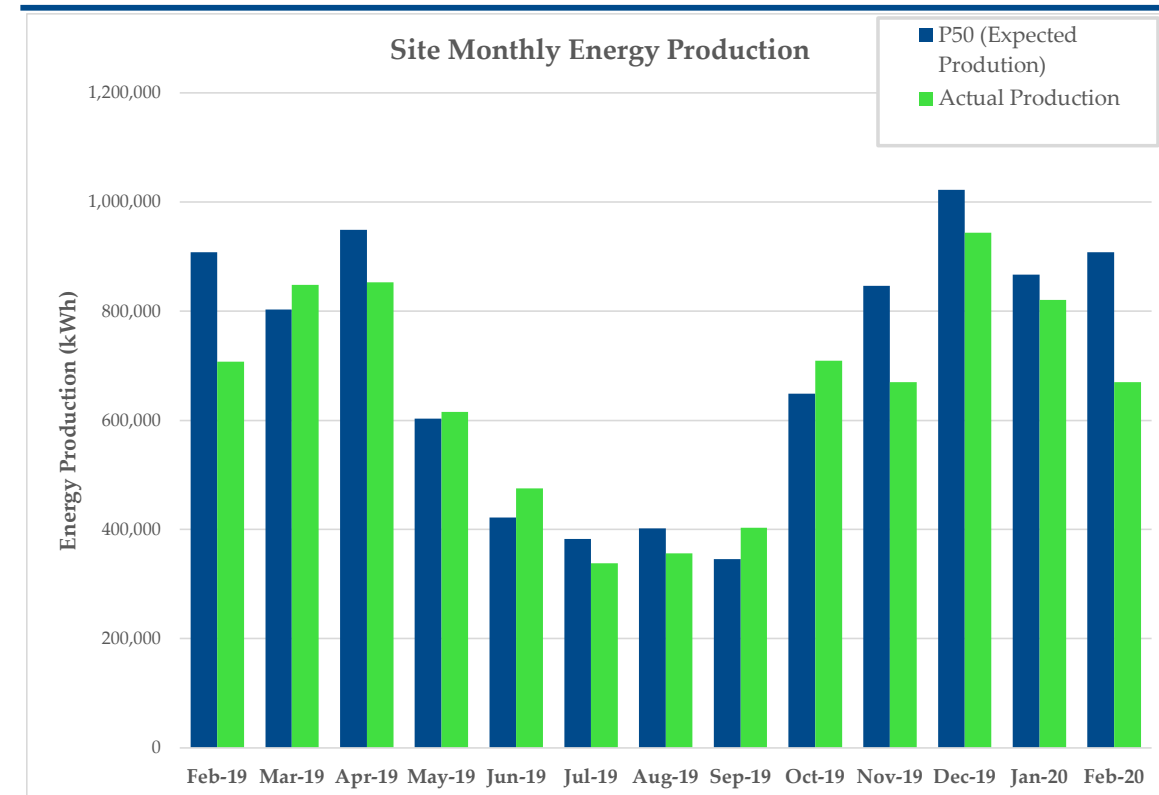

Monthly Report

February-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2020	Goldwind 4.5 Year Maintenance	~8	W1
May-2020	Goldwind 4.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/5-9/2020	Icing Event	Unplanned	92.49	W1
2/5-7/2020	Icing Event	Unplanned	38.12	W2
2/26-29/2020	Icing Event	Unplanned	46.01	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	100.00%
W2	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
W1	138.50	156.85
W2	38.12	46.50
Total	176.62	203.35

G. Billed Data

Meter Reading (Date/Time)	2/29/2020 12:00 AM
Meter To Date Produced	32,055,743 kWh
Meter To Date Consumed	64,280 kWh
Last Reading Produced	31,426,653 kWh
Last Reading Consumed	62,442 kWh
Billed kWh	627,252 kWh
Next Meter Reading	3/29/2020 12:00 AM

H. Report Notes and Comments
