


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Mar-19	422,000	450,944
Apr-19	499,000	450,366
May-19	318,000	335,596
Jun-19	222,000	276,978
Jul-19	201,000	166,408
Aug-19	211,000	188,300
Sep-19	182,000	205,853
Oct-19	341,000	395,663
Nov-19	445,000	329,892
Dec-19	537,000	480,035
Jan-20	455,000	427,899
Feb-20	478,000	353,172
Mar-20	422,000	413,290
Production 2020 (ytd) (kWh)	1,355,000	1,194,361
Total Production (kWh)*	4,311,000	4,023,452
Capacity Factor*	30.54%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

March-2020

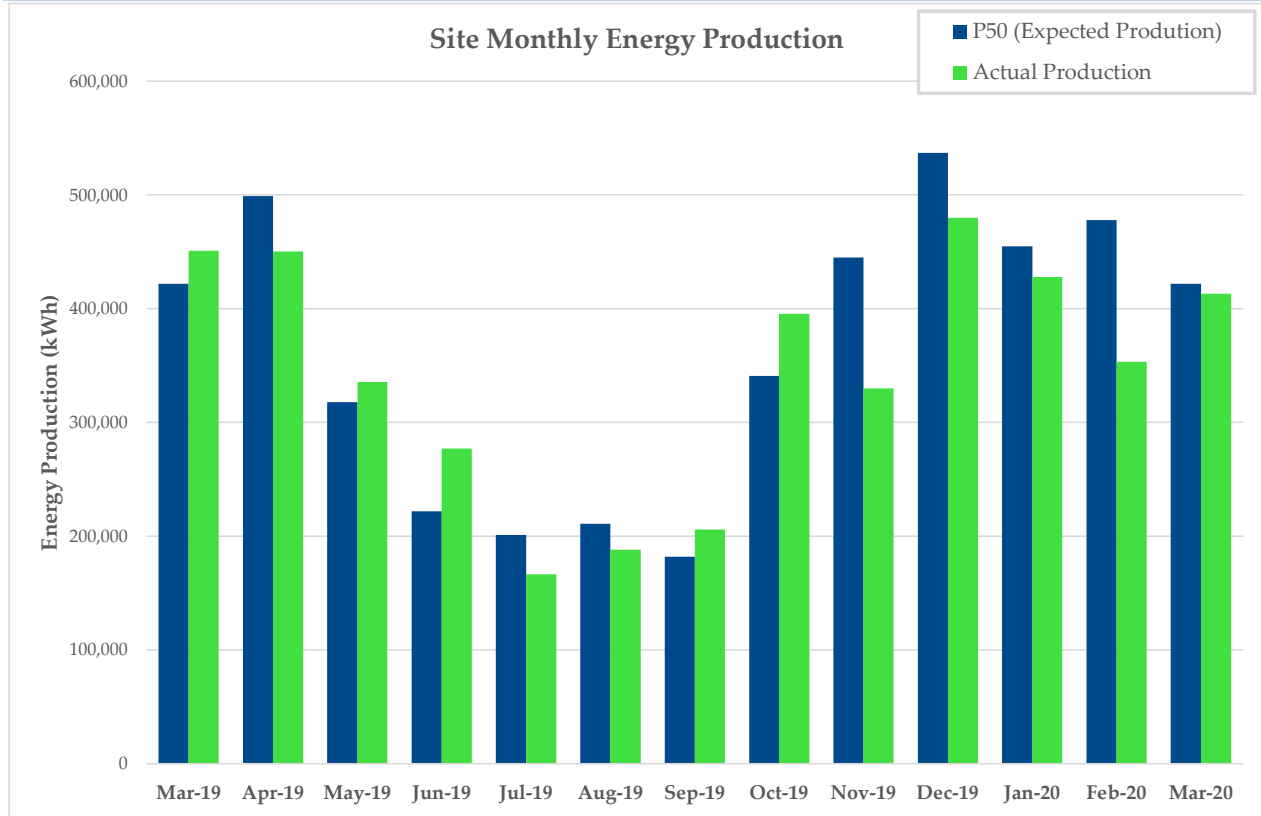

Monthly Report March-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
April-2020	Goldwind 2 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/5/2020	Goldwind 2 Year Maintenance	Planned	2.83	W1

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
W1	99.96%	99.99%
Downtime (hr)		
W1	8.19	95.84

G. Billed Data

Meter Reading (Date/Time)	4/1/2020 12:00 AM
Meter To Date Produced	8,501,442 kWh
Meter To Date Consumed	42,919 kWh
Last Reading Produced	8,093,799 kWh
Last Reading Consumed	41,445 kWh
Billed kWh	406,170 kWh
Next Meter Reading	5/1/2020 12:00 AM

H. Report Notes and Comments

*Goldwind 2 Year Maintenance to continue into April.

**Downtime pending further review.
