


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
May-19	927,000	753,487	261,344	247,282	244,861
Jun-19	634,000	653,072	224,916	205,888	222,268
Jul-19	527,000	357,677	119,328	116,242	122,107
Aug-19	449,000	423,670	145,657	134,069	143,944
Sep-19	610,000	414,660	141,275	131,797	141,588
Oct-19	990,000	916,038	308,623	294,939	312,476
Nov-19	1,123,000	846,849	291,098	273,259	282,492
Dec-19	1,153,000	1,139,609	398,017	365,419	376,173
Jan-20	1,306,000	1,063,984	370,096	346,270	347,618
Feb-20	1,137,000	767,713	286,395	246,834	234,484
Mar-20	1,134,000	1,101,462	378,775	354,544	368,143
Apr-20	1,176,000	1,028,204	354,270	335,252	338,682
May-20	927,000	863,616	293,660	275,555	294,401
Production 2020 (ytd) (kWh)	5,680,000	4,824,979	1,683,196	1,558,455	1,583,328
Total Production (kWh)*	11,166,000	9,576,554	3,312,110	3,080,068	3,184,376
Capacity Factor*	24.23%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

May-2020

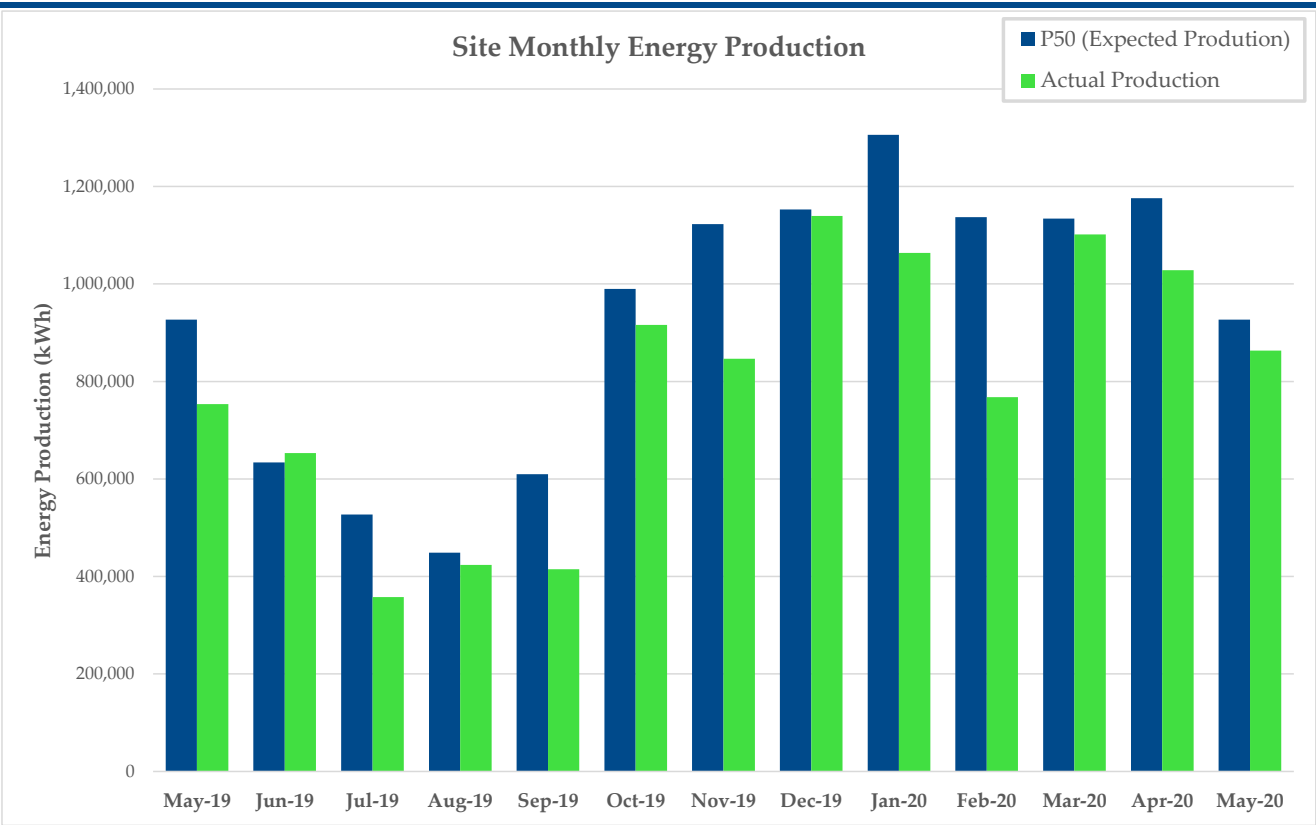

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events8

Date	Event	Duration (hr)	Turbine
October-2020	Goldwind 3 Year Maintenance	~15	W1
October-2020	Goldwind 3 Year Maintenance	~15	W2
October-2020	Goldwind 3 Year Maintenance	~15	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.95%
W2	100.00%	99.71%
W3	100.00%	99.99%
Avg	100.00%	99.88%

Downtime (hr)	This Month	Year To Date
W1	0.41	103.82
W2	0.41	144.33
W3	0.41	198.35
Total	1.23	446.50

G. Billed Data

Meter Reading (Date/Time)	5/21/2020 12:00 AM
Meter To Date Produced	24,269,146 kWh
Meter To Date Consumed	68,367 kWh
Last Reading Produced	23,174,690 kWh
Last Reading Consumed	67,105 kWh
Billed kWh	1,093,194 kWh
Next Meter Reading	6/21/2020 12:00 AM

H. Report Notes and Comments
