


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Jun-19	429,000	479,262	235,381	243,881
Jul-19	357,000	307,376	145,001	162,375
Aug-19	314,000	369,367	181,572	187,795
Sep-19	449,000	392,366	197,834	194,532
Oct-19	688,000	676,972	338,413	338,559
Nov-19	804,000	631,219	315,003	316,216
Dec-19	822,000	904,108	456,015	448,093
Jan-20	924,000	772,641	385,505	387,136
Feb-20	736,000	640,848	302,976	337,872
Mar-20	794,000	758,754	383,099	375,655
Apr-20	734,000	726,579	367,253	359,326
May-20	574,000	632,754	315,995	316,759
Jun-20	429,000	501,469	246,974	254,495
Production 2020 (ytd) (kWh)	4,191,000	4,033,045	2,001,802	2,031,243
Total Production (kWh)*	7,625,000	7,314,453	3,635,640	3,678,813
Capacity Factor*	27.76%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

June-2020

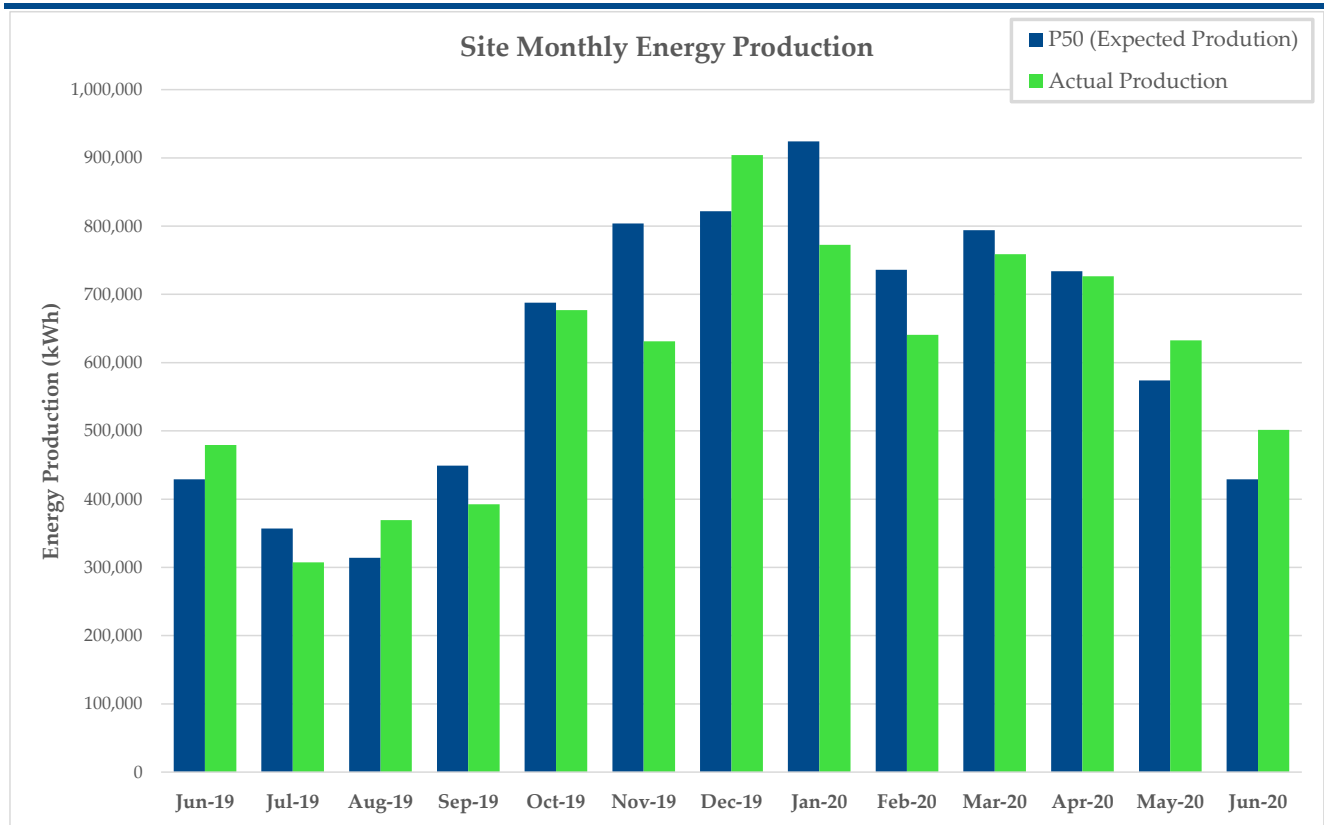

Monthly Report

June-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events*

Date	Event	Duration (hr)	Turbine
July-20	Goldwind 6 Month Maintenance	~8	V1
July-20	Goldwind 6 Month Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
6/15/2020	Owner/Operator Maintenance	Unplanned	6.94	V1

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	99.94%	99.99%
Avg	99.97%	99.99%

Downtime (hr)	This Month	Year To Date
V1	8.14	144.83
V2	1.63	150.62
Total	9.77	295.45

G. Billed Data

Meter Reading (Date/Time)	7/1/2020 12:00 AM
Meter To Date Produced	13,382,807 kWh
Meter To Date Consumed	32,183 kWh
Last Reading Produced	12,896,880 kWh
Last Reading Consumed	30,651 kWh
Billed kWh	484,395 kWh
Next Meter Reading	8/1/2020 12:00 AM

H. Report Notes and Comments

*Goldwind Maintenance moved to July.

**Goldwind Availability and Downtime under dispute.
