


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Aug-19	314,000	369,367	181,572	187,795
Sep-19	449,000	392,366	197,834	194,532
Oct-19	688,000	676,972	338,413	338,559
Nov-19	804,000	631,219	315,003	316,216
Dec-19	822,000	904,108	456,015	448,093
Jan-20	924,000	772,641	385,505	387,136
Feb-20	736,000	640,848	302,976	337,872
Mar-20	794,000	758,754	383,099	375,655
Apr-20	734,000	726,579	367,253	359,326
May-20	574,000	632,754	315,995	316,759
Jun-20	429,000	501,469	246,974	254,495
Jul-20	357,000	314,450	154,487	159,963
Aug-20	303,000	306,534	150,783	155,751
Production 2020 (ytd) (kWh)	4,851,000	4,654,029	2,307,072	2,346,957
Total Production (kWh)*	7,614,000	7,258,694	3,614,337	3,644,357
Capacity Factor*	27.55%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

August-2020

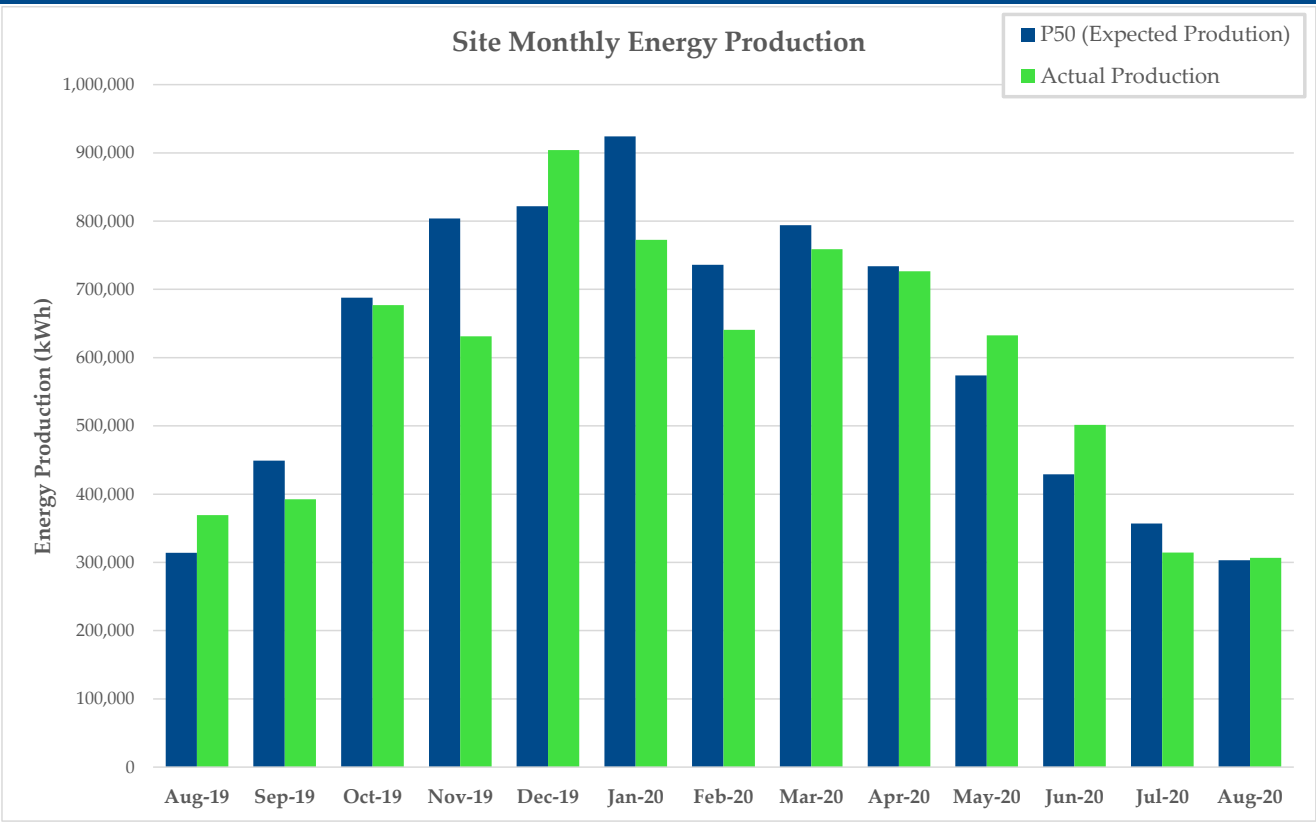

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
October-20	Goldwind 2 Year Maintenance	~15	V1
October-20	Goldwind 2 Year Maintenance	~15	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	99.80%	99.97%
Avg	99.90%	99.99%

Downtime (hr)	This Month	Year To Date
V1	3.55	207.58
V2	5.32	158.37
Total	8.87	365.95

G. Billed Data

Meter Reading (Date/Time)	9/1/2020 12:00 AM
Meter To Date Produced	13,983,850 kWh
Meter To Date Consumed	37,302 kWh
Last Reading Produced	13,687,373 kWh
Last Reading Consumed	34,724 kWh
Billed kWh	293,899 kWh
Next Meter Reading	10/1/2020 12:00 AM

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.

**Maintenance schedule updated due to settlement.
