


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Sep-19	346,000	403,384	203,853	199,531
Oct-19	649,000	709,389	354,865	354,524
Nov-19	846,000	669,872	338,584	331,288
Dec-19	1,022,000	943,766	481,616	462,150
Jan-20	867,000	820,679	407,059	413,620
Feb-20	908,000	670,274	317,389	352,885
Mar-20	803,000	795,295	400,369	394,926
Apr-20	949,000	706,174	357,900	348,274
May-20	603,000	633,162	322,304	310,858
Jun-20	422,000	512,907	257,351	255,556
Jul-20	383,000	317,320	159,723	157,597
Aug-20	399,000	300,935	157,115	143,820
Sep-20	337,000	489,578	244,573	245,005
Production 2020 (ytd) (kWh)	5,671,000	5,246,324	2,623,783	2,622,541
Total Production (kWh)*	8,188,000	7,569,351	3,798,848	3,770,503
Capacity Factor*	28.72%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

September-2020

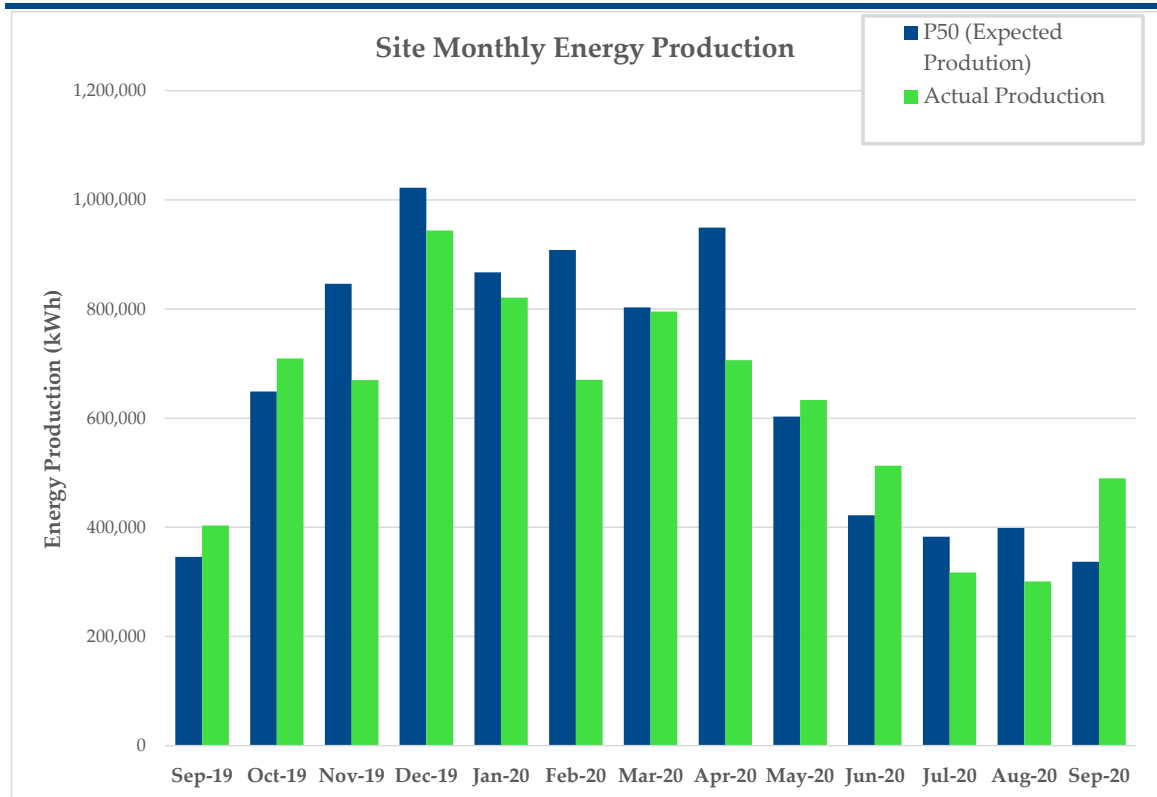

Monthly Report

September-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2020	Goldwind 5 Year Maintenance	~15	W1
October-2020	Goldwind 5 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.96%
W2	100.00%	99.39%
Avg	100.00%	99.67%

Downtime (hr)	This Month	Year To Date
W1	5.40	199.64
W2	3.90	124.80
Total	9.30	324.44

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.

G. Billed Data

Meter Reading (Date/Time)	9/29/2020 12:00 AM
Meter To Date Produced	35,737,546 kWh
Meter To Date Consumed	73,904 kWh
Last Reading Produced	35,273,711 kWh
Last Reading Consumed	72,803 kWh
Billed kWh	462,734 kWh
Next Meter Reading	10/29/2020 12:00 AM
