


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Oct-19	688,000	676,972	338,413	338,559
Nov-19	804,000	631,219	315,003	316,216
Dec-19	822,000	904,108	456,015	448,093
Jan-20	924,000	772,641	385,505	387,136
Feb-20	736,000	640,848	302,976	337,872
Mar-20	794,000	758,754	383,099	375,655
Apr-20	734,000	726,579	367,253	359,326
May-20	574,000	632,754	315,995	316,759
Jun-20	429,000	501,469	246,974	254,495
Jul-20	357,000	314,450	154,487	159,963
Aug-20	303,000	306,534	150,783	155,751
Sep-20	431,000	462,340	229,259	233,081
Oct-20	674,000	557,016	279,004	278,012
Production 2020 (ytd) (kWh)	5,956,000	5,673,385	2,815,335	2,858,050
Total Production (kWh)*	7,582,000	7,208,712	3,586,353	3,622,359
Capacity Factor*	27.36%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

October-2020

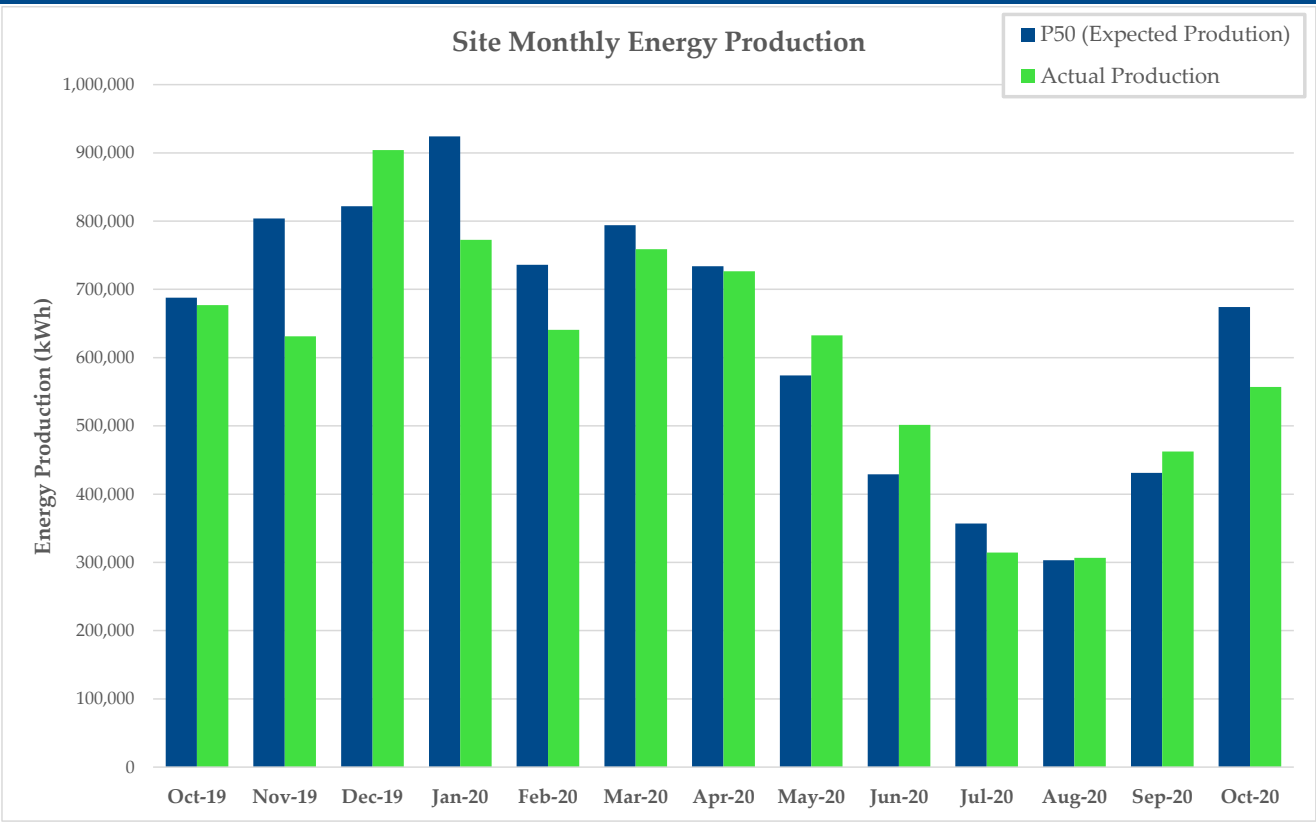

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
April-21	Goldwind 2.5 Year Maintenance	~8	V1
April-21	Goldwind 2.5 Year Maintenance	~8	V1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/27/2020	Goldwind 2 Year Maintenance	Planned	4.33	V1
10/27/2020	Goldwind 2 Year Maintenance	Planned	2.99	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	100.00%	99.96%
Avg	100.00%	99.98%

Downtime (hr)	This Month	Year To Date
V1	4.93	216.33
V2	3.59	166.36
Total	8.52	382.69

G. Billed Data

Meter Reading (Date/Time)	11/1/2020 12:00 AM
Meter To Date Produced	14,972,483 kWh
Meter To Date Consumed	40,198 kWh
Last Reading Produced	14,431,391 kWh
Last Reading Consumed	38,687 kWh
Billed kWh	539,581 kWh
Next Meter Reading	12/1/2020 12:00 AM

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.
