


A. Site Energy Production Summary*

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	L1	L2	L3
Aug-20	534,000	251,447	74,850	95,169	81,428
Sep-20	736,000	700,759	241,924	248,089	210,746
Oct-20	1,131,000	977,504	330,212	329,167	318,125
Nov-20	1,281,000				
Dec-20	1,263,000				
Jan-21	1,433,000				
Feb-21	1,213,000				
Mar-21	1,339,000				
Apr-21	1,327,000				
May-21	1,052,000				
Jun-21	751,000				
Jul-21	609,000				
Aug-21	534,000				
Production 2020 (ytd) (kWh)	2,401,000	1,929,710	646,986	672,425	610,299
Total Production (kWh)*	-	-	-	-	-
Capacity Factor*	- *Value calculated over the last 12 months				

B. Site Energy Production Graph

October-2020

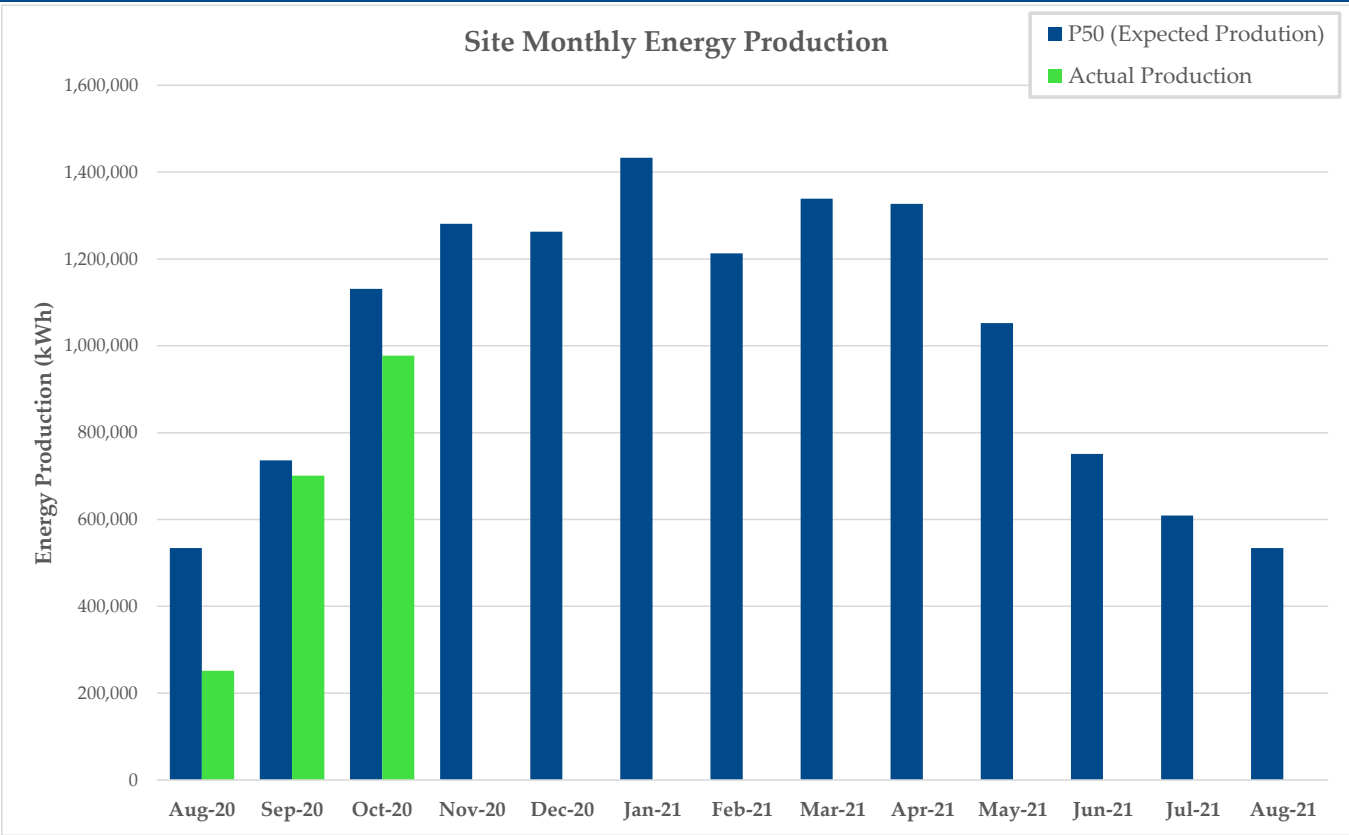

Monthly Report

October-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
February-2021	Goldwind 6 Month Maintenance	~8	L1
February-2021	Goldwind 6 Month Maintenance	~8	L2
February-2021	Goldwind 6 Month Maintenance	~8	L3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/7-8/2020	Converter Fault	Unplanned	18.05	L3

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
L1	100.00%	99.16%
L2	99.65%	99.33%
L3	97.57%	96.17%
Avg	99.07%	98.22%

Downtime (hr)	This Month	Year To Date
L1	1.55	23.38
L2	7.11	20.76
L3	19.35	63.48
Total	28.01	107.62

G. Billed Data

Meter Reading (Date/Time)	10/23/2020 12:00 AM
Meter To Date Produced	1,690,305 kWh
Meter To Date Consumed	9,497 kWh
Last Reading Produced	715,125 kWh
Last Reading Consumed	7,288 kWh
Billed kWh	972,971 kWh
Next Meter Reading	11/21/2020 12:00 AM

H. Report Notes and Comments

*Capacity factor to be included once full year of data is available.

**After review, reported September Downtime was accurate.
