


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Nov-19	804,000	631,219	315,003	316,216
Dec-19	822,000	904,108	456,015	448,093
Jan-20	924,000	772,641	385,505	387,136
Feb-20	736,000	640,848	302,976	337,872
Mar-20	794,000	758,754	383,099	375,655
Apr-20	734,000	726,579	367,253	359,326
May-20	574,000	632,754	315,995	316,759
Jun-20	429,000	501,469	246,974	254,495
Jul-20	357,000	314,450	154,487	159,963
Aug-20	303,000	306,534	150,783	155,751
Sep-20	431,000	462,340	229,259	233,081
Oct-20	674,000	557,016	279,004	278,012
Nov-20	796,000	913,861	455,668	458,193
Production 2020 (ytd) (kWh)	6,752,000	6,587,246	3,271,003	3,316,243
Total Production (kWh)*	7,574,000	7,491,354	3,727,018	3,764,336
Capacity Factor*	28.43%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

November-2020

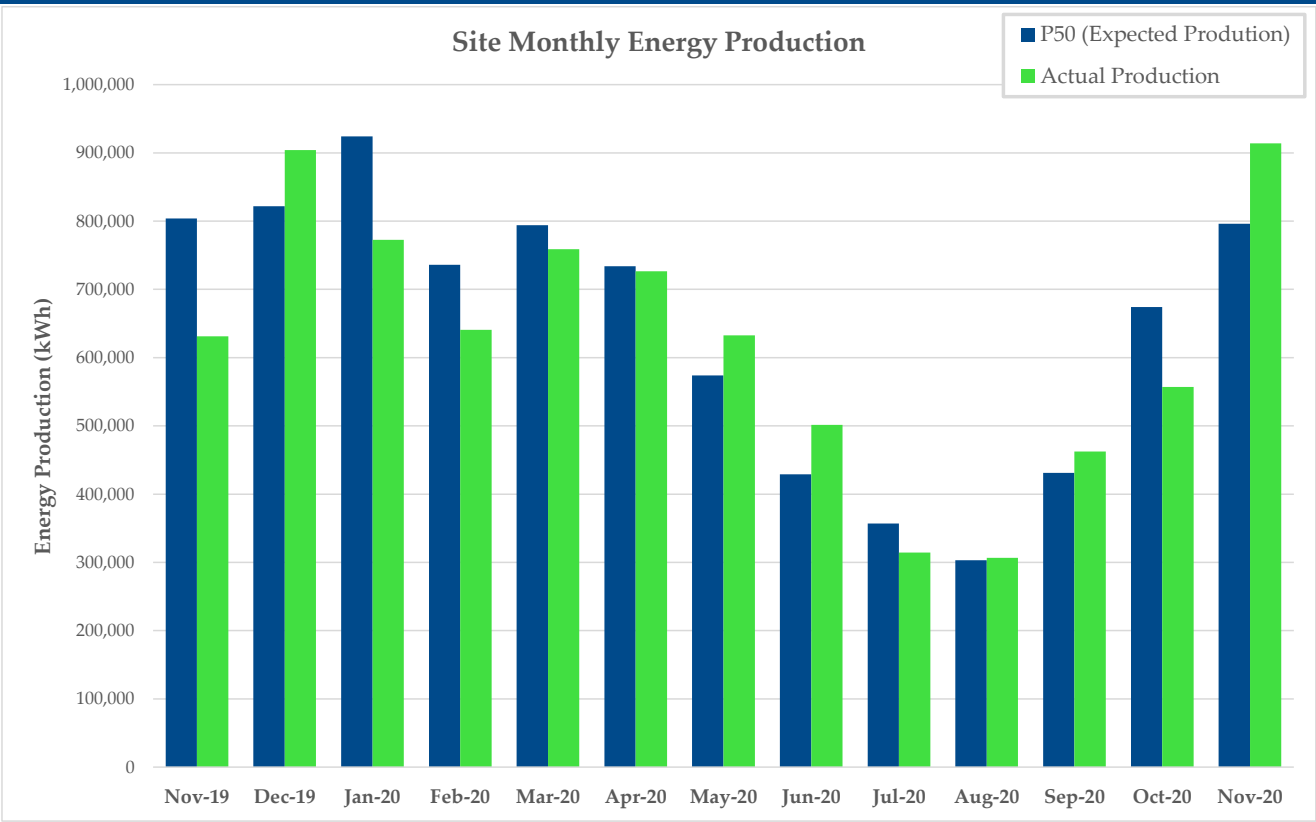

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events**

Date	Event	Duration (hr)	Turbine
April-21	Goldwind 2.5 Year Maintenance	~8	V1
April-21	Goldwind 2.5 Year Maintenance	~8	V1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/15/2020	Weather Shutdown	Unplanned	8.24	V1
11/15/2020	Weather Shutdown	Unplanned	8.24	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	100.00%	99.97%
Avg	100.00%	99.98%

Downtime (hr)	This Month	Year To Date
V1	10.47	226.80
V2	10.47	176.83
Total	20.94	403.63

G. Billed Data

Meter Reading (Date/Time)	12/1/2020 12:00 AM
Meter To Date Produced	15,861,956 kWh
Meter To Date Consumed	40,814 kWh
Last Reading Produced	14,972,483 kWh
Last Reading Consumed	40,198 kWh
Billed kWh	888,857 kWh
Next Meter Reading	1/1/2021 12:00 AM

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.
