


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Nov-19	846,000	669,872	338,584	331,288
Dec-19	1,022,000	943,766	481,616	462,150
Jan-20	867,000	820,679	407,059	413,620
Feb-20	908,000	670,274	317,389	352,885
Mar-20	803,000	795,295	400,369	394,926
Apr-20	949,000	706,174	357,900	348,274
May-20	603,000	633,162	322,304	310,858
Jun-20	422,000	512,907	257,351	255,556
Jul-20	383,000	317,320	159,723	157,597
Aug-20	399,000	300,935	157,115	143,820
Sep-20	337,000	489,578	244,573	245,005
Oct-20	637,000	603,877	306,458	297,419
Nov-20	834,000	945,207	479,511	465,696
Production 2020 (ytd) (kWh)	7,142,000	6,795,408	3,409,752	3,385,656
Total Production (kWh)*	8,164,000	7,739,174	3,891,368	3,847,806
Capacity Factor*	29.37%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

November-2020

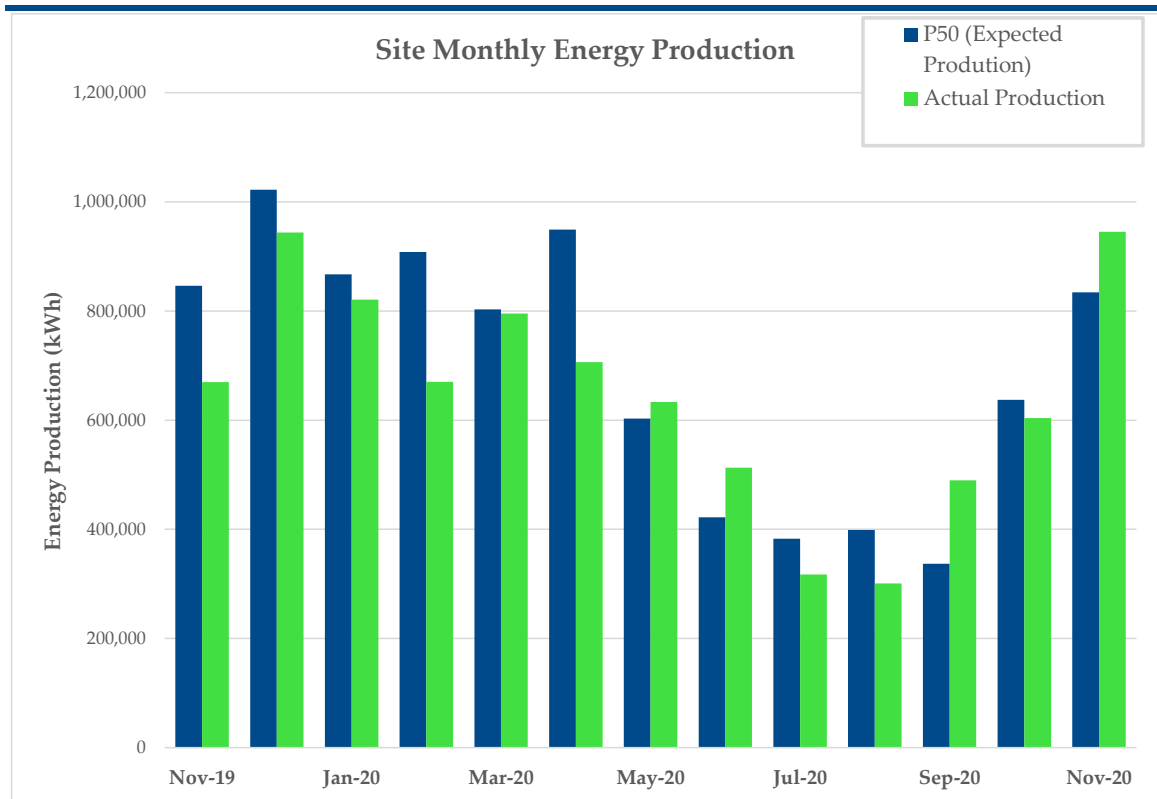

Monthly Report November-2020

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2021	Goldwind 5.5 Year Maintenance	~8	W1
April-2021	Goldwind 5.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/1/2020	Grid Fault	Unplanned	5.03	W1
11/1/2020	Grid Fault	Unplanned	4.02	W2
11/15/2020	Weather Stop	Unplanned	8.22	W1
11/15/2020	Weather Stop	Unplanned	8.22	W2

Availability	This Month	Year To Date	Meter Reading (Date/Time)	11/29/2020 12:00 AM
W1	100.00%	99.97%	Meter To Date Produced	37,278,158 kWh
W2	100.00%	99.50%	Meter To Date Consumed	75,495 kWh
Avg	100.00%	99.73%	Last Reading Produced	36,353,397 kWh
			Last Reading Consumed	75,029 kWh
			Billed kWh	924,295 kWh
			Next Meter Reading	12/29/2020 12:00 AM

Downtime (hr)	This Month	Year To Date
W1	17.55	222.12
W2	15.06	146.81
Total	32.61	368.93

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.
