


A. Site Energy Production Summary*

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jan-20	867,000	820,679	407,059	413,620
Feb-20	908,000	670,274	317,389	352,885
Mar-20	803,000	795,295	400,369	394,926
Apr-20	949,000	706,174	357,900	348,274
May-20	603,000	633,162	322,304	310,858
Jun-20	422,000	512,907	257,351	255,556
Jul-20	383,000	317,320	159,723	157,597
Aug-20	399,000	300,935	157,115	143,820
Sep-20	337,000	489,578	244,573	245,005
Oct-20	637,000	603,877	306,458	297,419
Nov-20	834,000	945,207	479,511	465,696
Dec-20	1,015,000	887,367	445,540	441,827
Jan-21	875,000	568,442	288,651	279,791
Production 2021 (ytd) (kWh)	875,000	568,442	288,651	279,791
Total Production (kWh)*	8,165,000	7,430,538	3,736,884	3,693,654
Capacity Factor*	28.20%		*Value calculated over the last 12 months	

B. Site Energy Production Graph

January-2021

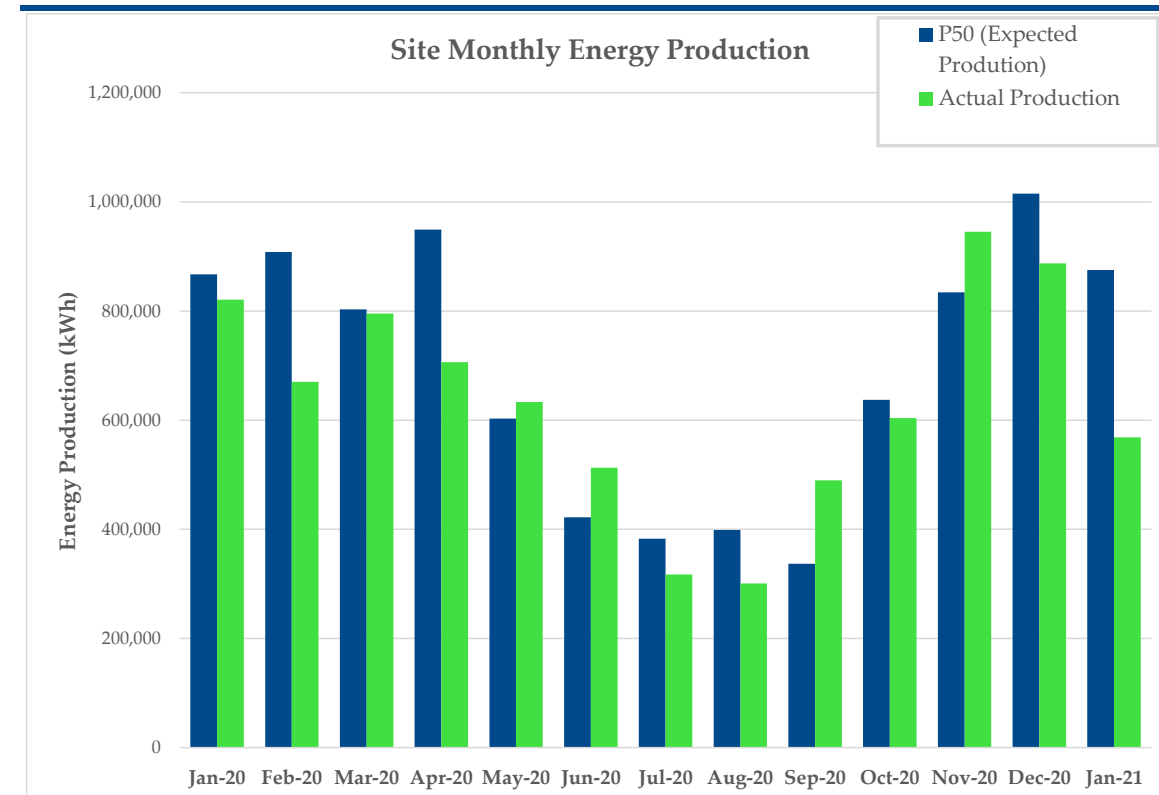

Monthly Report

January-2021

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2021	Goldwind 5.5 Year Maintenance	~8	W1
April-2021	Goldwind 5.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/1/-1/2/2021	Icing Event	Unplanned	19.33	W1
1/1/-1/2/2021	Icing Event	Unplanned	19.25	W2
1/26/2021	Icing Event	Unplanned	11.27	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	100.00%
W2	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
W1	35.55	35.55
W2	22.80	22.80
Total	58.35	58.35

G. Billed Data

Meter Reading (Date/Time)	01/29/2021 12:00 AM
Meter To Date Produced	38,691,919 kWh
Meter To Date Consumed	78,039 kWh
Last Reading Produced	38,129,308 kWh
Last Reading Consumed	76,369 kWh
Billed kWh	560,941 kWh
Next Meter Reading	3/1/2021 12:00 AM

H. Report Notes and Comments

*Change in production estimate due to Material Change of Circumstance.
