



BALL CORPORATION - ZEPHYR WIND PROJECT 2.0


North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary*

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Aug-20	448,000	412,465	141,347	122,472	148,646
Sep-20	617,000	710,596	228,314	239,356	242,926
Oct-20	956,000	850,601	284,918	272,587	293,096
Nov-20	1,107,000	1,330,282	442,746	426,184	461,352
Dec-20	1,098,000	1,263,339	421,761	411,065	430,513
Jan-21	1,251,000	798,530	263,091	267,336	268,103
Feb-21	1,044,000	1,137,529	368,454	371,784	397,291
Mar-21	1,119,000	1,351,254	441,435	433,777	476,042
Apr-21	1,116,000				
May-21	876,000				
Jun-21	637,000				
Jul-21	518,000				
Aug-21	448,000				
Production 2021 (ytd) (kWh)	3,414,000	3,287,313	1,072,980	1,072,897	1,141,436
Total Production (kWh)*	-	-	-	-	-
Capacity Factor*	- *Value calculated over the last 12 months				

B. Site Energy Production Graph

March-2021

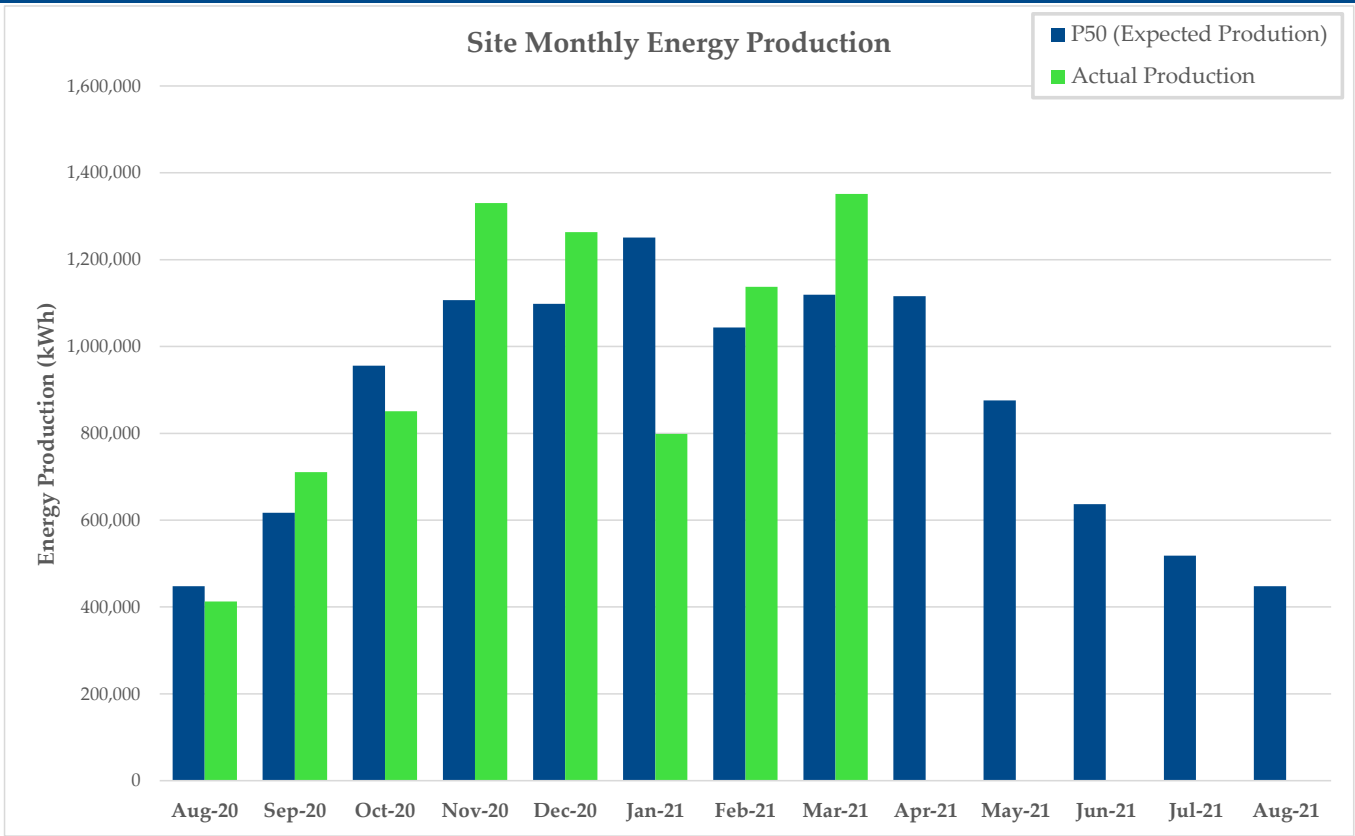

Monthly Report March-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
August-2021	Goldwind 1 Year Maintenance	~15	Z4
August-2021	Goldwind 1 Year Maintenance	~15	Z5
August-2021	Goldwind 1 Year Maintenance	~15	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/2/2021	Goldwind 6 Month Maintenance	Planned	2.56	Z6
3/16/2021	Fault Troubleshooting	Unplanned	4.70	Z4
3/16/2021	Fault Troubleshooting	Unplanned	4.39	Z5
3/16/2021	Fault Troubleshooting	Unplanned	4.22	Z6
3/16/2021	Grid Event	Unplanned	6.37	Z4
3/16/2021	Grid Event	Unplanned	6.37	Z5
3/16/2021	Grid Event	Unplanned	6.37	Z6
3/25-26/2021	Weather Shutdown	Unplanned	7.42	Z4
3/25-26/2021	Weather Shutdown	Unplanned	7.42	Z5
3/25-26/2021	Weather Shutdown	Unplanned	7.42	Z6
3/31/2021	Owner/Operator Maintenance	Unplanned	4.04	Z4

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
Z4	99.13%	99.71%
Z5	99.30%	99.77%
Z6	99.20%	99.58%
Avg	99.21%	99.69%

Downtime (hr)	This Month	Year To Date
Z4	28.12	74.51
Z5	22.83	51.78
Z6	26.36	67.07
Total	77.31	193.36

G. Billed Data

Meter Reading (Date/Time)	3/19/2021 12:00 AM
Ball 2.0 Production (This Period)	1,279,269 kWh
Ball 2.0 Consumption (This Period)	996 kWh
Billed kWh	1,278,273 kWh
Next Meter Reading	4/20/2021 12:00 AM

H. Report Notes and Comments

*Capacity factor to be included once full year of data is available.

**Downtime and availability under further review.
