



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0

North Findlay Wind Campus, Findlay, OH

Monthly Report

March-2021




A. Site Energy Production Summary*

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Mar-20	1,197,000	1,162,213	396,502	388,972	376,739
Apr-20	1,415,000	1,077,278	363,770	357,740	355,768
May-20	900,000	924,506	311,078	306,313	307,115
Jun-20	628,000	745,225	255,090	244,089	246,046
Jul-20	571,000	463,808	161,712	150,497	151,599
Aug-20	559,000	415,856	150,588	137,019	128,249
Sep-20	482,000	686,455	244,046	228,724	213,685
Oct-20	916,000	853,114	301,587	287,867	263,660
Nov-20	1,203,000	1,333,905	455,233	450,343	428,329
Dec-20	1,475,000	1,298,566	447,593	437,476	413,497
Jan-21	1,260,000	763,428	269,281	243,111	251,036
Feb-21	1,310,000	1,112,551	384,385	376,283	351,883
Mar-21	1,140,000	1,328,761	439,843	458,260	430,658
Production 2021 (ytd) (kWh)	3,710,000	3,204,740	1,093,509	1,077,654	1,033,577
Total Production (kWh)*	11,859,000	11,003,453	3,784,206	3,677,722	3,541,525
Capacity Factor*	27.91% *Value calculated over the last 12 months				

B. Site Energy Production Graph

March-2021

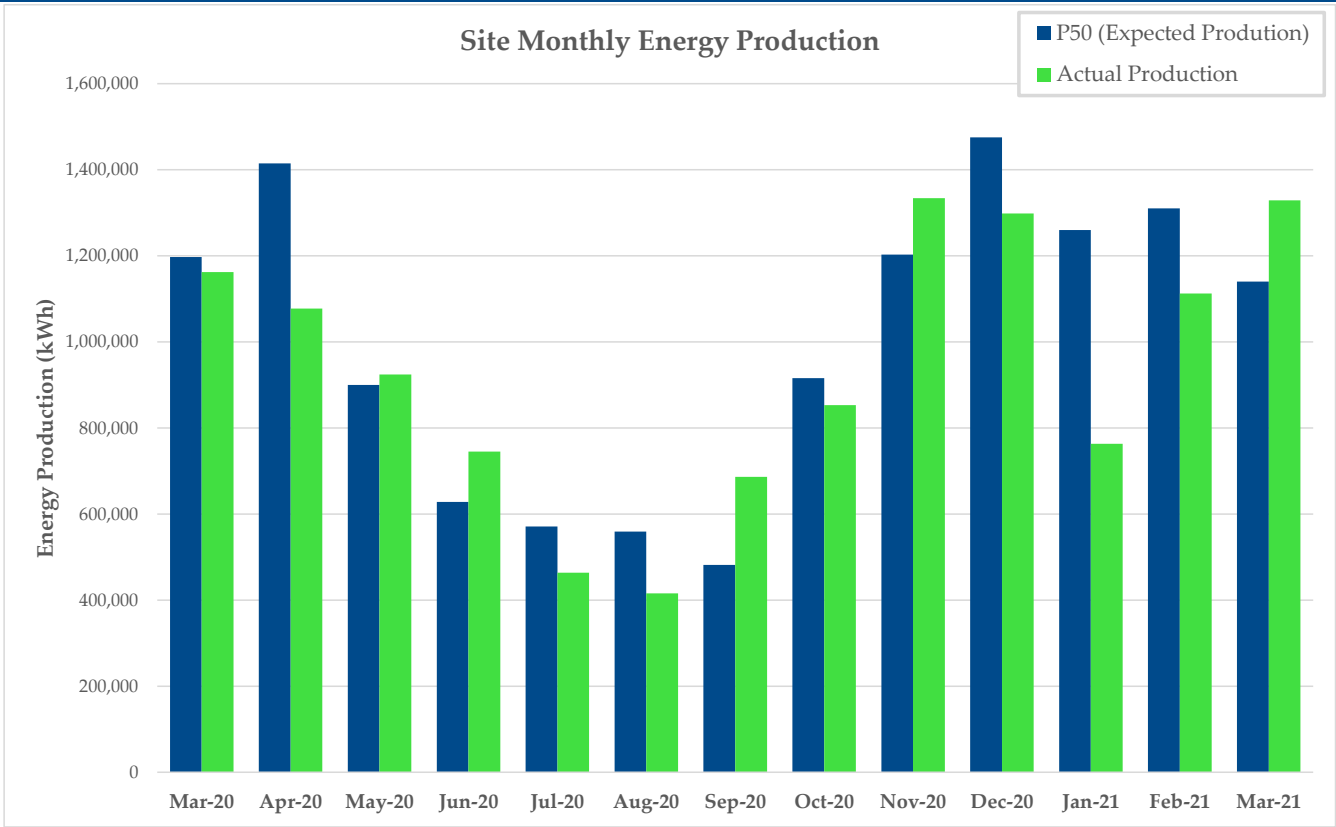

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2021	Goldwind 5 Year Maintenance	~15	Z1
April-2021	Goldwind 5 Year Maintenance	~15	Z2
April-2021	Goldwind 5 Year Maintenance	~15	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/14-16/2021	Fault	Unplanned	55.12	Z1
3/16/2021	Fault Troubleshooting	Unplanned	4.21	Z2, Z3
3/16/2021	Grid Event	Unplanned	6.60	Z2
3/16/2021	Grid Event	Unplanned	6.06	Z3
3/25-26/2021	Weather Shutdown	Unplanned	7.41	Z1
3/25-26/2021	Weather Shutdown	Unplanned	7.41	Z2
3/25-26/2021	Weather Shutdown	Unplanned	7.41	Z3
3/27/2021	Fault	Unplanned	5.01	Z1

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
Z1	91.92%	97.27%
Z2	99.19%	98.49%
Z3	99.20%	99.73%
Avg	96.77%	98.50%

Downtime (hr)	This Month	Year To Date
Z1	70.09	94.10
Z2	23.64	75.31
Z3	23.11	60.84
Total	116.84	230.25

G. Billed Data

Meter Reading (Date/Time)	3/19/2021 12:00 AM
Ball 1.0 Production (This Period)	1,336,127 kWh
Ball 1.0 Consumption (This Period)	407 kWh
Billed kWh	1,335,720 kWh
Next Meter Reading	4/20/2021 12:00 AM

H. Report Notes and Comments

*Change in production estimate due to Material Change in Circumstance.

**Downtime and availability under further review.
