



HARPSTER WIND PROJECT

Harpster, OH


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Apr-20	399,000	351,248
May-20	311,000	301,340
Jun-20	228,000	211,118
Jul-20	179,000	127,434
Aug-20	157,000	119,753
Sep-20	224,000	194,360
Oct-20	338,000	240,522
Nov-20	402,000	356,013
Dec-20	403,000	399,725
Jan-21	460,000	252,077
Feb-21	372,000	359,816
Mar-21	417,000	441,144
Apr-21	399,000	331,073
Production 2021 (ytd) (kWh)	1,648,000	1,384,110
Total Production (kWh)*	3,890,000	3,334,375
Capacity Factor*	25.38%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

April-2021

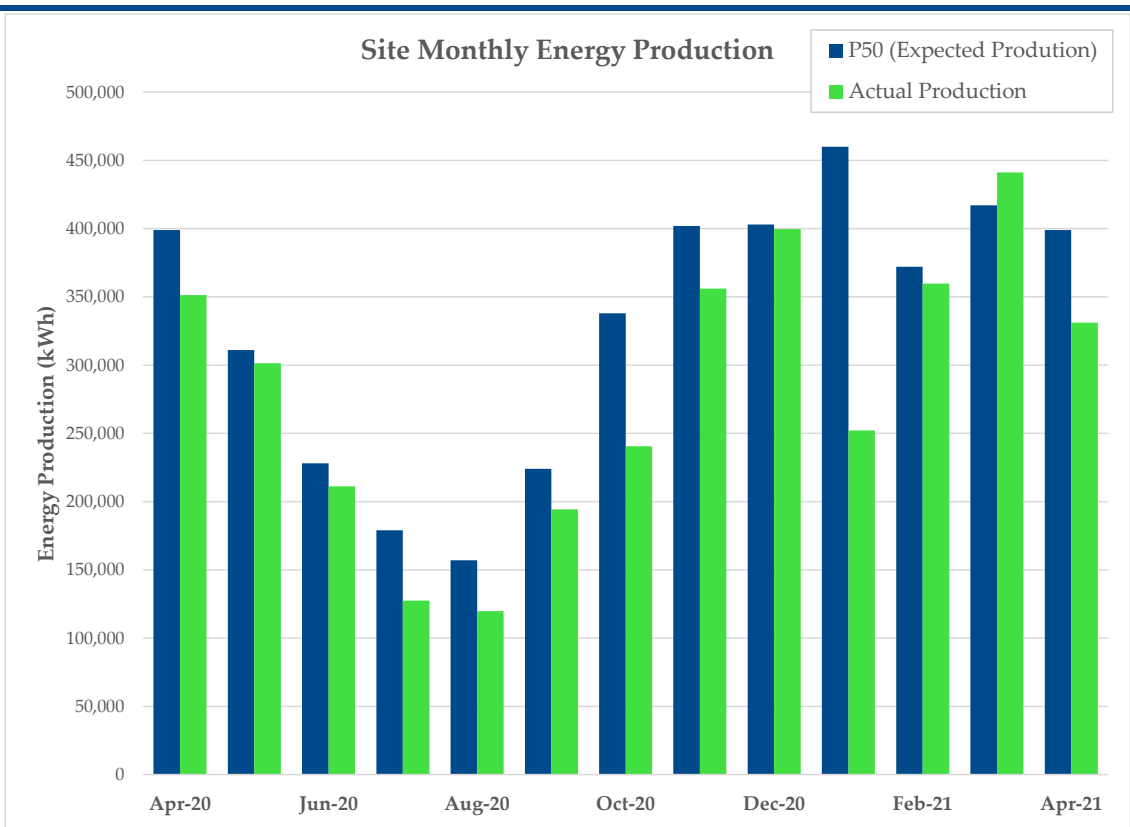

Monthly Report

April-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2021	Goldwind 5.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/2/2021	Owner/Operator Maintenance	Unplanned	2.06	H1
4/13/2021	Goldwind 5 Year Maintenance	Planned	3.45	H1
4/21/2021	Owner/Operator Maintenance	Unplanned	1.66	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	100.00%	99.97%
Downtime (hr)	This Month	Year To Date
H1	7.74	38.82

G. Billed Data

Meter Reading (Date/Time)	4/27/2021 12:00 AM
Meter To Date Produced	17,355,932 kWh
Meter To Date Consumed	57,624 kWh
Last Reading Produced	16,990,941 kWh
Last Reading Consumed	57,062 kWh
Billed kWh	364,429 kWh
Next Meter Reading	5/26/2021 12:00 AM

H. Report Notes and Comments
